

License

This slide deck is provided with an open CC-BY license, which means that you can use it (share and adapt it for commercial and non-commercial purposes) without asking for permission and only by mentioning the original source.

More information:

<https://creativecommons.org/licenses/by/4.0/>

Some of the content in this slide deck (the Integrated Project Board, the Follow-Up Register, etc.) are borrowed from OMIMO, which are available with an open CC-BY license and you can reuse them by mentioning their source: <https://omimo.org>

EXPECTED MONETARY VALUE KICKOFF MEETING EARNED VALUE ANALYSIS DISCRETIONARY DEPENDENCY
VERIFICATION UNCERTAINTY RISK REGISTER DECISION TREE DEVELOPMENT APPROACH GOVERNANCE
ARTIFACT TOLERANCE ANALOGOUS ESTIMATING ESTIMATE AT COMPLETION CONTRACT COST OF QUALITY
DECOMPOSITION ACCEPTANCE CRITERIA ITERATION CONST BENEFIT ANALYSIS AMBIGUITY BASELINE
BENCHMARK DECLUTTER BUDGET AT COMPLETION PRODUCT SCOPE UNCERTAINTY CRITICAL PATH
DELIVERABLE VALUE ENGINEERING CUMULATIVE FLOW DIAGRAM DASHBOARD SPONSOR CONTRACT
ROLLING WAVE PLANNING YOUR RELEASE PLANNING REQUIREMENTS BUSINESS CASE CYCLE TIME
THRESHOLD PREDICTIVE BIDDER CONFERENCE PROJECT MANAGEMENT CHANGE REQUEST CONSTRAINT
COMPLEXITY ROOT CAUSE ANALYSIS WORK PACKAGE TAILORING STATEMENT OF WORK CHARTER
BACKLOG MANAGEMENT RESERVE LEAD TIME HISTOGRAM SYSTEM CONFORMANCE ACCURACY
FRAMEWORK LAG TIME TACIT KNOWLEDGE STORY POINTS STAKEHOLDER ENGAGEMENT CHANGE CONTROL
PERFORMANCE MEASUREMENT REGRESSION ANALYSIS PROBABILITY AND IMPACT MATRIX ISSUE LOG
ACTUAL COST BURN CHART CONTINGENCY RESERVE MODELING LESSONS LEARNED NETWORK DIAGRAM
FORECAST METHODOLOGY PHASE GATE PRIORITIZATION MATRIX ORGANIZATIONAL BREAKDOWN STRUCTURE
QUALITY LIFE CYCLE WORK BREAKDOWN STRUCTURE TREND ANALYSIS PROGRESSIVE ELABORATION AGILE

Nader K. Rad



Nader K. Rad

minimalist project management architect

Core team member @ OMIMO
Training specialist @ Management Plaza



Civil Engineering (BS)

Philosophy of Science (MS)

Nader K. Rad

minimalist project management architect

Core team member @ OMIMO
Training specialist @ Management Plaza


28
Years of
working with
projects

Nader K. Rad

minimalist project management architect

Core team member @ OMIMO
Training specialist @ Management Plaza



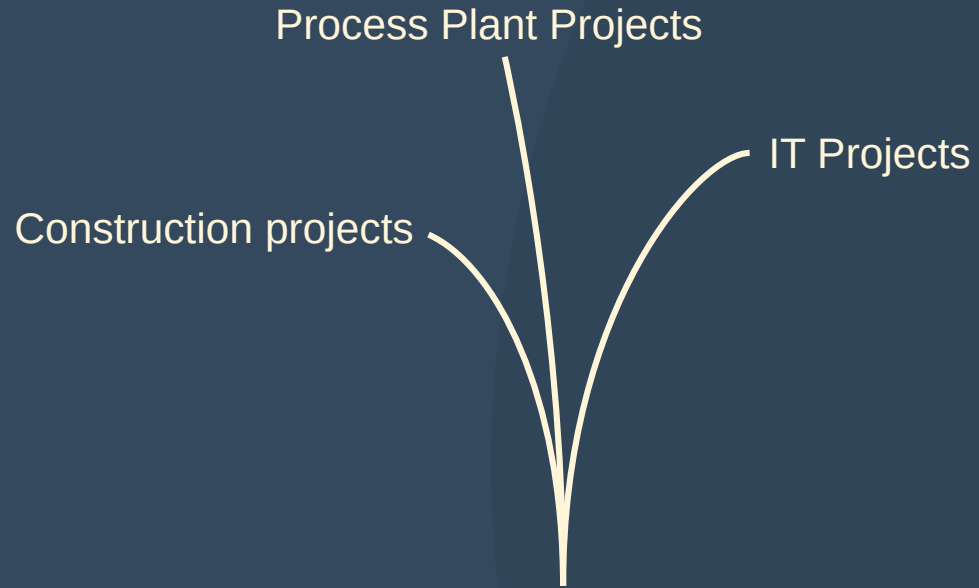

minimalist project management architect

Core team member @ OMIMO
Training specialist @ Management Plaza



Nader K. Rad

minimalist project management architect

Core team member @ OMIMO
Training specialist @ Management Plaza




Nader K. Rad

minimalist project management architect

Core team member @ OMIMO
Training specialist @ Management Plaza

Contributing to standards
Writing books and articles
Making eLearning courses
Giving presentations



Nader K. Rad

minimalist project management architect


Core team member @ OMIMO
Training specialist @ Management Plaza


CORE TEAM

P3.express
NUPP
PMBOK Guide v7
micro.P3.express
P5.express
P1.express
LB Compass

CONSULTANT

PRINCE2 Agile v1
PRINCE2 v6
MSP v4
PRINCE2 Agile v2

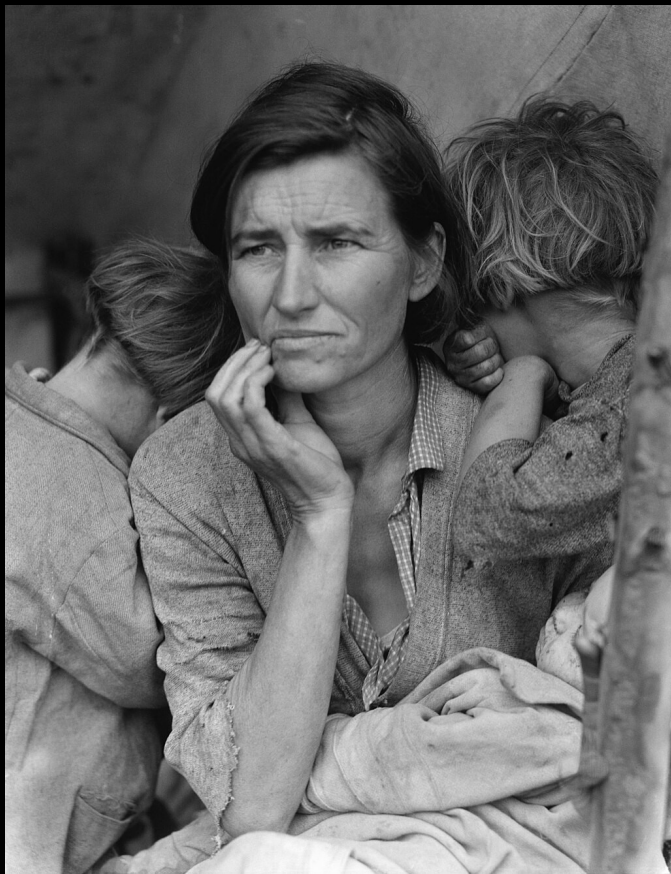

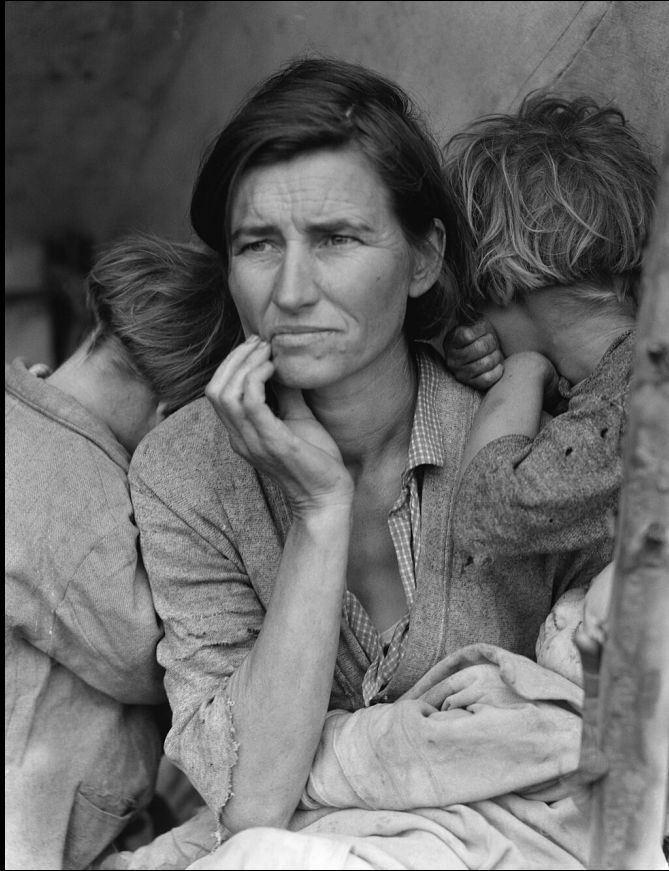

Migrant Mother, 1936




Dorothea Lange (1895-1965)





The Tetons and the Snake River, 1942

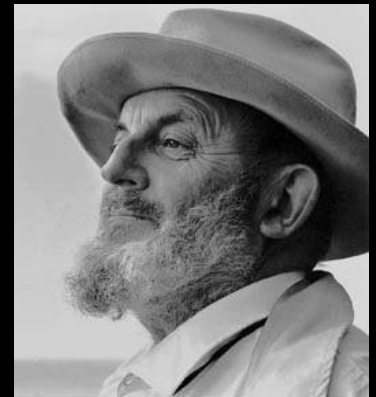


Ansel Adams (1902-1984)



Hobbyist



Great artist

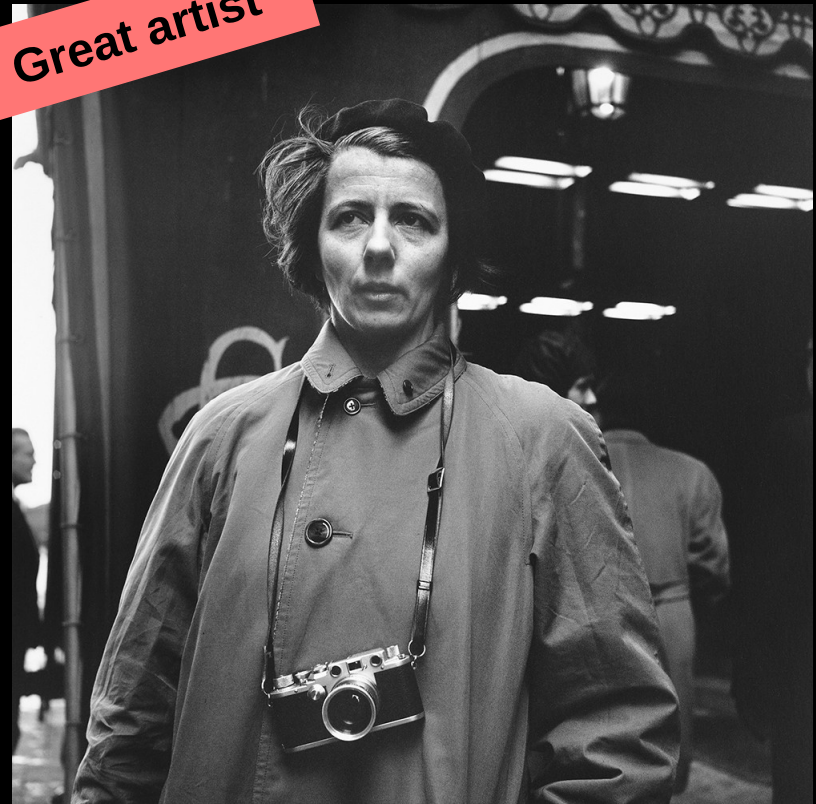

Vivian Maier (1926-2009)

features


MORE IS BETTER




Wegner 16999
2006 (?)
141 functions

MORE IS BETTER (?)


usefulness

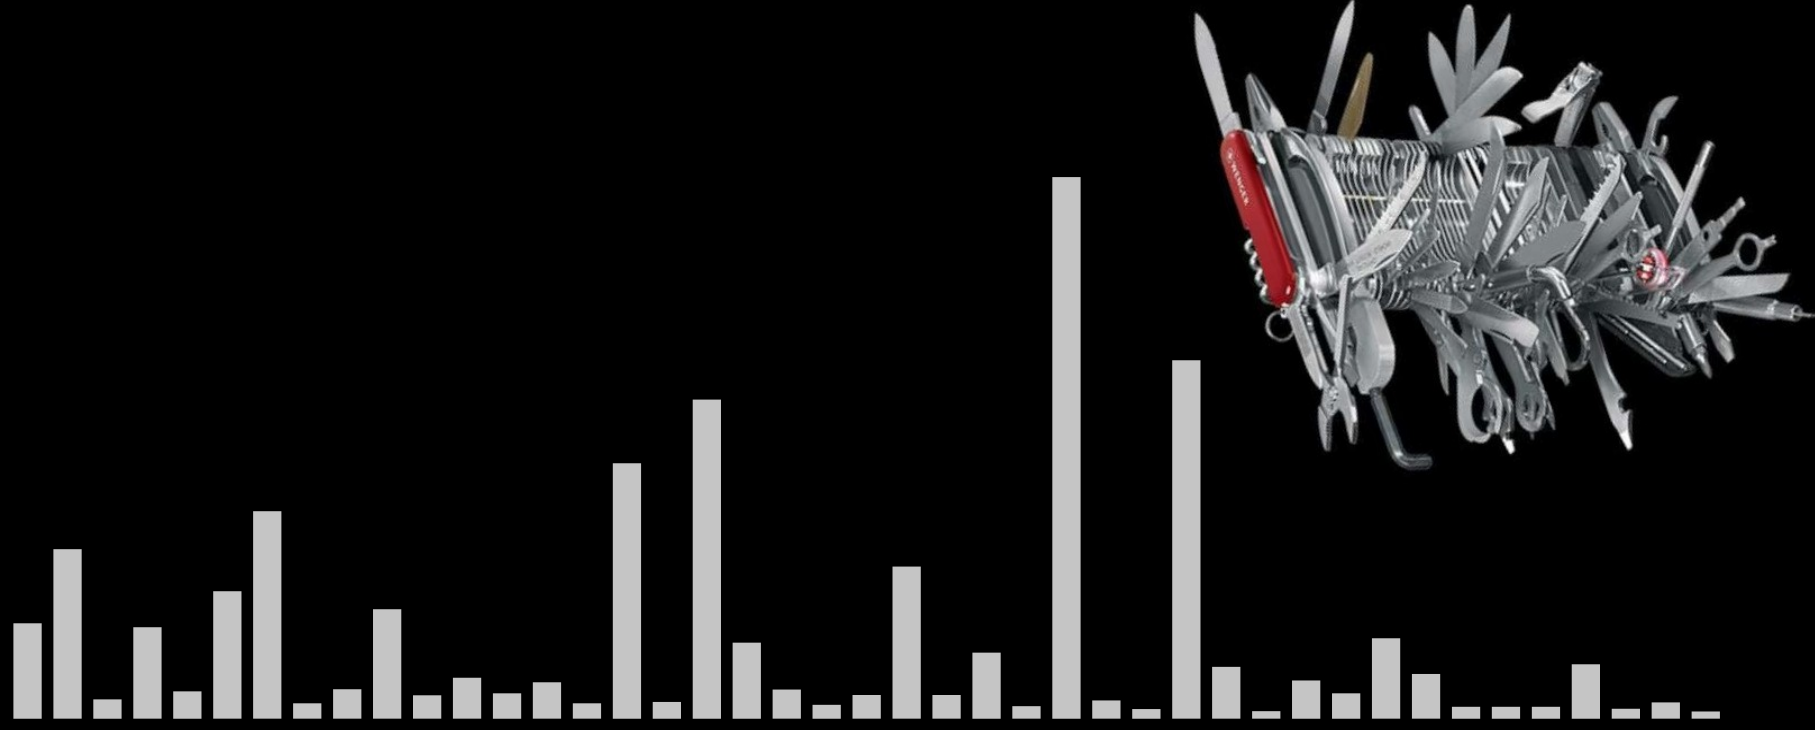


usefulness

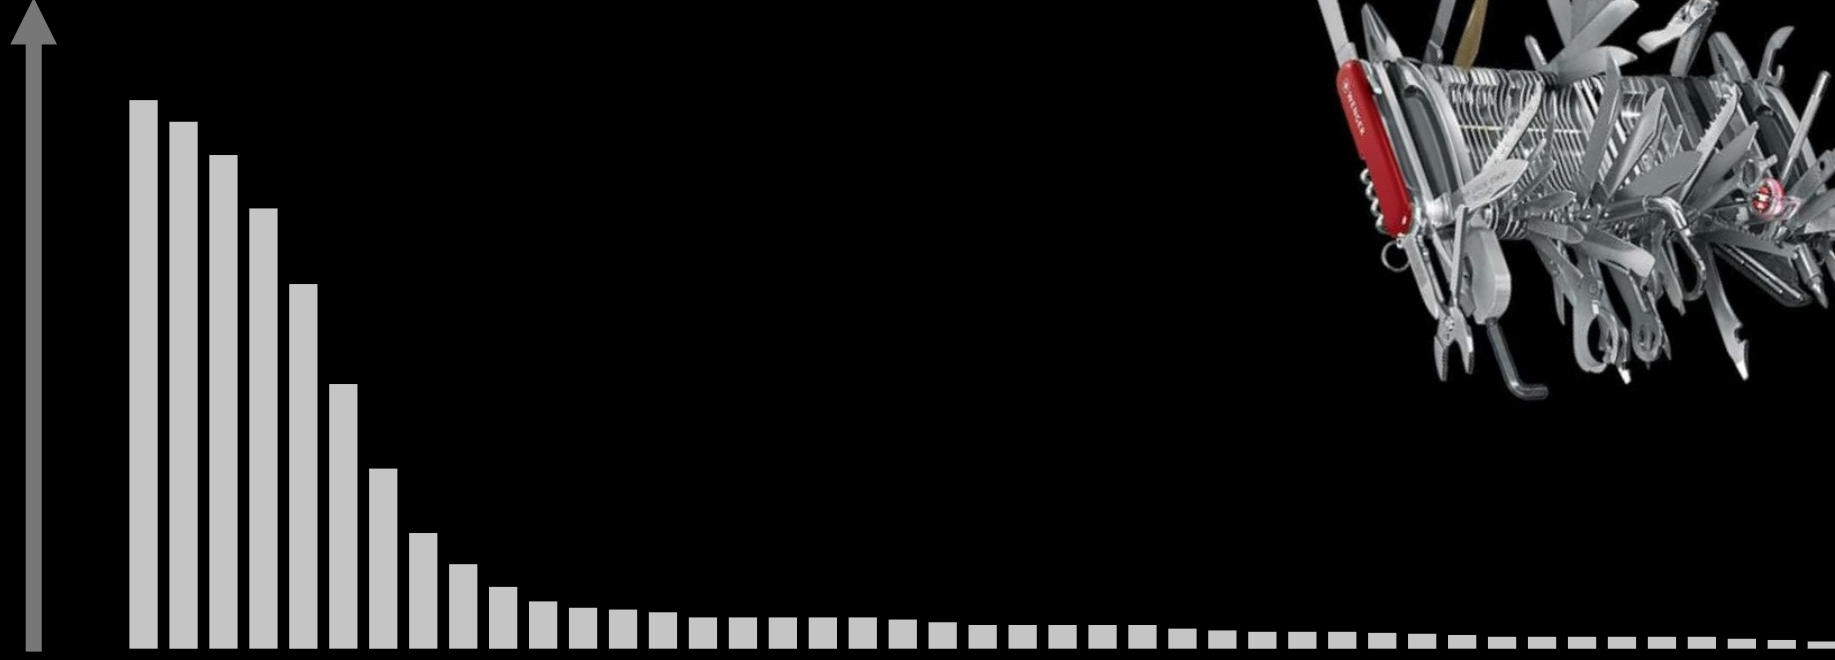

usefulness

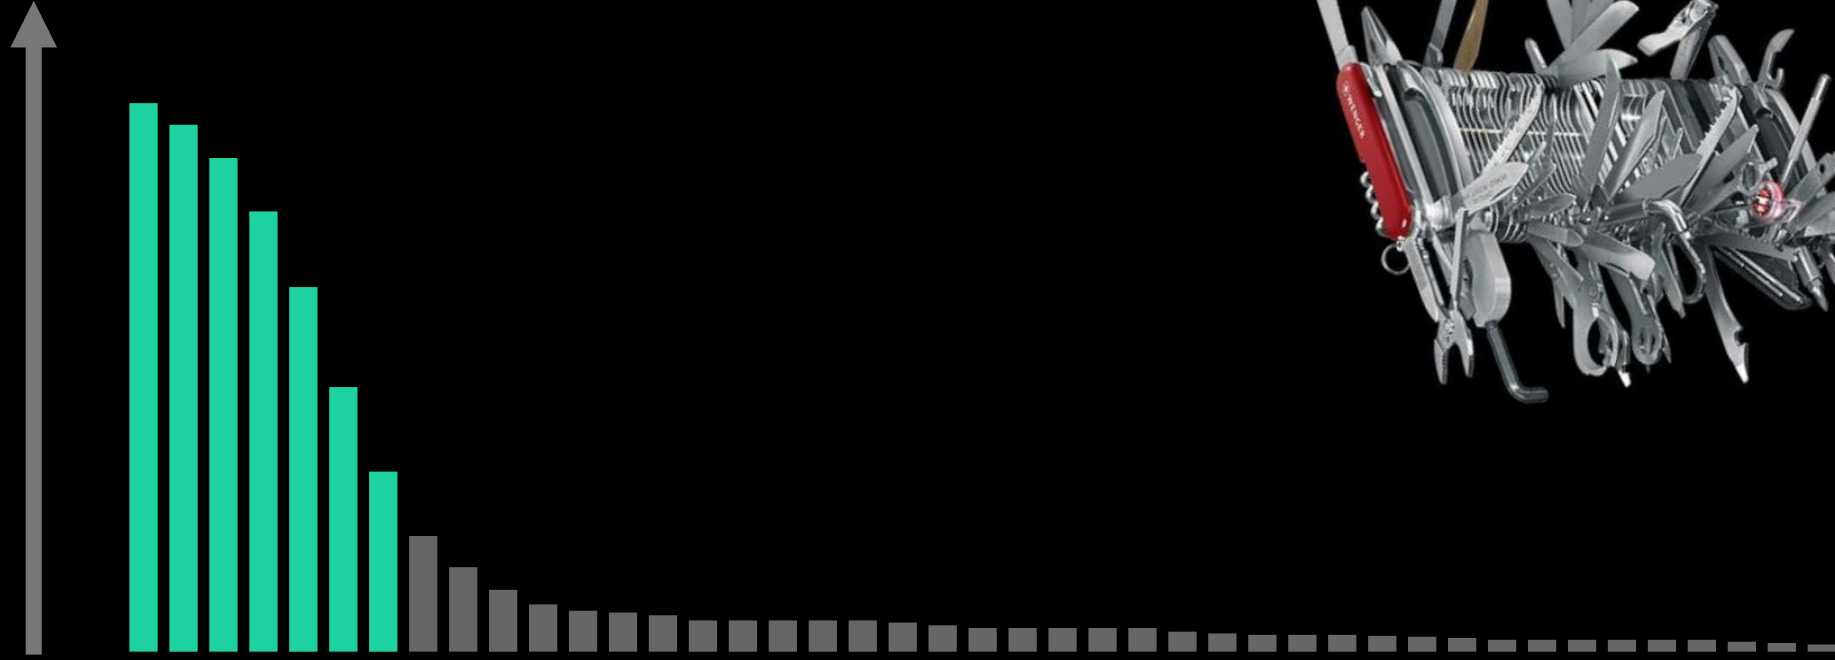


usefulness

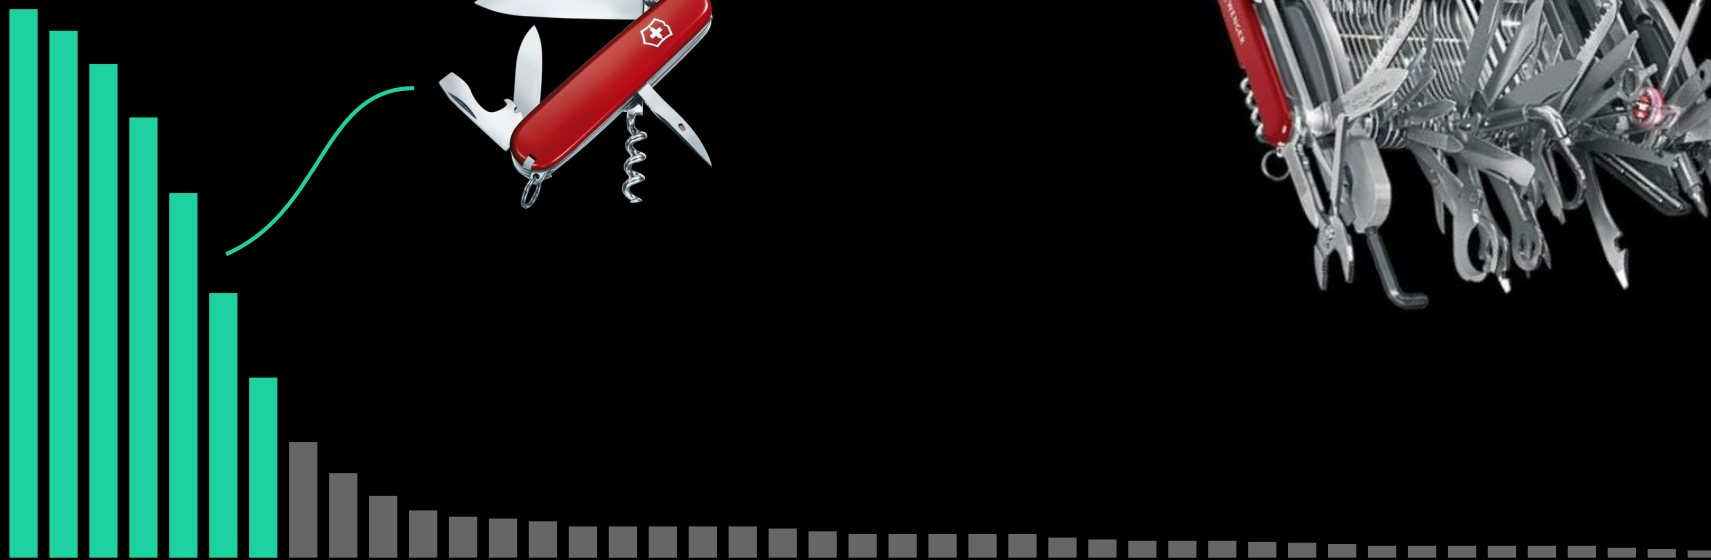

minimalist



usefulness




The most
essential
aspects

minimalist



usefulness




The most
essential
aspects



minimalist

maximalist

usefulness



The most
essential
aspects



Distractions!

minimalist

maximalist



MINIMALIST

MAXIMALIST

RISK MANAGEMENT



RISK MANAGEMENT

[illegible]





ID	Author	Date Registered	Category	Desc.	Probability	Impact	EV	Proximity	Response Categories	Responses	Status	Owner	Actionee
					Low	Medium							
					Medium	Low							
					High	Low							
					High	High							
					Low	Low							
					Medium	Medium							




ID	Author	Date Registered	Category	Desc.	Probability	Impact	EV	Proximity	Response Categories	Responses	Status	Owner	Actionee
					20%	€50k							
					40%	€5k							
					70%	€12k							
					80%	€120k							
					10%	€20k							
					35%	€80k							

[illegible]

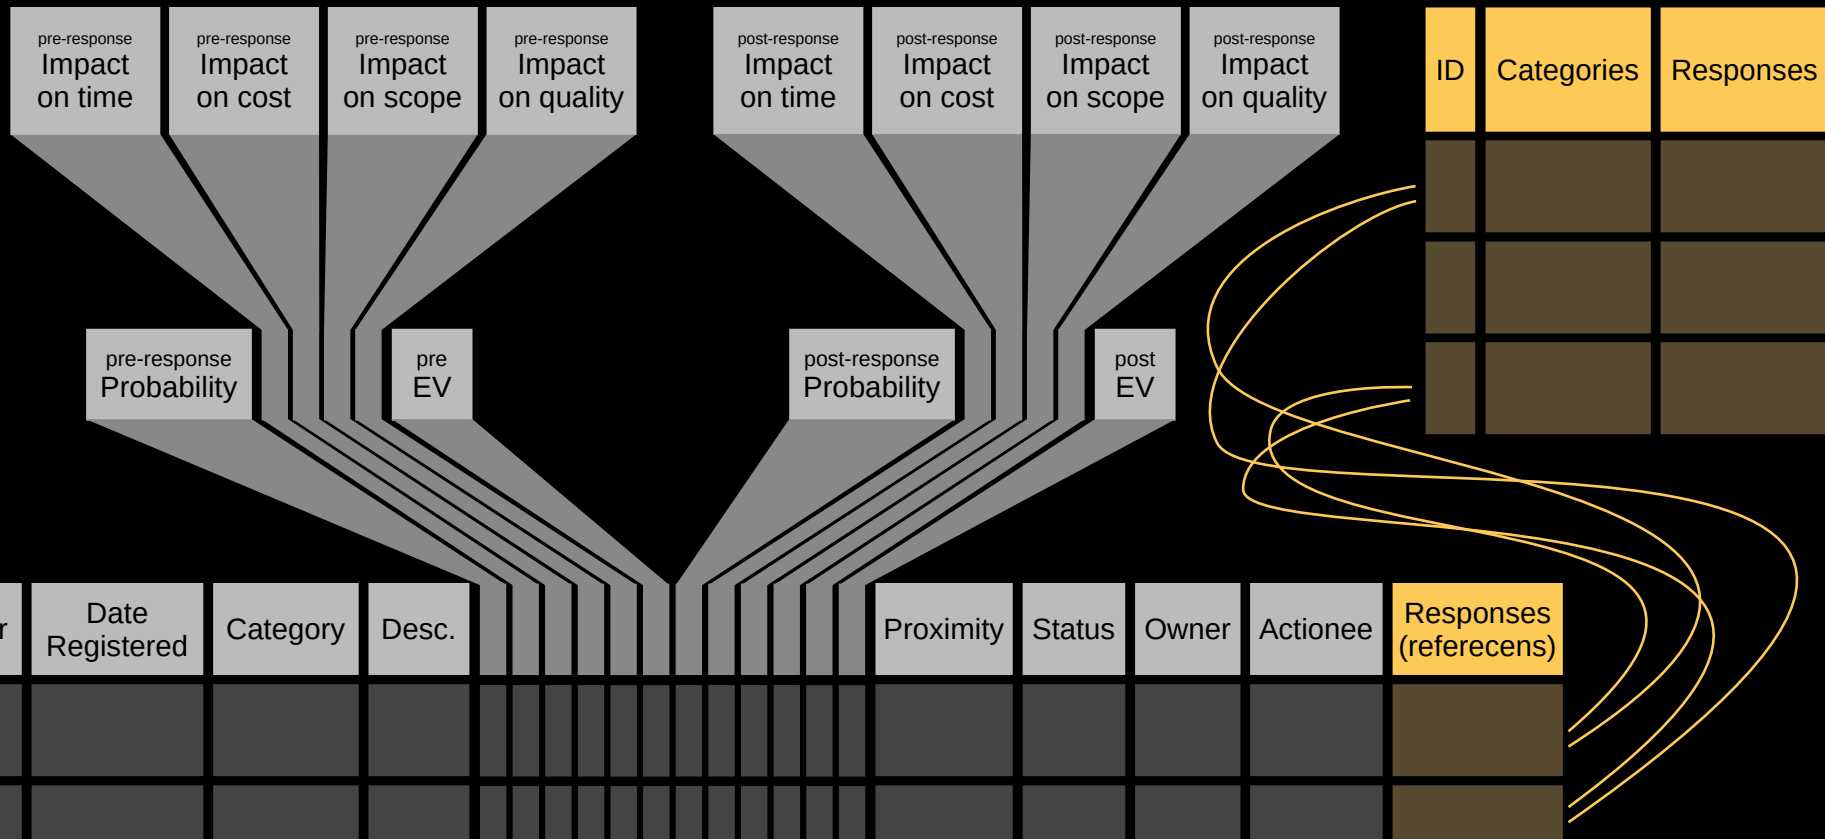

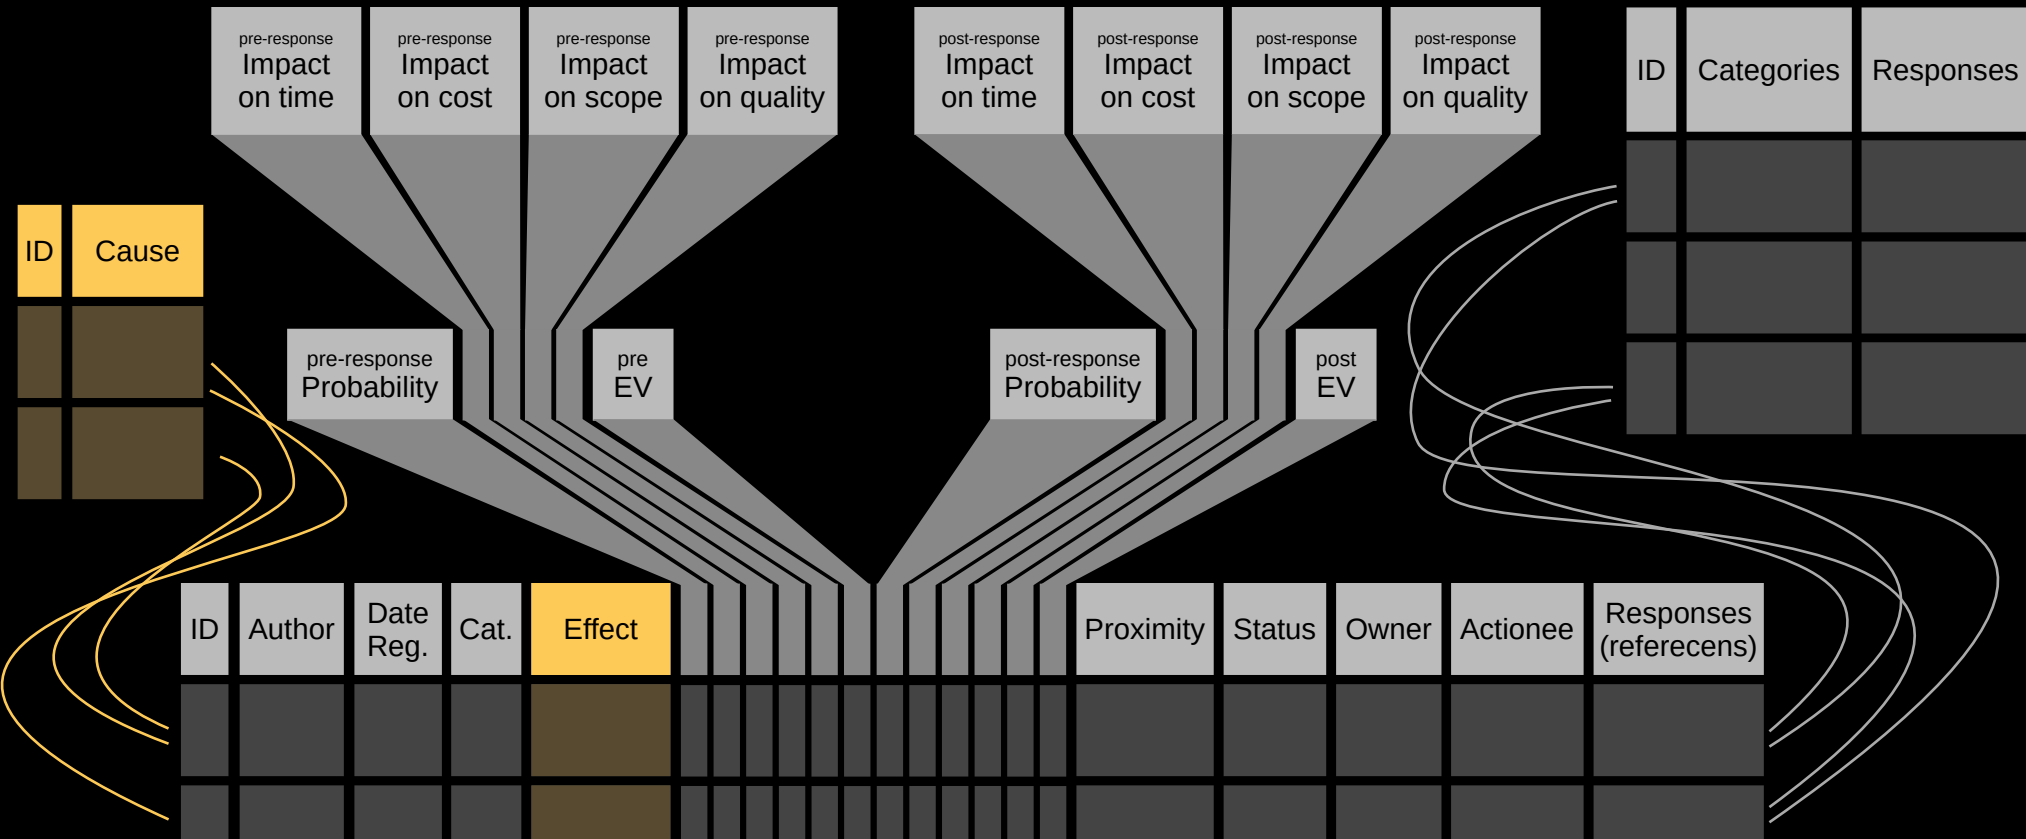

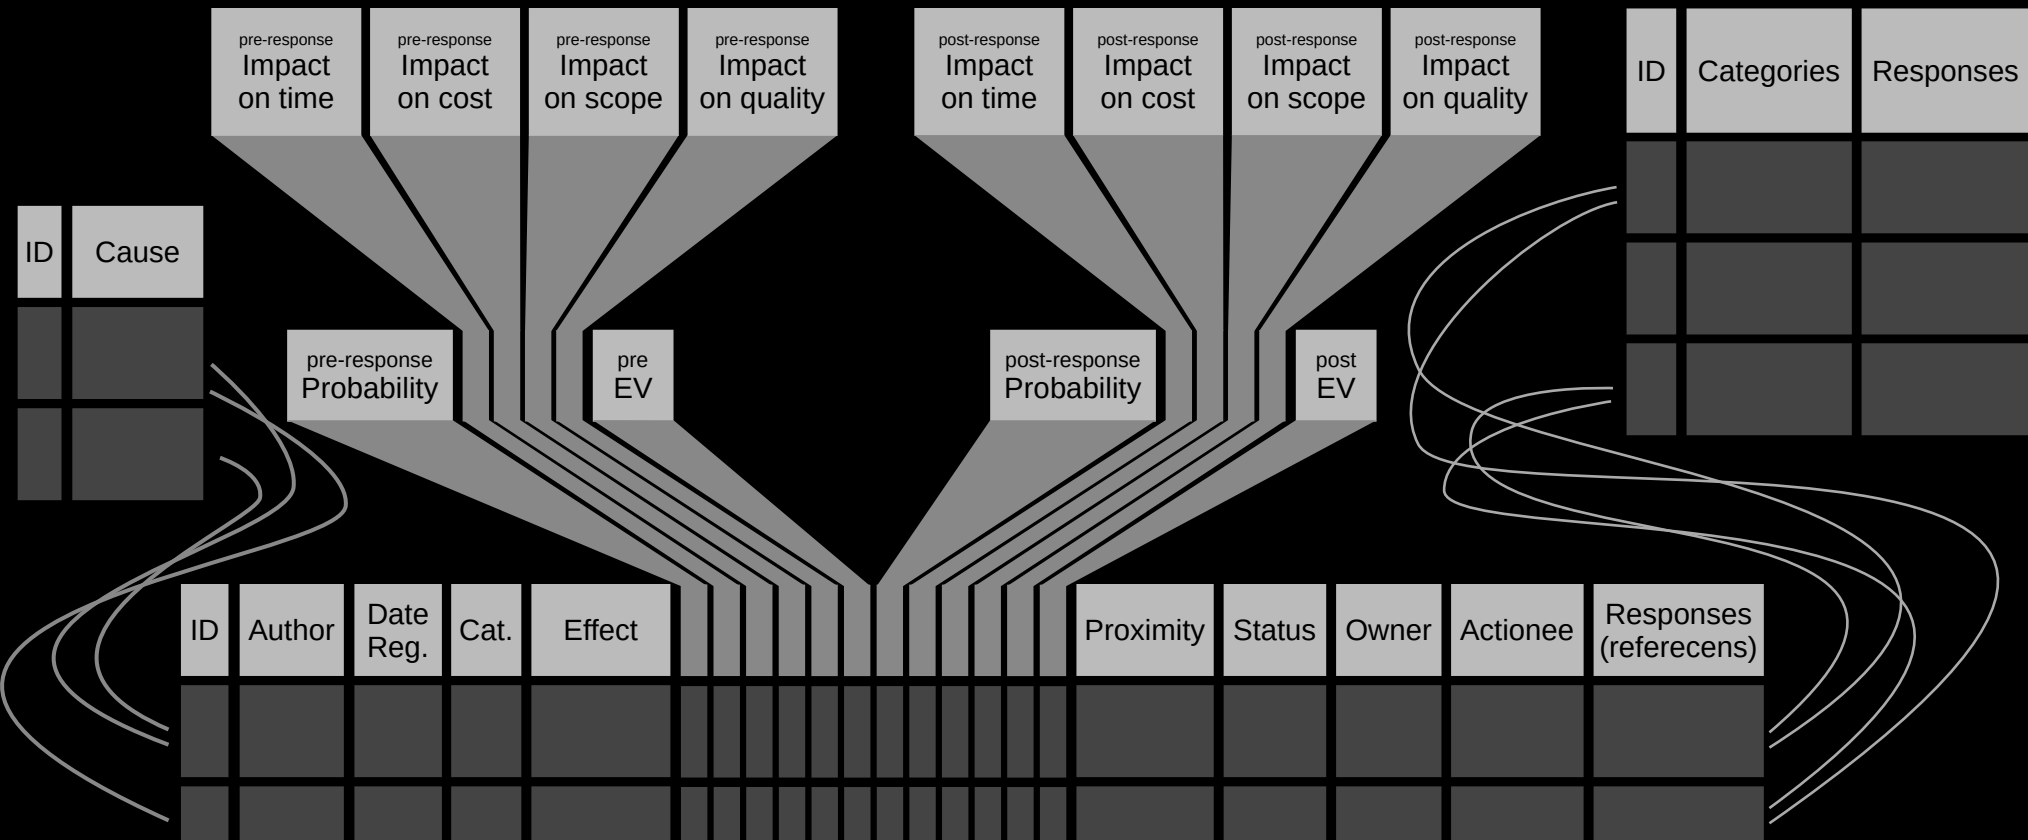



Custodian: Didi

The potential X/Y war!

2022-01-20, **Concern:**
Country X may attack Country Y, which may increase oil prices,
which in turn increases the cost of all material we have to buy for the project.



Custodian: Didi

The potential X/Y war!

2022-01-20, **Concern:**
Country X may attack Country Y, which may increase oil prices, which in turn increases the cost of all material we have to buy for the project.

2022-01-20, **Action:**
Let's take about two weeks and study the situation in detail.

2022-02-04, **Comment:**
There's an 80% chance that it will happen, and if so, our best estimate is 12% increase in the total project cost.

2022-02-04, **Action:**
Let's see if the customer would help us with it.

2022-02-06, **Comment:**
They don't!

2022-02-08, **Action:**
Let's get a loan as soon as possible and buy all the material now, before prices increase. That would limit our loss to maximum 4%.



Custodian: Didi

The potential X/Y war!

2022-01-20, **Concern:**
Country X may attack Country Y, which may increase oil prices, which in turn increases the cost of all material we have to buy for the project.

2022-01-20, **Action:**
Let's take about two weeks and study the situation in detail.

2022-02-04, **Comment:**
There's an 80% chance that it will happen, and if so, our best estimate is 12% increase in the total project cost.

2022-02-04, **Action:**
Let's see if the customer would help us with it.

2022-02-06, **Comment:**
They don't!

2022-02-08, **Action:**
Let's get a loan as soon as possible and buy all the material now, before prices increase. That would limit our loss to maximum 4%.

2022-02-20, **Comment:**
Everything is done. We're closing this follow-up item.



Custodian: Didi

The potential X/Y war!

2022-01-20, **Concern:**
Country X may attack Country Y, which may increase oil prices, which in turn increases the cost of all material we have to buy for the project.

2022-01-20, **Action:**
Let's take about two weeks and study the situation in detail.

2022-02-04, **Comment:**
There's an 80% chance that it will happen, and if so, our best estimate is 12% increase in the total project cost.

2022-02-04, **Action:**
Let's see if the customer would help us with it.

2022-02-06, **Comment:**
They don't!



2022-02-08, **Action:**
Let's get a loan as soon as possible and buy all the material now, before prices increase. That would limit our loss to maximum 4%.

2022-02-20, **Comment:**
Everything is done. We're closing this follow-up item.

2022-02-24, **P.S.:**
X started the war :(

2022-04-15, **P.S.:**
Without our upfront procurement, our project cost would have increased 18%.



Queued	In-Progress	To-Review	Closed
	 On-Hold 		

The potential X/Y war!

Custodian: Didi

2022-01-20, **Concern:**
Country X may attach Country Y, which may increase oil prices, which in turn increases the cost of all material we have to buy for the project.

2022-01-20, **Action:**
Let's take about two weeks and study the situation in detail.

2022-02-04, **Comment:**
There's an 80% chance that it will happen, and if so, our best estimate is 12% increase in the total project cost.

2022-02-04, **Action:**
Let's see if the customer would help us with it.


2022-02-06, **Comment:**
They don't!



2022-02-08, **Action:**
Let's get a loan as soon as possible and buy all the material now, before prices increase. That would limit our loss to maximum 4%.


2022-02-20, **Comment:**
Everything is done. We're closing this follow-up item.

2022-02-24, **P.S.:**
X started the war :(

2022-04-15, **P.S.:**
Without our upfront procurement, our project cost would have increased 18%.

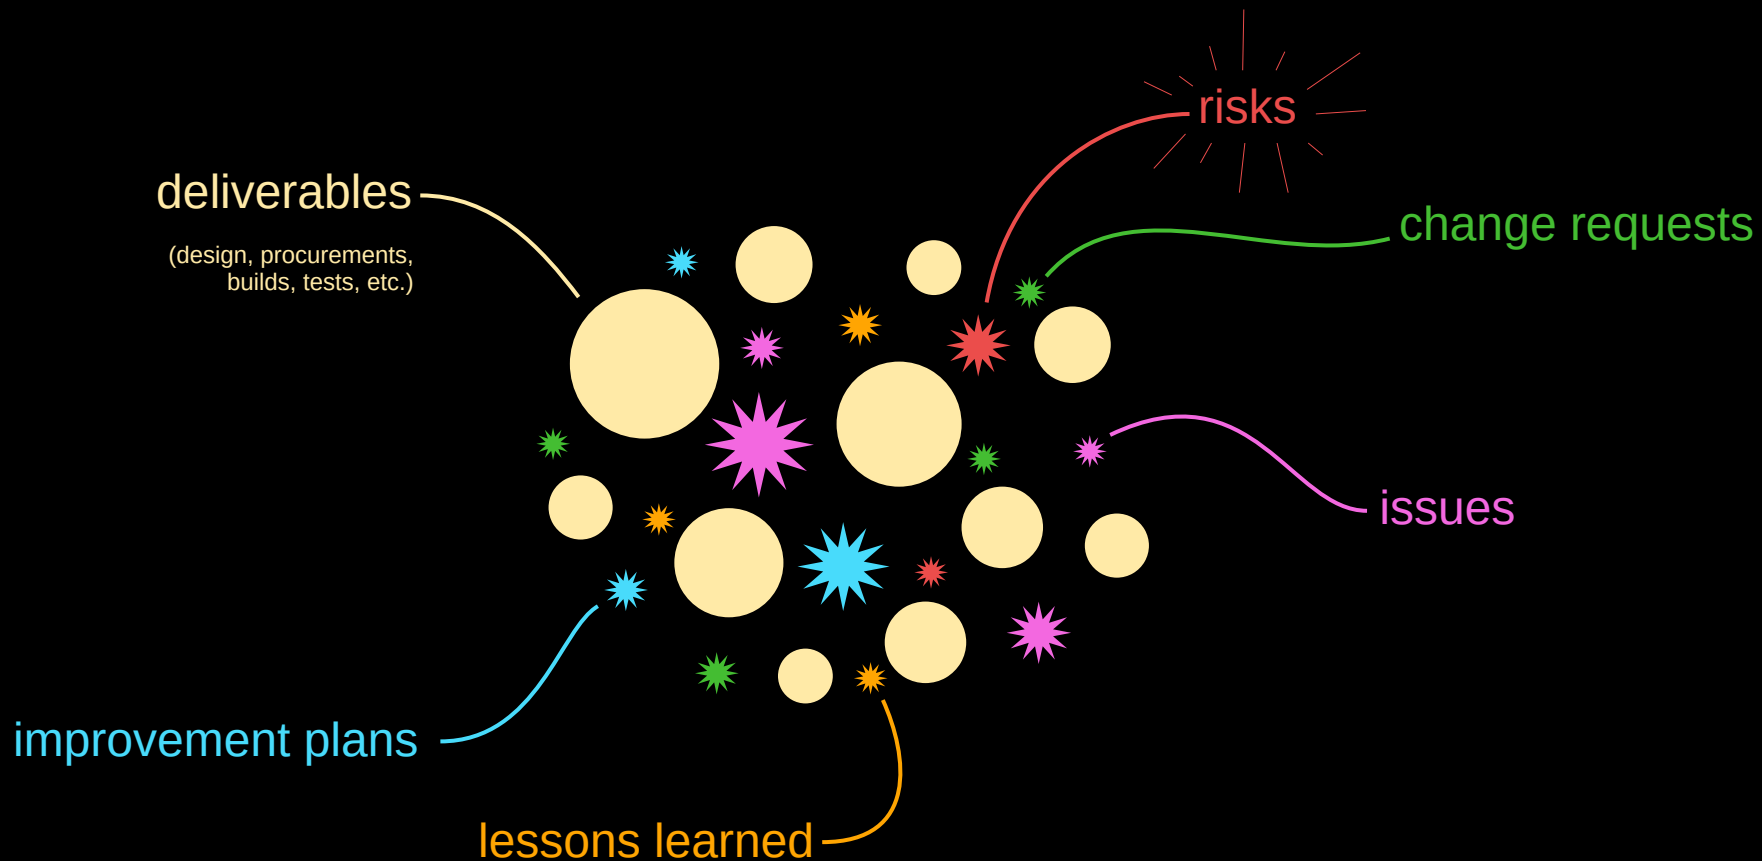

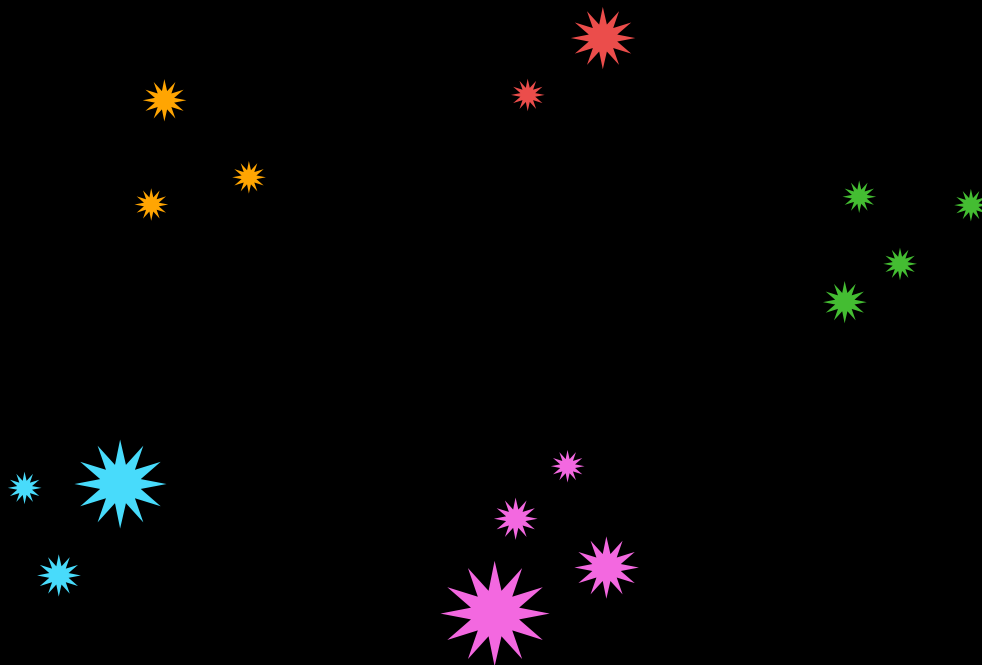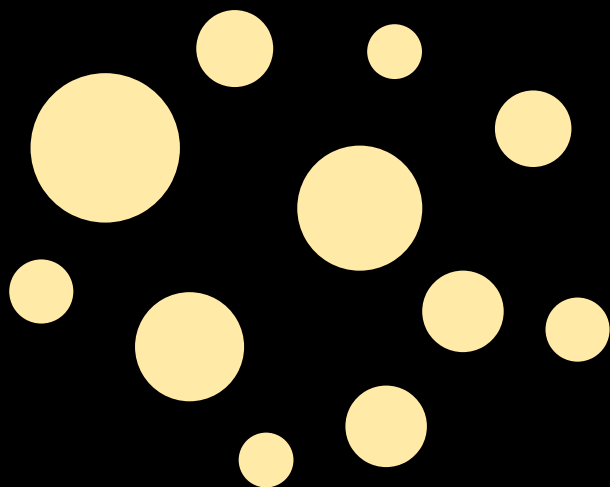


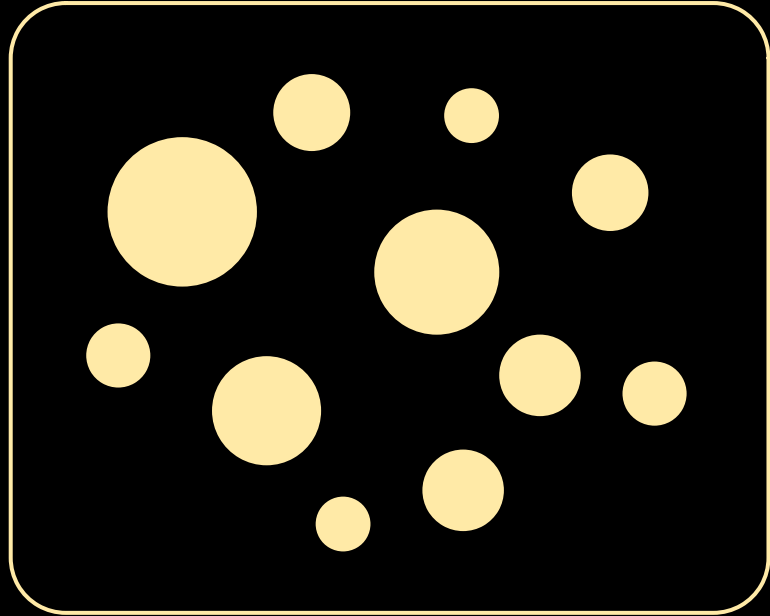


WBS / Schedule Model




Lessons Log




Risk Register




Change Requests
Change Log




Improvements Log




Issue Log/Register

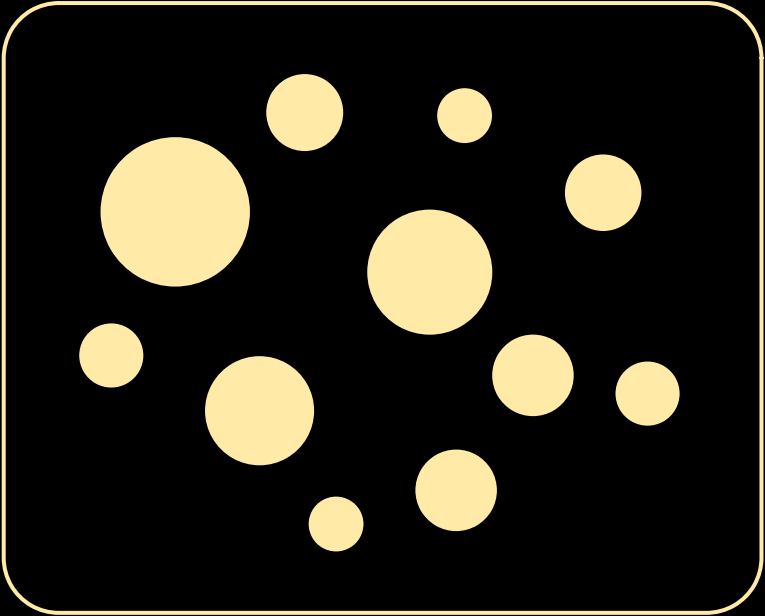


WBS / Schedule Model




Lessons Log




Risk Register




Change Requests
Change Log



Improvements Log




Issue Log/Register

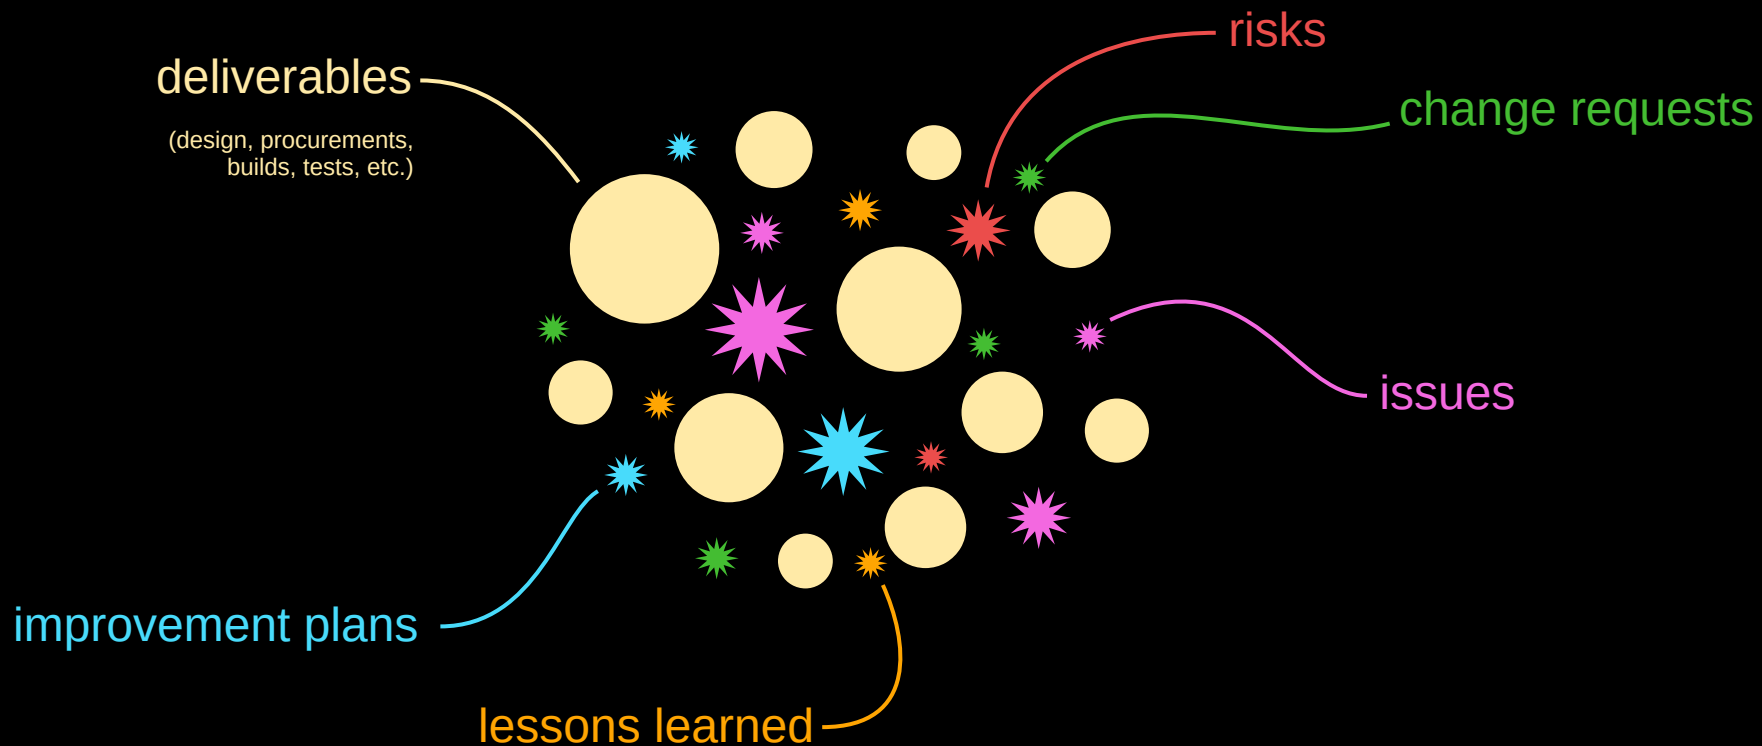




deliverables

(design, procurements,
builds, tests, etc.)

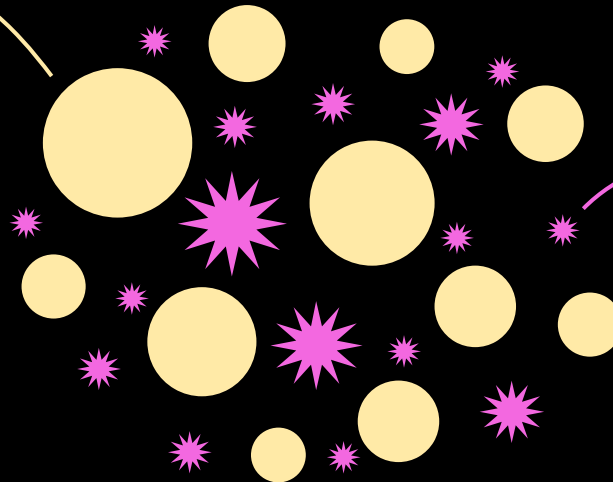


follow-up items

(risks, issues, change requests,
improvement plans, lessons learned)

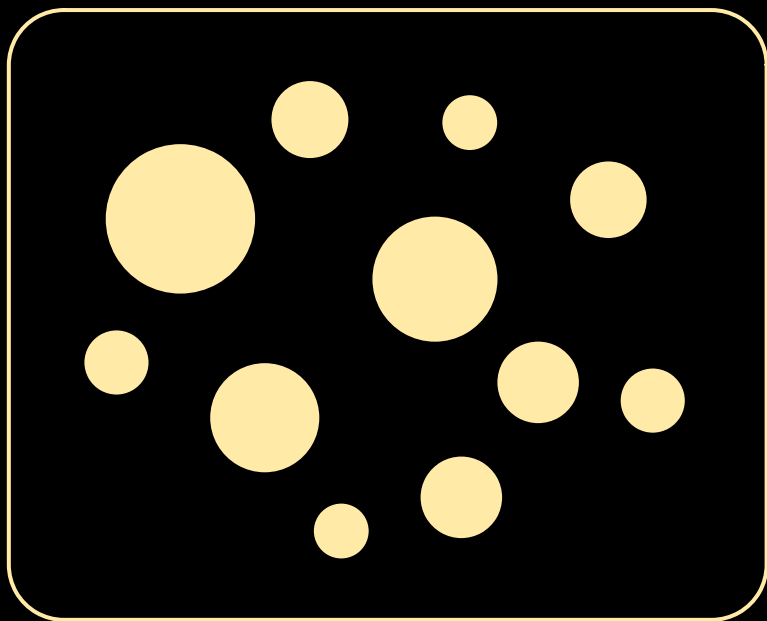

Deliverables Map

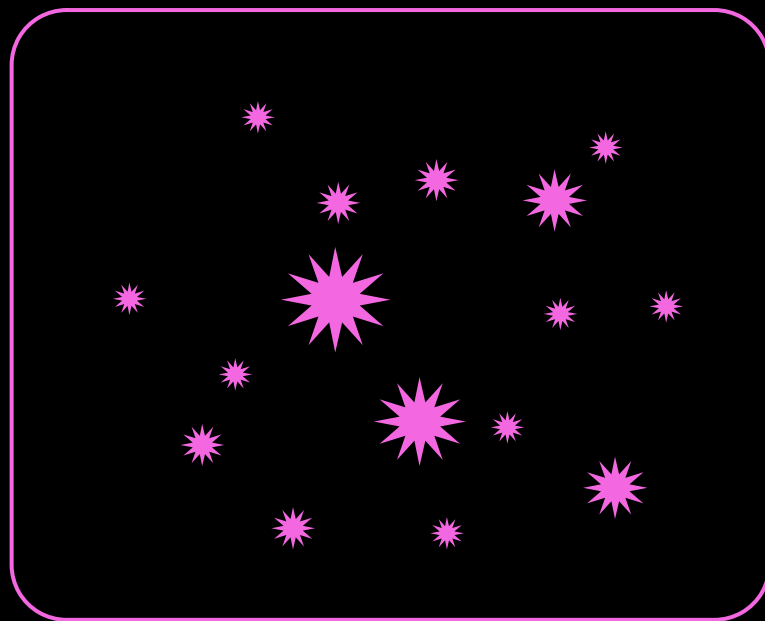

Follow-Up Register



The potential X/Y war!

Custodian: Didi

2022-01-20, **Concern:**
Country X may attach Country Y, which may increase oil prices, which in turn increases the cost of all material we have to buy for the project.

2022-01-20, **Action:**
Let's take about two weeks and study the situation in detail.

2022-02-04, **Comment:**
There's an 80% chance that it will happen, and if so, our best estimate is 12% increase in the total project cost.

2022-02-04, **Action:**
Let's see if the customer would help us with it.

2022-02-06, **Comment:**
They don't!

2022-02-08, **Action:**
Let's get a loan as soon as possible and buy all the material now, before prices increase. That would limit our loss to maximum 4%.

2022-02-20, **Comment:**
Everything is done. We're closing this follow-up item.

2022-02-24, **P.S.:**
X started the war :(

2022-04-15, **P.S.:**
Without our upfront procurement, our project cost would have increased 18%.


Queued	In-Progress	To-Review	Closed
	On-Hold		

Follow-Up Register




deliverables

(design, procurements,
builds, tests, etc.)

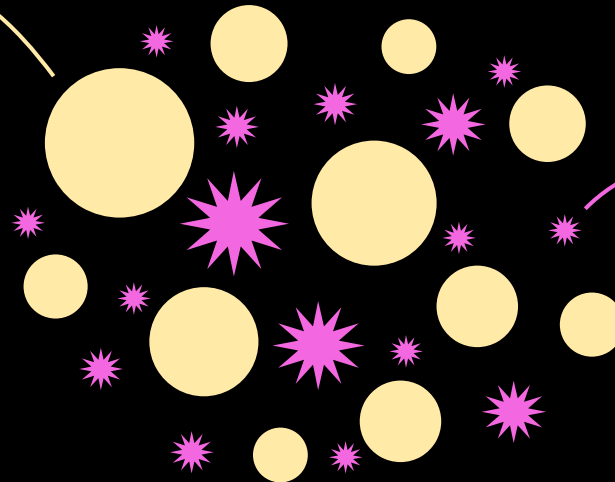


follow-up items

(risks, issues, change requests,
improvement plans, lessons learned)

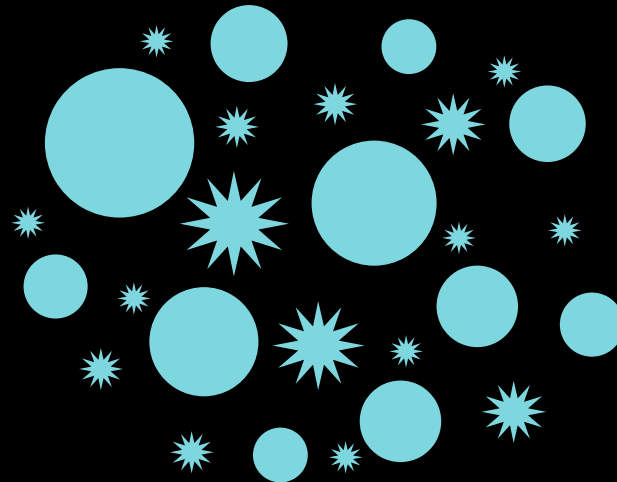

Items!

(risks, issues, change requests, improvement plans, lessons learned, design, procurements, builds, tests, etc.)

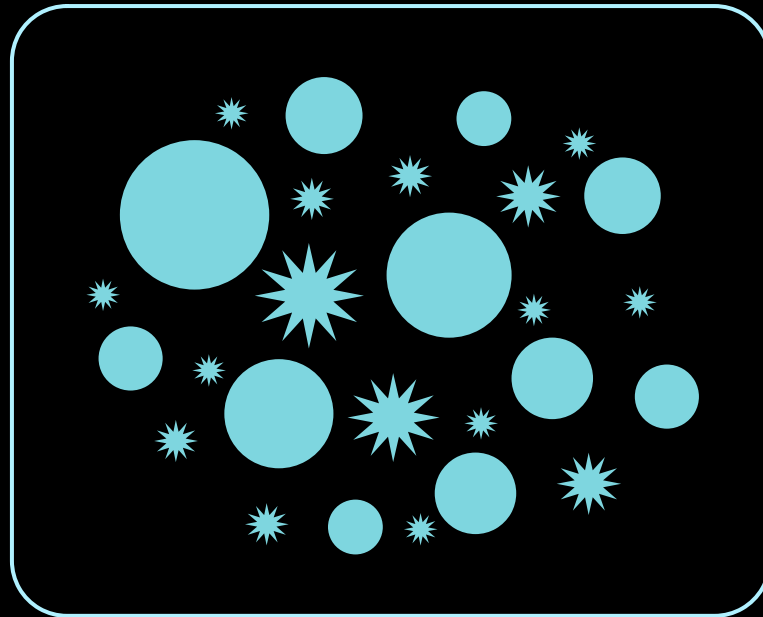


Integrated Project Board






3


micro.P3.express

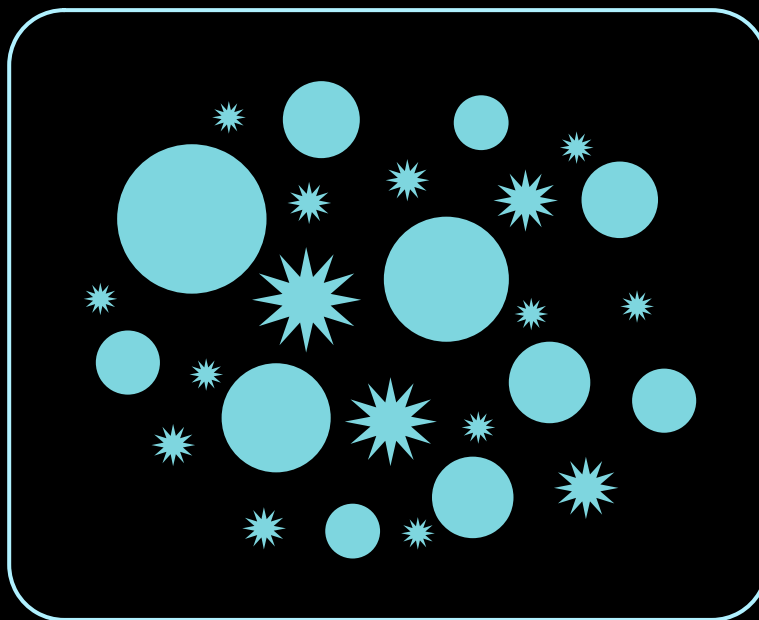


Integrated Project Board

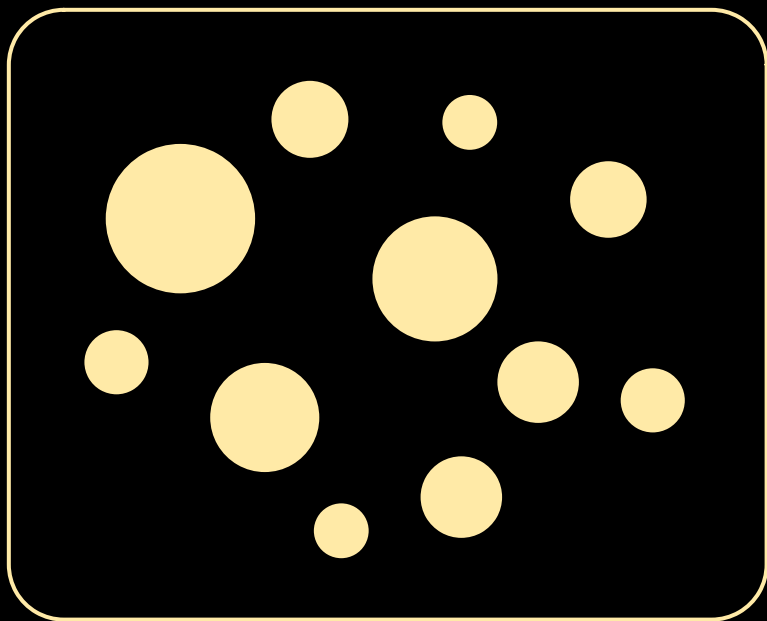



Deliverables Map

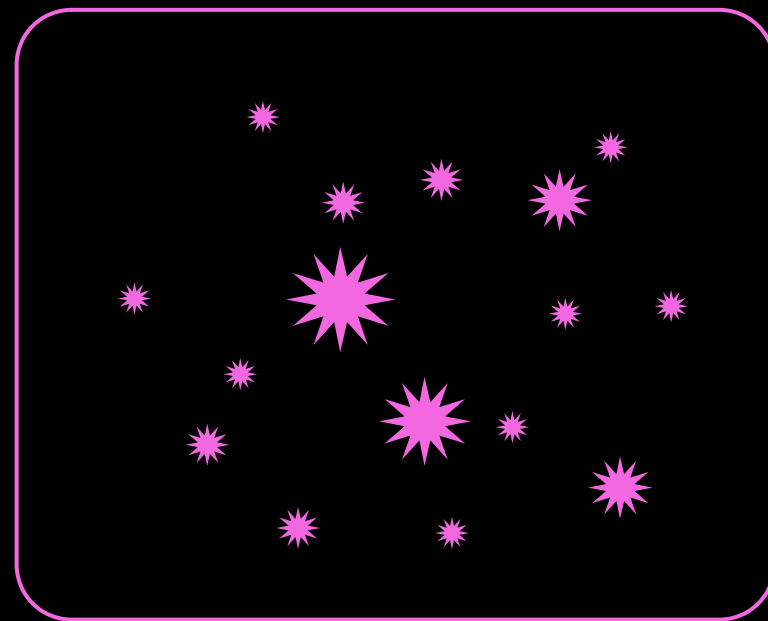

Follow-Up Register

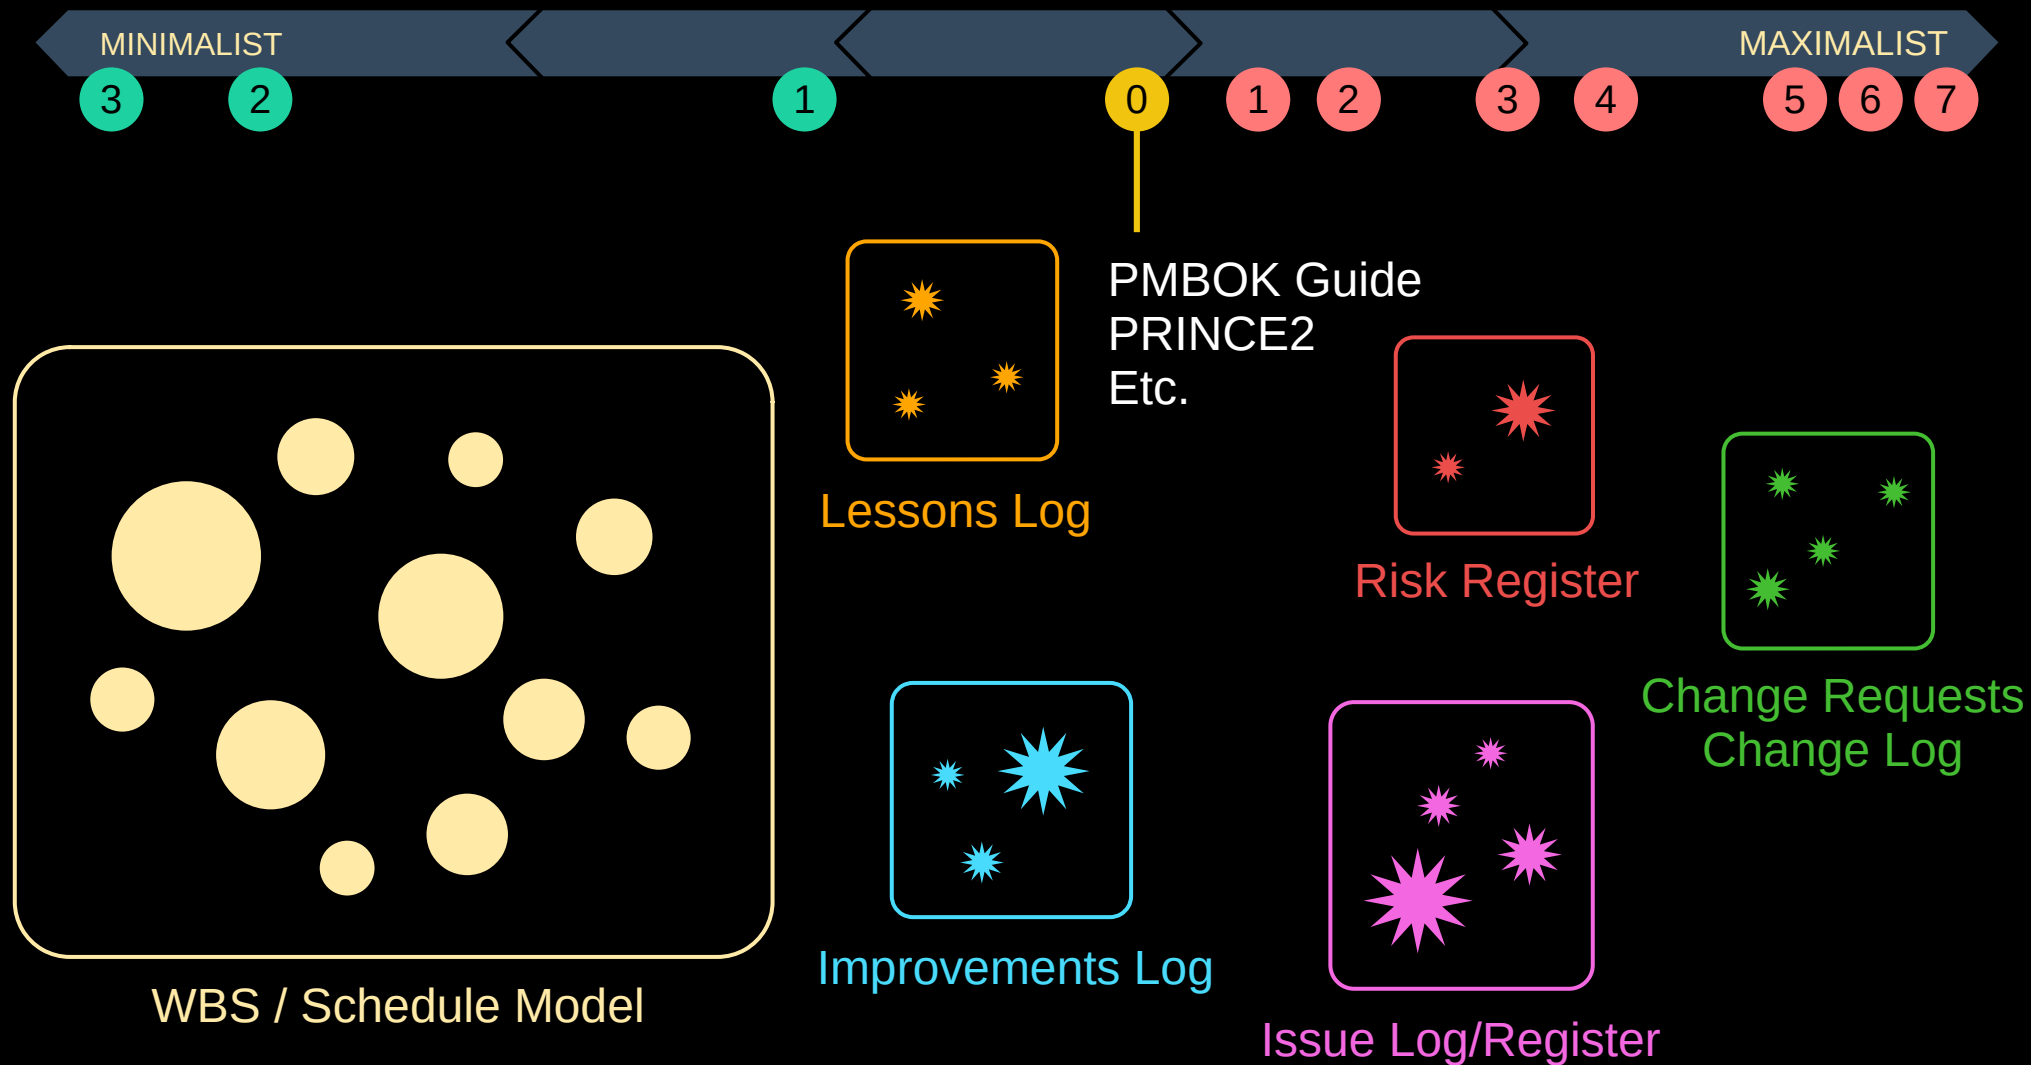

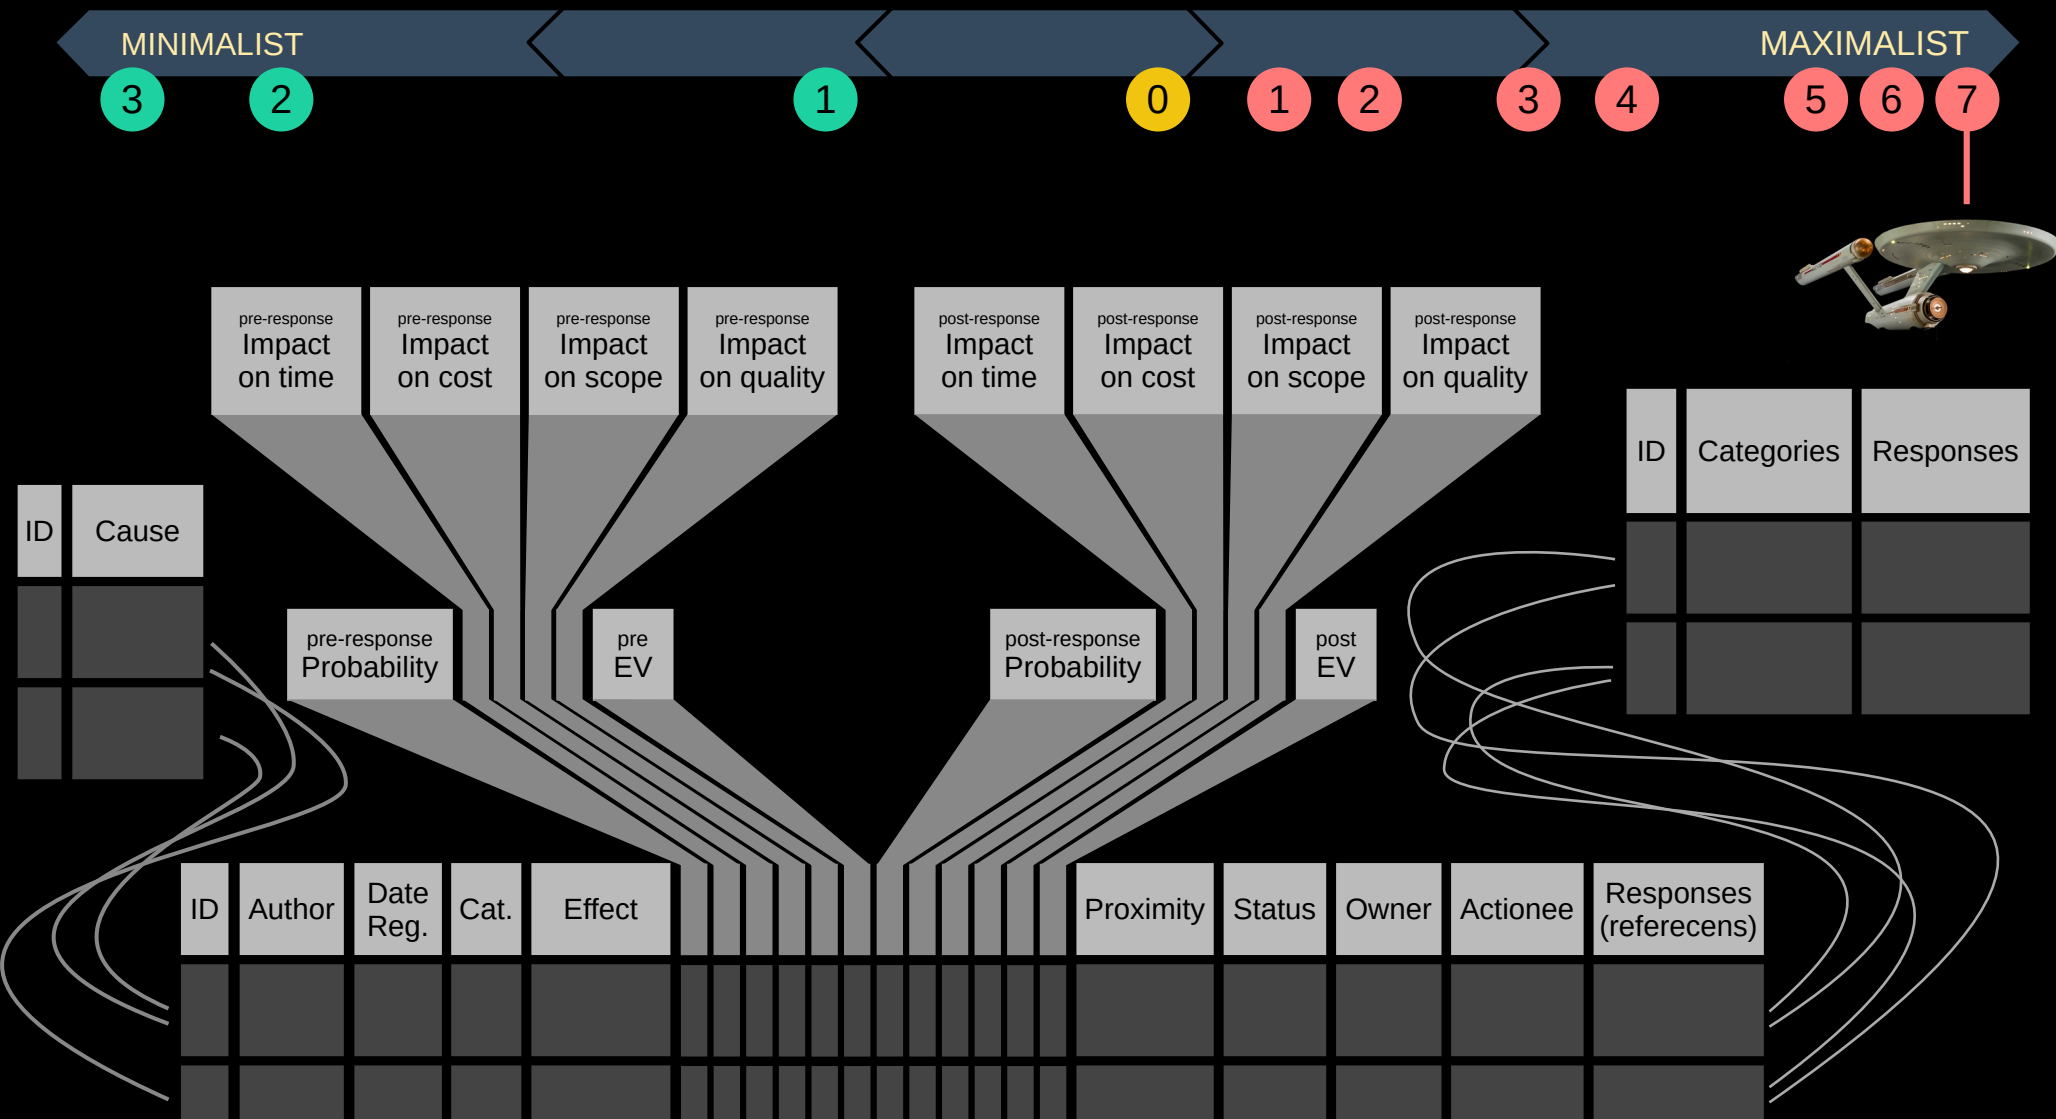

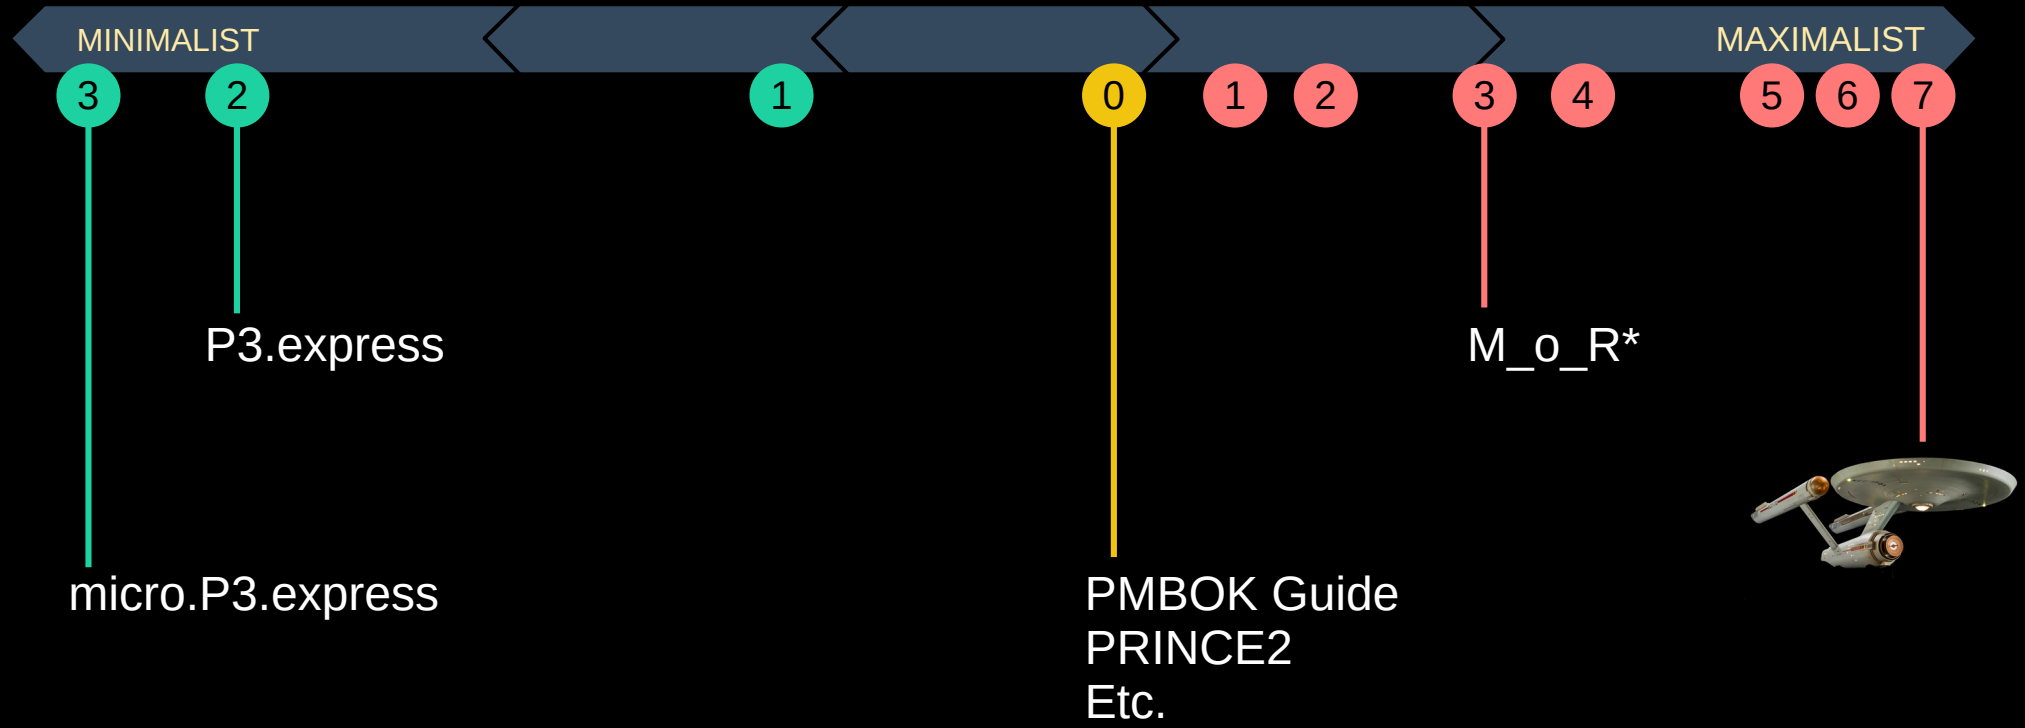

A yellow speech bubble with a black outline and a tail pointing towards the bottom left, set against a solid black background.

**Do you want
to try it?**

The potential X/Y war!

Custodian: Didi

2022-01-20, **Concern:**

Country X may attack Country Y, which may increase oil prices, which in turn increases the cost of all material we have to buy for the project.

2022-01-20, **Action:**

Let's take about two weeks and study the situation in detail.

2022-02-04, **Comment:**

There's an 80% chance that it will happen, and if so, our best estimate is 12% increase in the total project cost.

2022-02-04, **Action:**

Let's see if the customer would help us with it.

2022-02-06, **Comment:**

They don't!

2022-02-08, **Action:**

Let's get a loan as soon as possible and buy all the material now, before prices increase. That would limit our loss to maximum 4%.

2022-02-20, **Comment:**

Everything is done. We're closing this follow-up item.

2022-02-24, **P.S.:**

X started the war :(

2022-04-15, **P.S.:**

Without our upfront procurement, our project cost would be

Risks

Issues

Change
Requests

Improvement
Plans

Lessons

Queued	In-Progress	To-Review	Closed
	  On-Hold 	 	    

Do you want
to try it?

Follow-Up Register



<https://nader.pm/presentations/bg-2025/>

- My website, email address, LinkedIn profile, etc.
- This slide deck
- Related resources
- Etc.
