

License


This slide deck is provided with an open CC-BY license, which means that you can use it (share and adapt it for commercial and non-commercial purposes) without asking for permission and only by mentioning the original source.

More information:

<https://creativecommons.org/licenses/by/4.0/>

Some of the content in this slide deck (the Integrated Project Board, the Follow-Up Register, etc.) are borrowed from OMIMO, which are available with an open CC-BY license and you can reuse them by mentioning their source:

<https://omimo.org/>




Empower Your Life with


P1 . express

Nader K. Rad


School 21, Samarkand, 2026-05-13



Nader K. Rad




Nader K. Rad



Nader K. Rad

minimalist project management architect

Core team member @ OMIMO
Training specialist @ Management Plaza

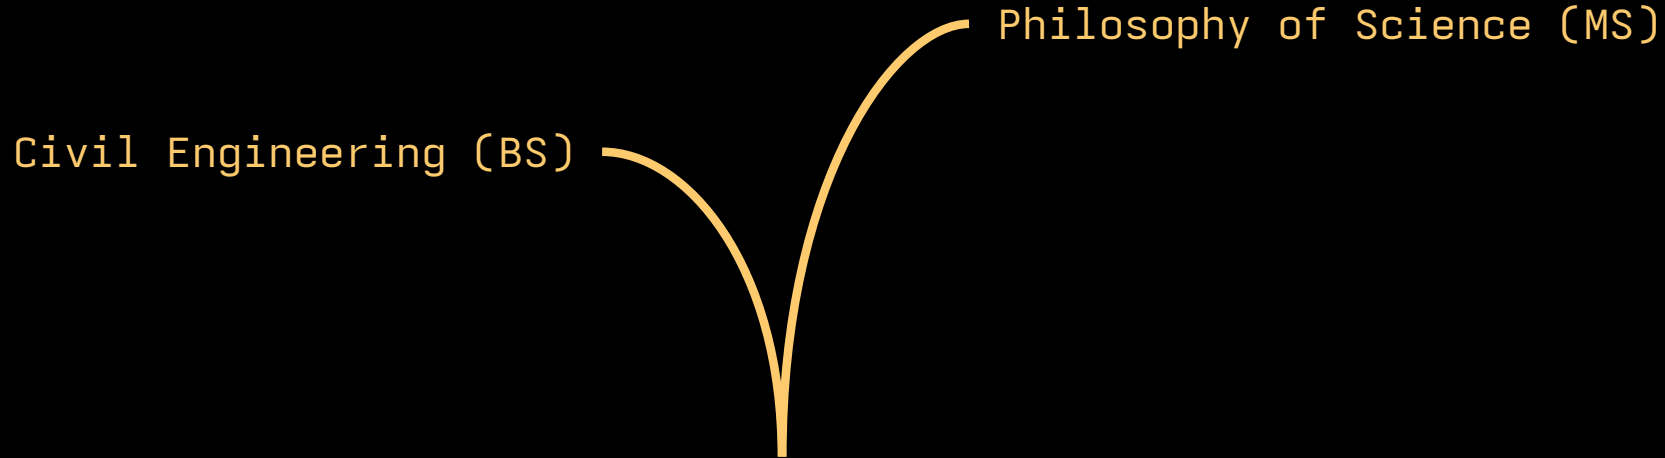

Nader K. Rad

minimalist project management architect

Core team member @ OMIMO
Training specialist @ Management Plaza

29 Years of
working with
projects

Nader K. Rad

minimalist project management architect

Core team member @ OMIMO
Training specialist @ Management Plaza

Process Plant Projects


IT Projects

Construction projects

Nader K. Rad

minimalist project management architect

Core team member @ OMIMO
Training specialist @ Management Plaza

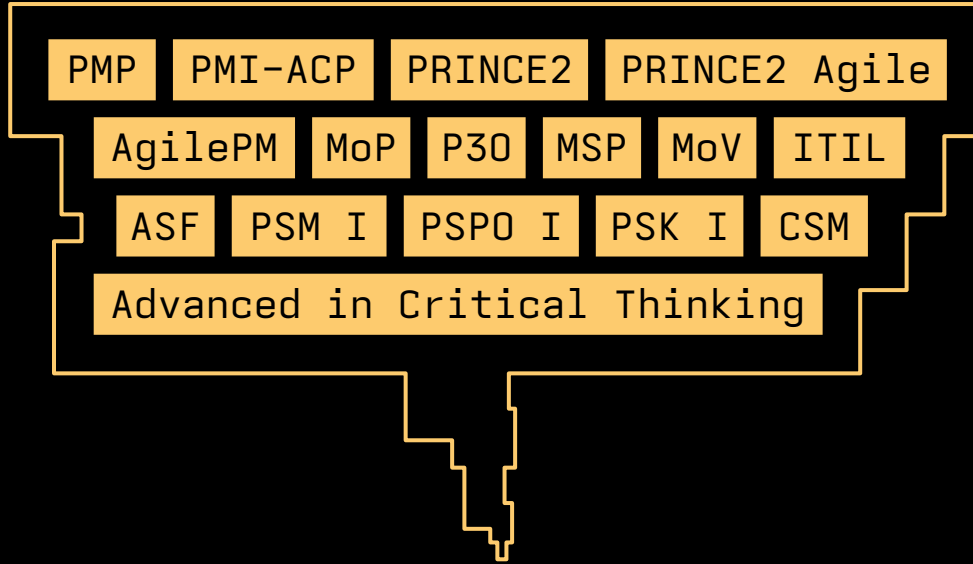


Nader K. Rad

minimalist project management architect

Core team member @ OMIMO
Training specialist @ Management Plaza

Contributing to standards
Writing books and articles
Making eLearning courses
Giving presentations




Nader K. Rad

minimalist project management architect

Core team member @ OMIMO
Training specialist @ Management Plaza

Contributing to standards
Writing books and articles
Making eLearning courses
Giving presentations



Nader K. Rad

minimalist project management architect

Core team member @ OMIMO
Training specialist @ Management Plaza

Contributing to standards
Writing books and articles
Making eLearning courses
Giving presentations



~50 books

Nader K. Rad

minimalist project management architect

Core team member @ OMIMO
Training specialist @ Management Plaza

CORE TEAM

P3.express
NUPP
PMBOK Guide v7
micro.P3.express
P5.express
P1.express
Compass
P4.express

CONSULTANT

PRINCE2 v6
PRINCE2 Agile v1
MSP v4
PRINCE2 Agile v2

Disclaimer!

Opinions in the presentation are mine and not those of any organization I've worked with, such as OMIMO, PMI, and PeopleCert.

Nader K. Rad

minimalist project management architect

Core team member @ OMIMO
Training specialist @ Management Plaza

CORE TEAM

P3.express
NUPP
PMBOK Guide v7
micro.P3.express
P5.express
P1.express
Compass
P4.express

CONSULTANT

PRINCE2 v6
PRINCE2 Agile v1
MSP v4
PRINCE2 Agile v2

Nader K. Rad



minimalist project management architect


Core team member @ OMIMO
Training specialist @ Management Plaza



Nader K. Rad

minimalist project management architect

Core team member @ OMIMO
Training specialist @ Management Plaza

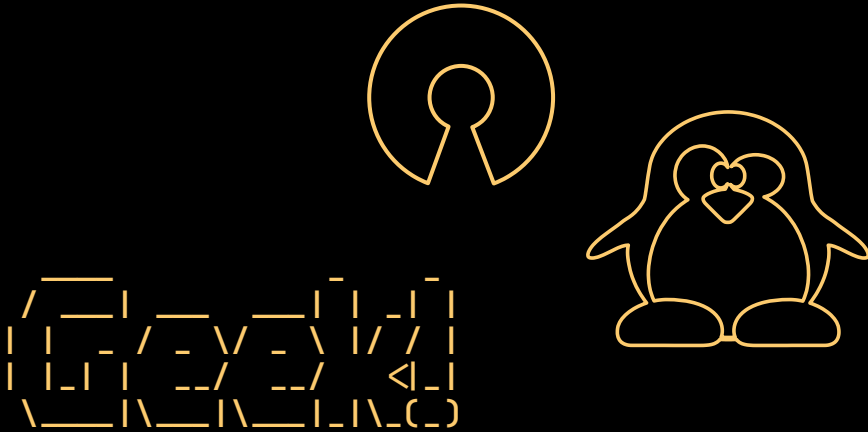

Nader K. Rad

minimalist project management architect



Core team member @ OMIMO
Training specialist @ Management Plaza



Nader K. Rad

minimalist project management architect



Core team member @ OMIMO
Training specialist @ Management Plaza



Nader K. Rad

minimalist project management architect



Core team member @ OMIMO
Training specialist @ Management Plaza



Nader K. Rad

minimalist project management architect


Core team member @ OMIMO
Training specialist @ Management Plaza



Nader K. Rad

minimalist project management architect

Core team member @ OMIMO
Training specialist @ Management Plaza




P1.express



P1.express




P1.express



A libre, minimalist task management method for individuals




P1.express



A libre, minimalist task management method for individuals



P1.express




A libre, minimalist task management method for individuals

Free of charge



P1.express




A libre, minimalist task management method for individuals

Free of charge

Free of copyright restrictions



P1.express



A libre, minimalist task management method for individuals


Avoiding clutter and waste by
focusing on the essentials

Free of charge

Free of copyright restrictions



P1.express



A libre, minimalist task management method for individuals

Avoiding clutter and waste by
focusing on the essentials


Not software

Free of charge

Free of copyright restrictions



P1.express



A libre, minimalist task management method for individuals

Avoiding clutter and waste by
focusing on the essentials

Not software


Not a “guide”

Free of charge

Free of copyright restrictions



P1.express



A libre, minimalist task management method for individuals

Avoiding clutter and waste by
focusing on the essentials

Not software

Not a “guide”


Free of charge

Free of copyright restrictions

from
OMIMO



P1.express



A libre, minimalist task management method for individuals

Avoiding clutter and waste by
focusing on the essentials

Not software

Not a “guide”

Free of charge


Free of copyright restrictions

from
OMIMO

Open Minimalist Modules



P1.express




A libre, minimalist task management method for individuals



P1.express




P1.express



Why?!




P1.express




Giving up




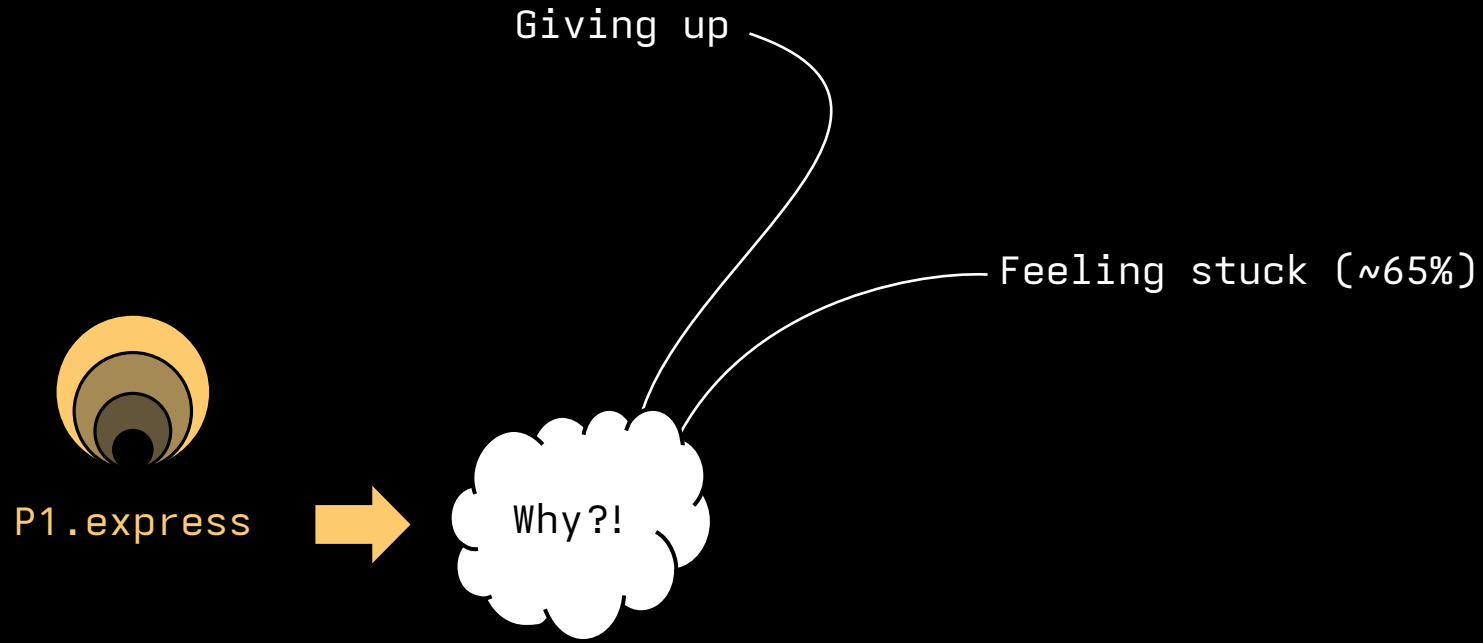

Feeling stuck statistic: From a 2024 Glassdoor research in the US

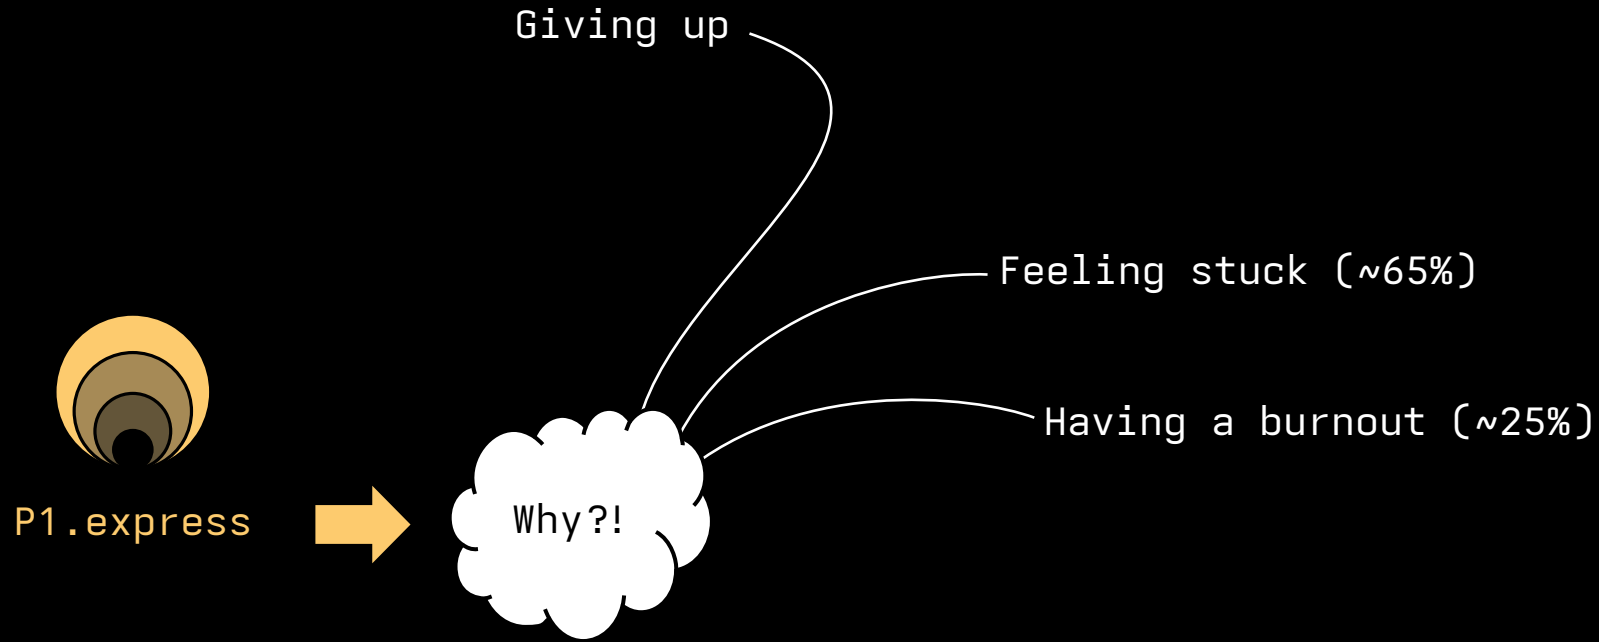

Burnout statistic: From a semi-global research done by McKinsey
Feeling stuck statistic: From a 2024 Glassdoor research in the US

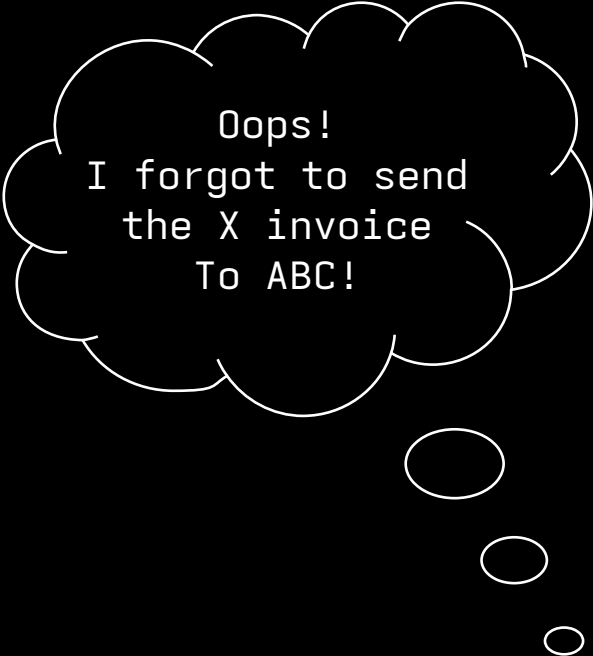

Oops!
I forgot to send
the X invoice
To ABC!

Prepare and send the X invoice to ABC.

Prepare and send the X invoice to ABC.



OH! The router
is disconnected
again!!!

Prepare and send the X invoice to ABC.

Fix the random disconnections in the router.

Prepare and send the X invoice to ABC.
Fix the random disconnections in the router.
↻ Water the plants – every 5 days
Record a video about procrastination.
Write the digital rights report for the UN.
↻ Check the server logs – every 2 weeks
Visit Liege to see its book market.
Add a plain text sitemap to all websites.
↻ Do laundry – every Sunday
Review Dilshod's screenplay.
Submit the ZIM packages to the Kiwix library.
⋮



Your task list

Prepare and send the X invoice to ABC.
Fix the random disconnections in the router.
↻ Water the plants – every 5 days
Record a video about procrastination.
Write the digital rights report for the UN.
↻ Check the server logs – every 2 weeks
Visit Liege to see its book market.
Add a plain text sitemap to all websites.
↻ Do laundry – every Sunday
Review Dilshod's screenplay.
Submit the ZIM packages to the Kiwix library.
⋮

Your task list

Everything you

- have to do, or
- want to do, or
- consider doing.

Prepare and send the X invoice to ABC.
Fix the random disconnections in the router.
↻ Water the plants – every 5 days
Record a video about procrastination.
Write the digital rights report for the UN.
↻ Check the server logs – every 2 weeks
Visit Liege to see its book market.
Add a plain text sitemap to all websites.
↻ Do laundry – every Sunday
Review Dilshod's screenplay.
Submit the ZIM packages to the Kiwix library.
⋮

Your task list

Everything you

- have to do, or
- want to do, or
- consider doing.

Won't
forget

Prepare and send the X invoice to ABC.
Fix the random disconnections in the router.
↻ Water the plants – every 5 days
Record a video about procrastination.
Write the digital rights report for the UN.
↻ Check the server logs – every 2 weeks
Visit Liege to see its book market.
Add a plain text sitemap to all websites.
↻ Do laundry – every Sunday
Review Dilshod's screenplay.
Submit the ZIM packages to the Kiwix library.
⋮

Your task list

Everything you

- have to do, or
- want to do, or
- consider doing.

Won't
forget

Saving
mental
energy

Prepare and send the X invoice to ABC.
Fix the random disconnections in the router.
↻ Water the plants – every 5 days
Record a video about procrastination.
Write the digital rights report for the UN.
↻ Check the server logs – every 2 weeks
Visit Liege to see its book market.
Add a plain text sitemap to all websites.
↻ Do laundry – every Sunday
Review Dilshod's screenplay.
Submit the ZIM packages to the Kiwix library.
⋮

Your task list

Everything you

- have to do, or
- want to do, or
- consider doing.


Won't
forget

Saving
mental
energy

Avoiding
distractions

Prepare and send the X invoice to ABC.
Fix the random disconnections in the router.
↻ Water the plants – every 5 days
Record a video about procrastination.
Write the digital rights report for the UN.
↻ Check the server logs – every 2 weeks
Visit Liege to see its book market.
Add a plain text sitemap to all websites.
↻ Do laundry – every Sunday
Review Dilshod's screenplay.
Submit the ZIM packages to the Kiwix library.
⋮

Your task list

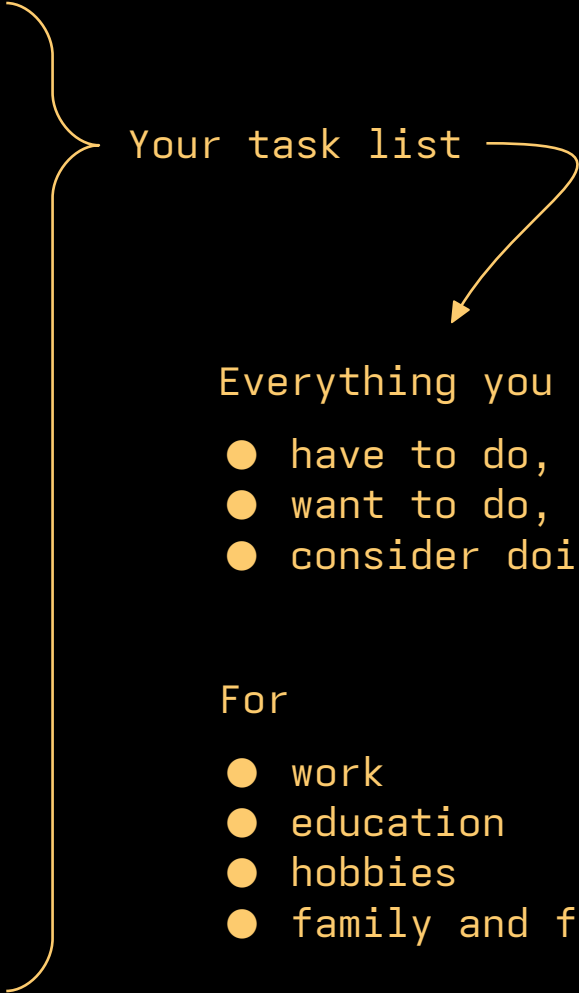

Everything you

- have to do, or
- want to do, or
- consider doing.

For

- work
- education
- hobbies
- family and friends

Prepare and send the X invoice to ABC.

Fix the random disconnections in the router.

↻ Water the plants – every 5 days

Record a video about procrastination.

Write the digital rights report for the UN.

↻ Check the server logs – every 2 weeks

Visit Liege to see its book market.

Add a plain text sitemap to all websites.

↻ Do laundry – every Sunday

Review Dilshod's screenplay.

Submit the ZIM packages to the Kiwix library.

⋮



Write
Clearly

Prepare and send the X invoice to ABC.

Fix the random disconnections in the router.

↻ Water the plants – every 5 days

Record a video about procrastination.

Write the digital rights report for the UN.

↻ Check the server logs – every 2 weeks

Visit Liege to see its book market.

Add a plain text sitemap to all websites.


↻ Do laundry – every Sunday

Review Dilshod's screenplay.

Submit the ZIM packages to the Kiwix library.

⋮

Prepare and send the X invoice to ABC.
Fix the random disconnections in the router.
↻ Water the plants – every 5 days
Record a video about procrastination.
Write the digital rights report for the UN.
↻ Check the server logs – every 2 weeks
Visit Liege to see its book market.
Add a plain text sitemap to all websites.
↻ Do laundry – every Sunday
Review Dilshod's screenplay.
Submit the ZIM packages to the Kiwix library.
⋮



Do first


Do later

Do much later

Do last

Prepare and send the X invoice to ABC.
Fix the random disconnections in the router.
🕒 Water the plants – every 5 days
Record a video about procrastination.
Write the digital rights report for the UN.
🕒 Check the server logs – every 2 weeks
Visit Liege to see its book market.
Add a plain text sitemap to all websites.
🕒 Do laundry – every Sunday
Review Dilshod's s
Submit the ZIM par library.
⋮

Buried tasks!



Do first

Do later

Do much later

Do last

Prepare and send the X invoice to ABC.

Fix the random disconnections in the router.

↻ Water the plants – every 5 days

Record a video about procrastination.

Write the digital rights policy for the UN.

↻ Check the server logs for errors.

Visit Liege to see its book market.

Add a plain text sitemap to all websites.

↻ Do laundry – every Sunday

Review Dilshod's script.

Submit the ZIM package to the library.

⋮

Lost
opportunities

Stress!

Buried tasks!

Option 1: prioritizing


Do first

Do later

Do much later

Do last

Prepare and send the X invoice to ABC.
Fix the random disconnections in the router.
🕒 Water the plants – every 5 days
Record a video about procrastination.
Write the digital rights report for the UN.
🕒 Check the server logs – every 2 weeks
Visit Liege to see its book market.
Add a plain text sitemap to all websites.
🕒 Do laundry – every Sunday
Review Dilshod's screenplay.
Submit the ZIM packages to the Kiwix library.
⋮

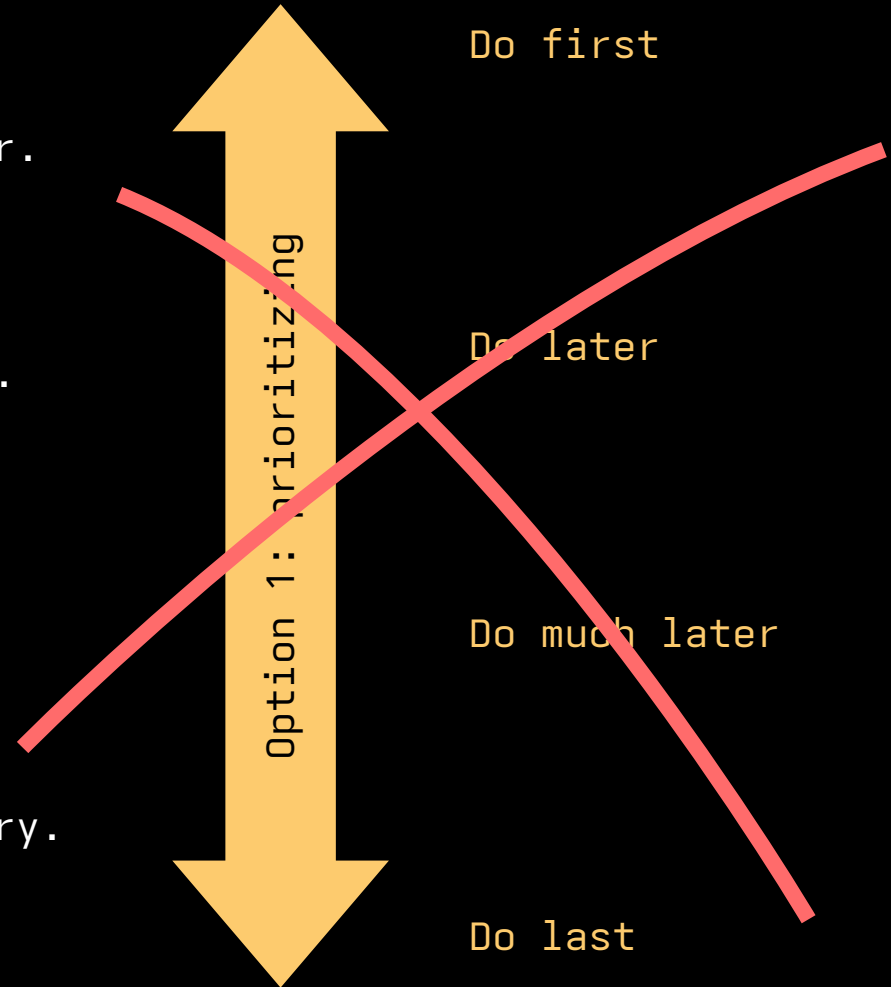

Doing

Prepare and send the X invoice to ABC.

Fix the random disconnections in the router.

↻ Water the plants – every 5 days

Record a video about procrastination.

Write the digital rights report for the UN.

↻ Check the server logs – every 2 weeks

Visit Liege to see its book market.

Add a plain text sitemap to all websites.

↻ Do laundry – every Sunday

Review Dilshod's screenplay.

Submit the ZIM packages to the Kiwix library.

⋮

Option 2:
Postponing

Doing

Prepare and send the X invoice to ABC.

Fix the random disconnections in the router.

↻ Water the plants – every 5 days

⋮

Option 2:
Postponing

Doing

Prepare and send the X invoice to ABC.

Fix the random disconnections in the router.

↻ Water the plants – every 5 days

⋮

Postponed

Option 2:
Postponing

Doing

Prepare and send the X invoice to ABC.

Fix the random disconnections in the router.

↻ Water the plants - every 5 days

⋮

postponing

```
graph LR; subgraph Doing; D1[Prepare and send the X invoice to ABC.]; D2[Fix the random disconnections in the router.]; D3[↻ Water the plants - every 5 days]; D4[⋮]; end; subgraph Postponed; P1[2026-05-14 -- Prepare and send the X invoi...]; end; D1 -- postponing --> P1;
```

The diagram illustrates the process of postponing a task. It features two main containers: 'Doing' at the top and 'Postponed' at the bottom. The 'Doing' container lists several tasks, including 'Prepare and send the X invoice to ABC.', 'Fix the random disconnections in the router.', '↻ Water the plants - every 5 days', and a vertical ellipsis. The 'Postponed' container shows a single task entry: '2026-05-14 -- Prepare and send the X invoi...'. A red arrow labeled 'postponing' originates from the first task in the 'Doing' list and points to the task in the 'Postponed' list.

Postponed

2026-05-14 -- Prepare and send the X invoi...

Doing

Prepare and send the X invoice to ABC.
Fix the random disconnections in the router.
↻ Water the plants - every 5 days
⋮

Postponed

2026-05-14 -- Prepare and send the X invoi...

postponing

To a realistic
Date, not always
“tomorrow”!

Doing

Fix the random disconnections in the router.

↻ Water the plants – every 5 days

Record a video about procrastination.

⋮

Postponed

2026-05-14 -- Prepare and send the X invo...

Doing

Fix the random disconnections in the router.

↻ Water the plants – every 5 days

Record a video about procrastination.

⋮

postponing

```
graph LR; subgraph Doing; D1[Fix the random disconnections in the router.]; D2[↻ Water the plants – every 5 days]; D3[Record a video about procrastination.]; D4[⋮]; end; subgraph Postponed; P1[2026-05-14 -- Prepare and send the X invoice.]; P2[2026-05-20 -- Fix the random disconnection...]; end; D1 -- postponing --> P2;
```

The diagram illustrates the concept of postponing tasks. It features two main containers: 'Doing' and 'Postponed'. The 'Doing' container lists tasks currently being performed, while the 'Postponed' container lists tasks that have been delayed. A red arrow labeled 'postponing' points from the first task in the 'Doing' list to the second task in the 'Postponed' list, indicating the transition of a task from being done to being postponed.

Postponed

2026-05-14 -- Prepare and send the X invoice...

2026-05-20 -- Fix the random disconnection...

Doing

🕒 Water the plants – every 5 days

Record a video about procrastination.

Write the digital rights report for the UN.

⋮

Postponed

2026-05-14 -- Prepare and send the X invoi...

2026-05-20 -- Fix the random disconnection...

Doing

Record a video about procrastination.
Review Dilshod's screenplay.
Submit the ZIM packages to the Kiwix library.

A number of items
You can realistically
do today

Postponed

2026-05-14 -- Prepare and send the X invoi...
2026-05-15 -- ↻ Water the plants - every ...
2026-05-20 -- Fix the random disconnection...
⋮

Doing

Record a video about procrastination.
Review Dilshod's screenplay.
Submit the ZIM packages to the Kiwix library.

We don't need to be
constantly distracted
by the future work.

Postponed

Doing

Record a video about procrastination.
Review Dilshod's screenplay.
Submit the ZIM packages to the Kiwix library.

Postponed

Finished

Canceled

4 types of
Status for tasks
in P1.express

```
graph LR; A[4 types of Status for tasks in P1.express] --- B[Doing]; A --- C[Postponed]; A --- D[Finished]; A --- E[Canceled]; B --- F[Record a video about procrastination.]; B --- G[Review Dilshod's screenplay.]; B --- H[Submit the ZIM packages to the Kiwix library.];
```



Doing

Record a video about procrastination.

Review Dilshod's screenplay.

Submit the ZIM packages to the Kiwix library.

Postponed

Finished

Canceled

Pen and
paper


Doing


Record a video about procrastination.
Review Dilshod's screenplay.
Submit the ZIM packages to the Kiwix library.

Postponed

Finished

Canceled

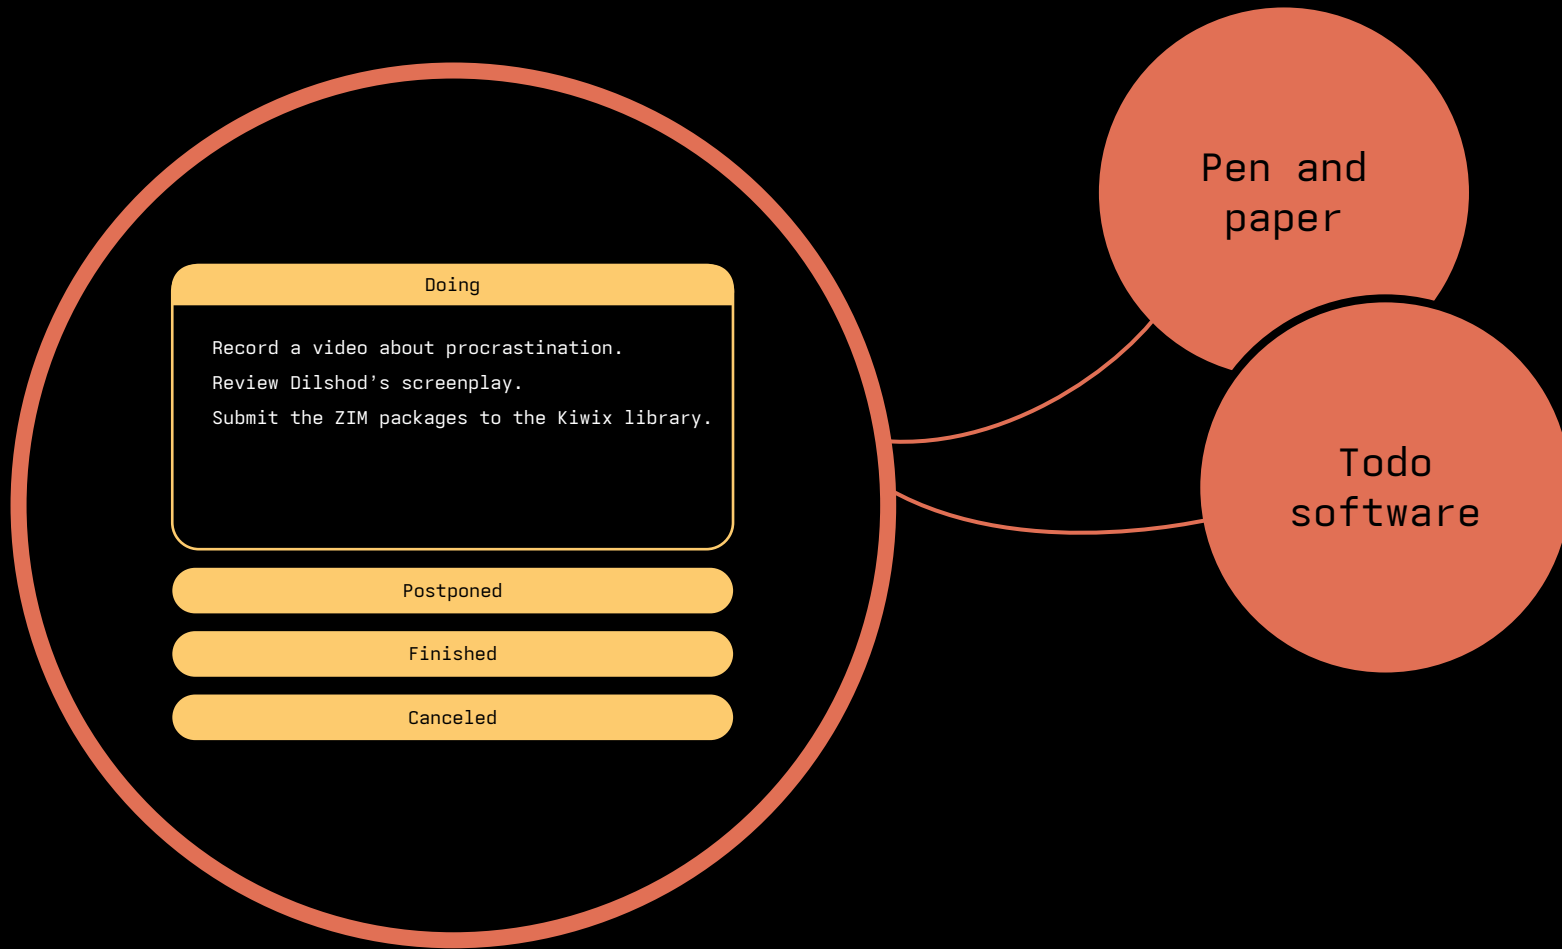

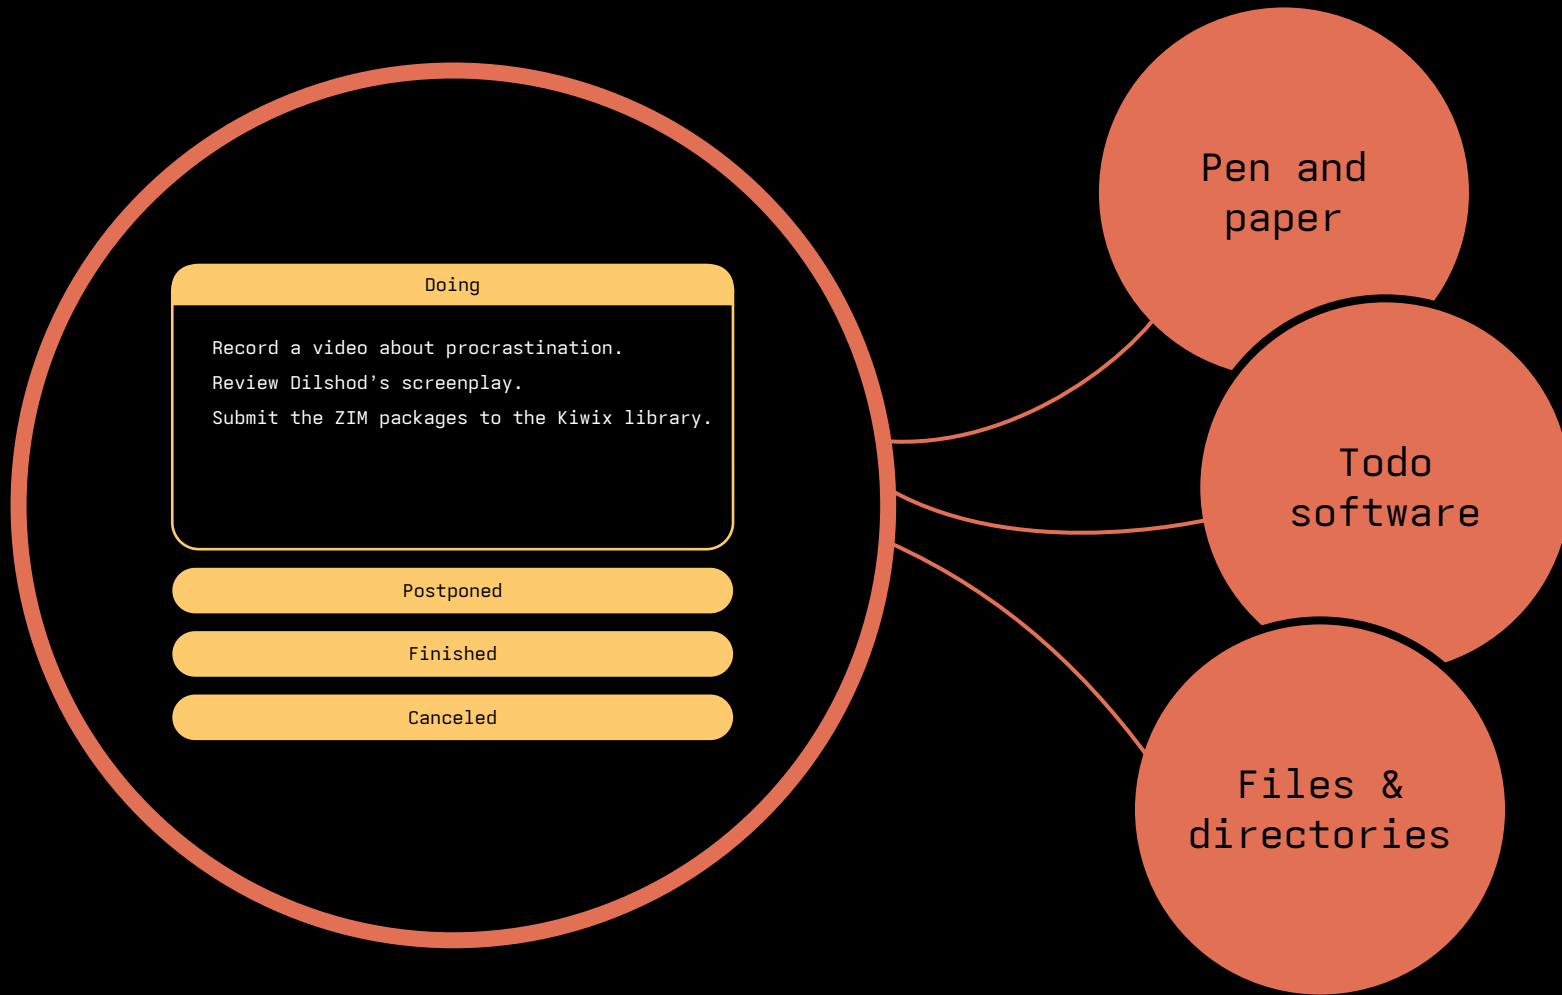

Doing

Record a video about pro...

Review Dilshod's screenp...

Submit the ZIM packages ...

Add a plain text sitemap...

🔄 Do laundry – every Su...

Postponed

Finished

Canceled

Doing

Record a video about pro...
Review Dilshod's screenp...
Submit the ZIM packages ...
Add a plain text sitemap...
↻ Do laundry – every Su...

Postponed

Finished

Canceled




Doing

Record a video about pro...
Review Dilshod's screenp...
Submit the ZIM packages ...
Add a plain text sitemap...
🔄 Do laundry – every Su...

Postponed

Finished

Canceled

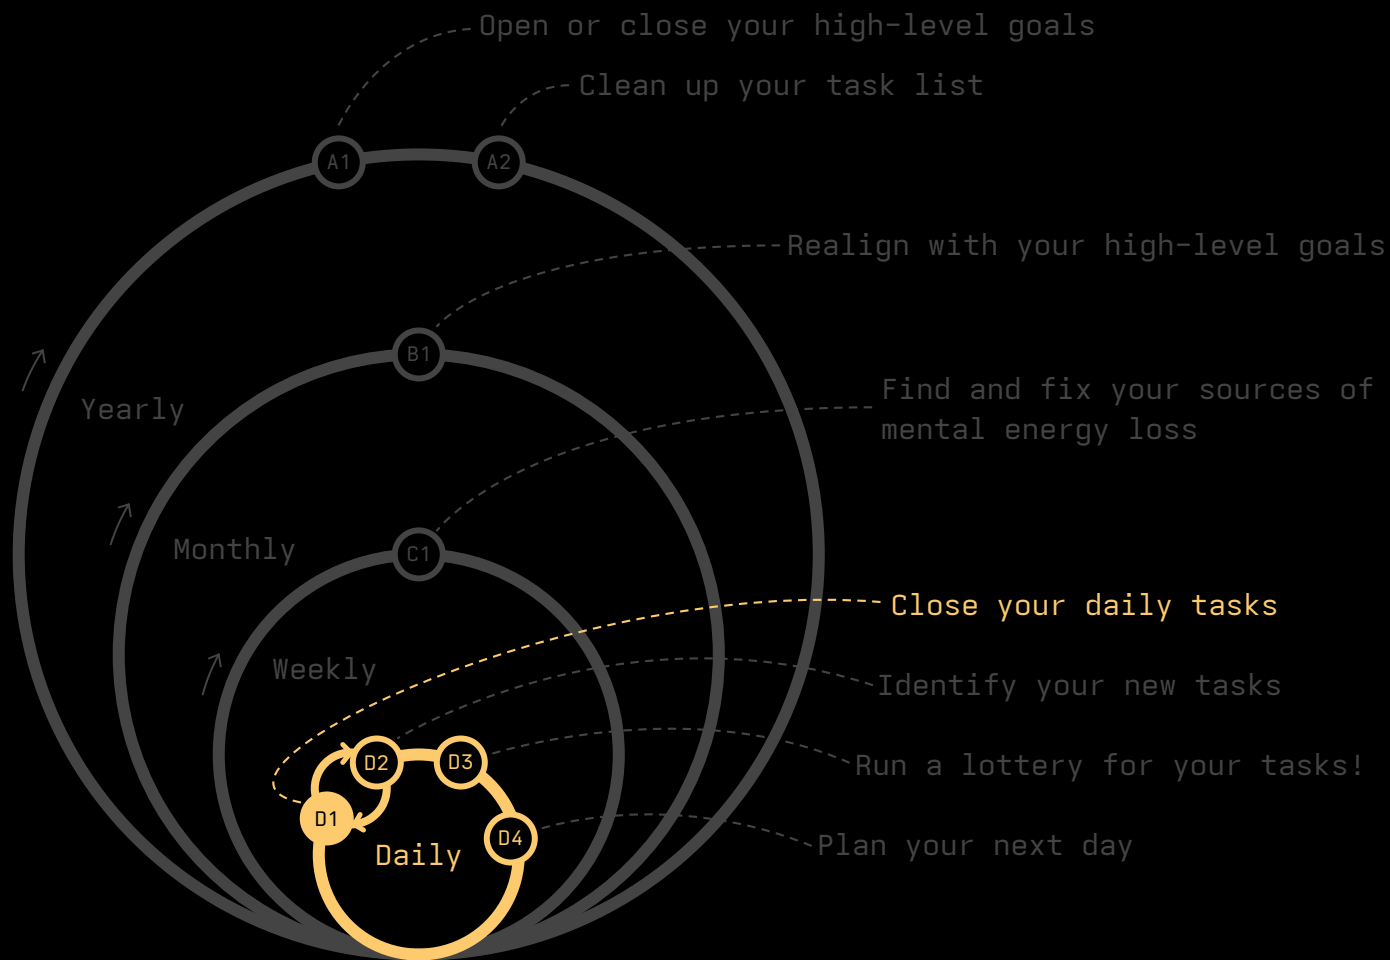


Doing

Record a video about pro...
Review Dilshod's screenp...
Submit the ZIM packages ...
Add a plain text sitemap...
🔄 Do laundry – every Su...

Postponed

Finished

Canceled

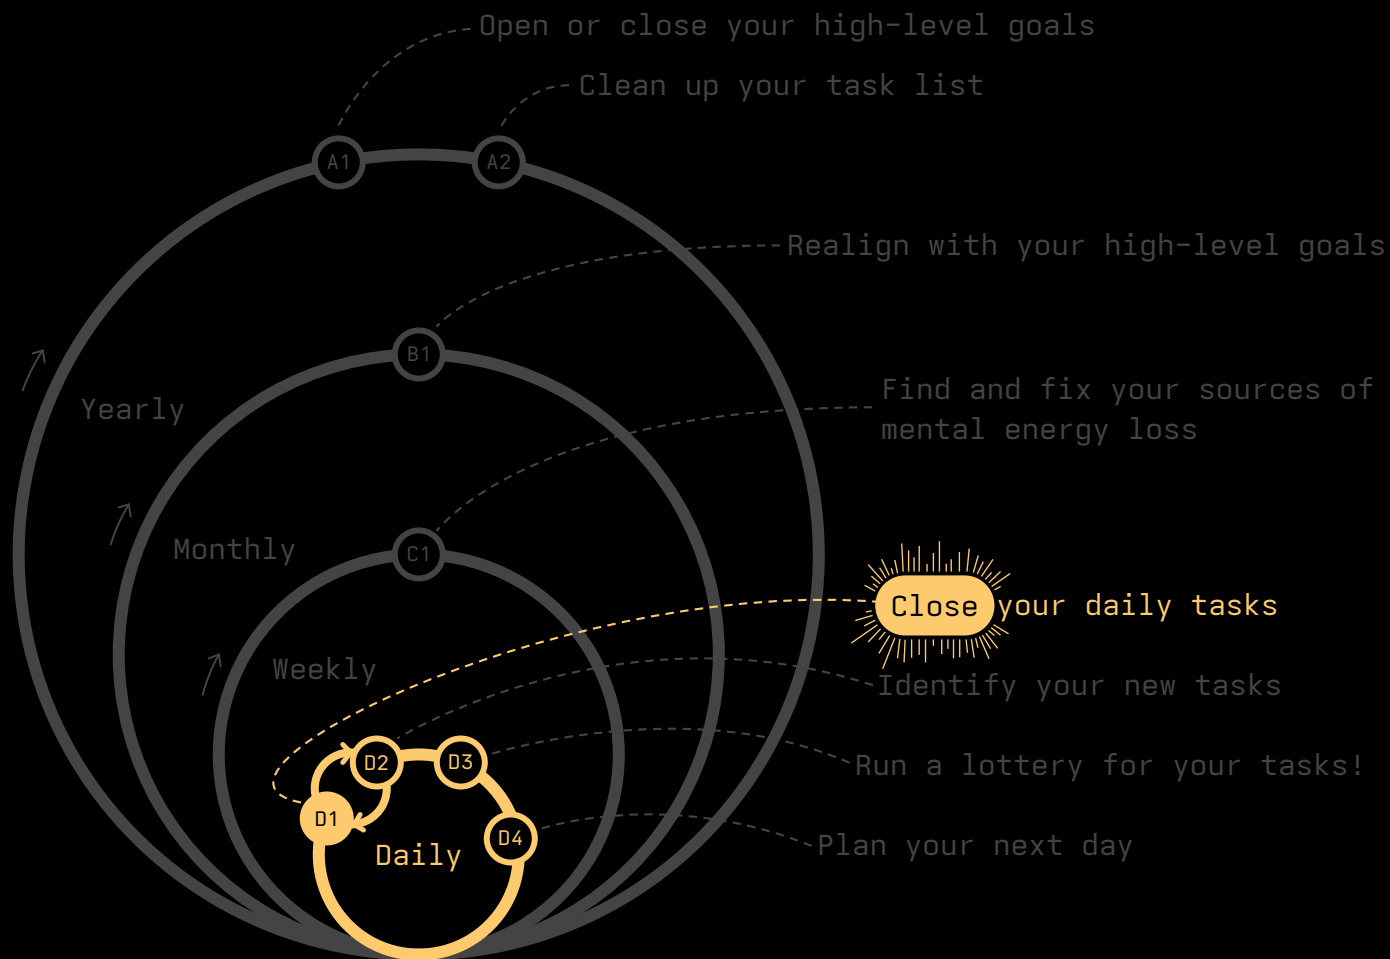


Doing

Record a video about pro...
Review Dilshod's screenp...
Submit the ZIM packages ...
Add a plain text sitemap...
🔄 Do laundry – every Su...

Postponed

Finished

Canceled

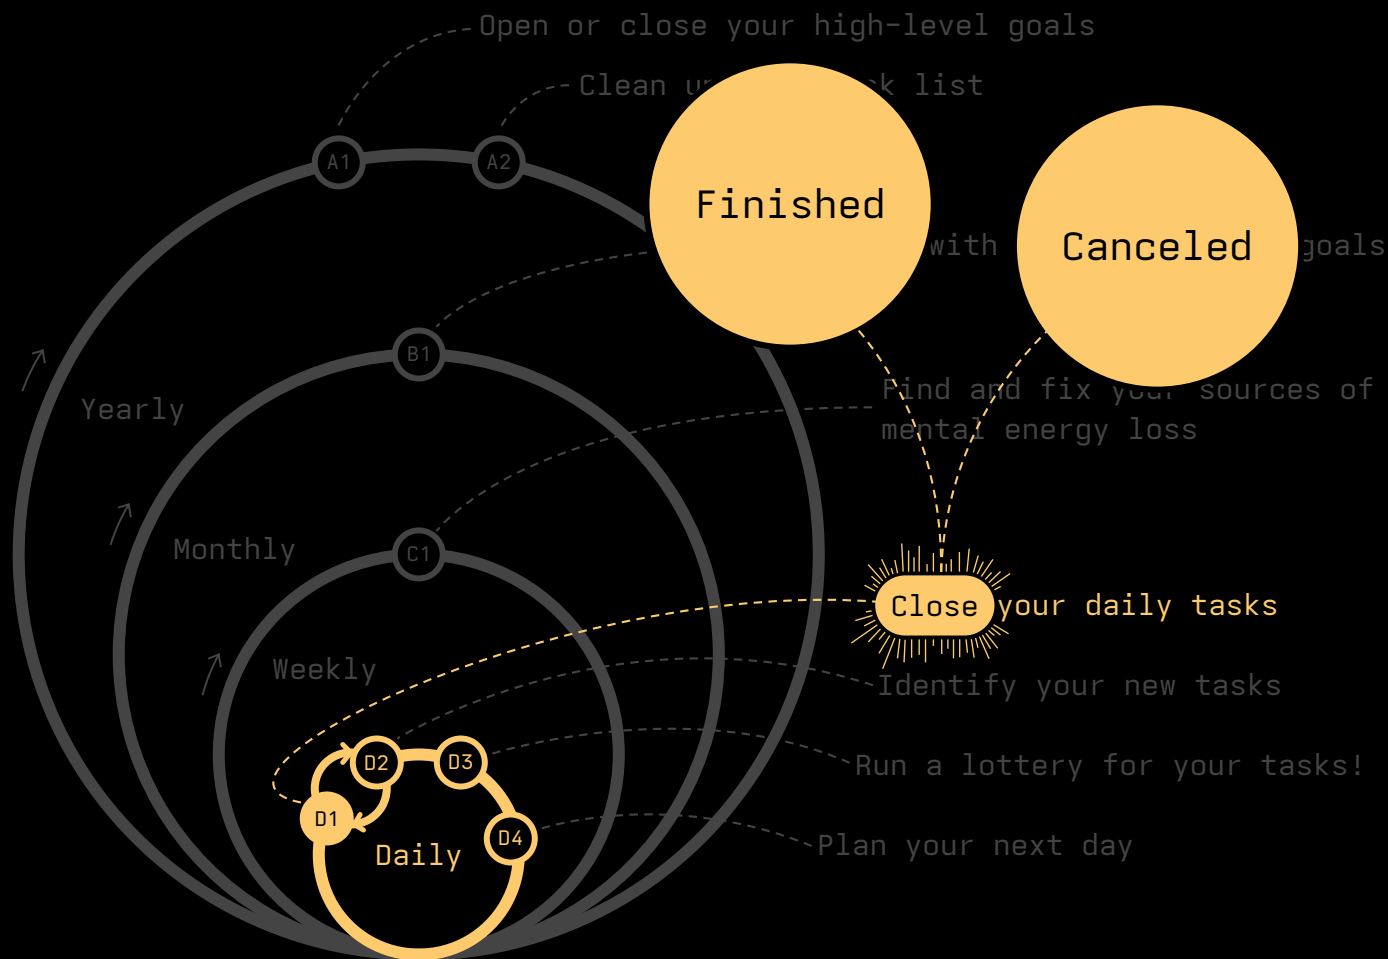

Doing


Record a video about pro...
Review Dilshod's screenp...
Add a plain text sitemap...
🔄 Do laundry - every Su...

Postponed

Finished

2026-05-12 -- Write the...
2026-05-13 -- Submit the...

Canceled

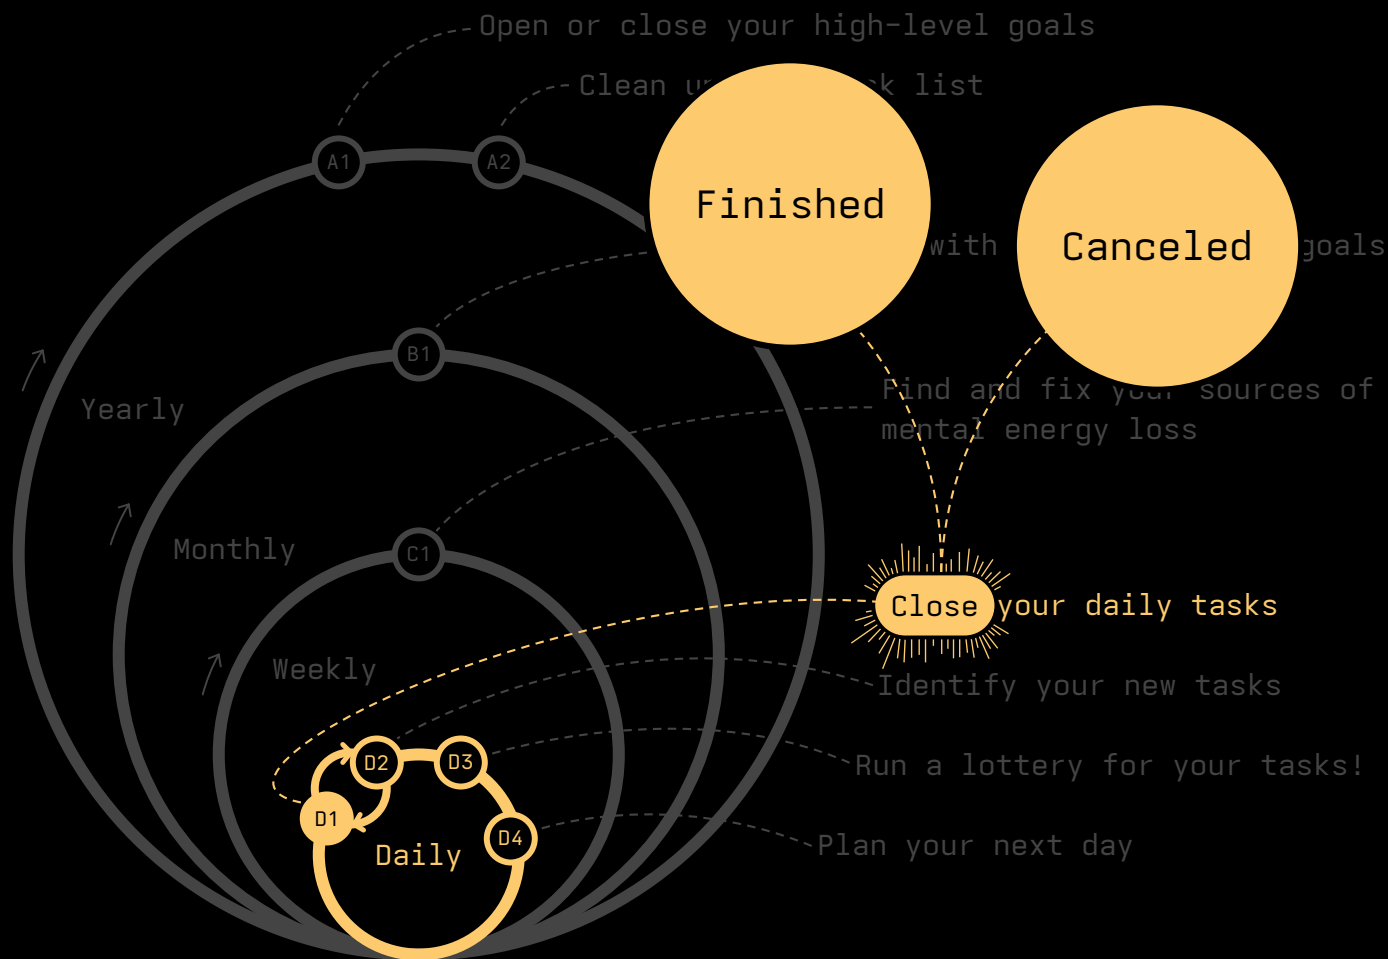

Doing

Record a video about pro...
Review Dilshod's screenp...
Add a plain text sitemap...
🔄 Do laundry - every Su...

Postponed

Finished

2026-05-12 -- Write the...
2026-05-13 -- Submit the...

Canceled

Submit the ZIM packages to the Kiwix library

Why? Increased awareness of people who might need these packages. Most of them install packages directly from that library.

Packages must comply with the standard to be accepted.

Address to submit:
<https://library.kiwix.org/>

Done!
They approved the packages immediately.

Doing

Record a video about pro...
Review Dilshod's screenp...
Add a plain text sitemap...
🔄 Do laundry - every Su...

Postponed

Finished

2026-05-12 -- Write the...
2026-05-13 -- Submit the...

Canceled

Submit the ZIM packages to the Kiwix library

Why? Increased awareness of people who might need these packages. Most of them install packages directly from that library.

Packages must comply with the standard to be accepted.

Address to submit:
<https://library.kiwix.org/>

Done!
They approved the packages immediately.

Write
clearly

Doing

Record a video about pro...

Review Dilshod's screenp...

Add a plain text sitemap...

🔄 Do laundry – every Su...

Postponed

Finished

2026-05-12 -- Write the...

2026-05-13 -- Submit the...

Canceled

🔄 Do laundry – every Sunday

- Wash towels separately, with 90° wash and without softener (reduces absorbability)
- For the rest, separate colored, black, and white clothes and use their separate washing liquids. Add softeners as well. Wash everything in 30° mode to be safe.
- Don't put shirts and other nice things in The dryer; they age faster that way. Just hang them after the wash.
- ?

Doing

Record a video about pro...

Review Dilshod's screenp...

Add a plain text sitemap...

🔄 Do laundry - every Su...

Postponed

Finished

2026-05-12 -- Write the...

2026-05-13 -- Submit the...

Canceled

🔄 Do laundry - every Sunday

- Wash towels separately, with 90° wash and without softener (reduces absorbability)
- For the rest, separate colored, black, and white clothes and use their separate washing liquids. Add softeners as well. Wash everything in 30° mode to be safe.
- Don't put shirts and other nice things in The dryer; they age faster that way. Just hang them after the wash.
- ?

Gradually
improve it

Doing


Record a video about pro...
Review Dilshod's screenp...
Add a plain text sitemap...
🔄 Do laundry - every Su...

Postponed

Finished

2026-05-12 -- Write the...
2026-05-13 -- Submit the...

Canceled

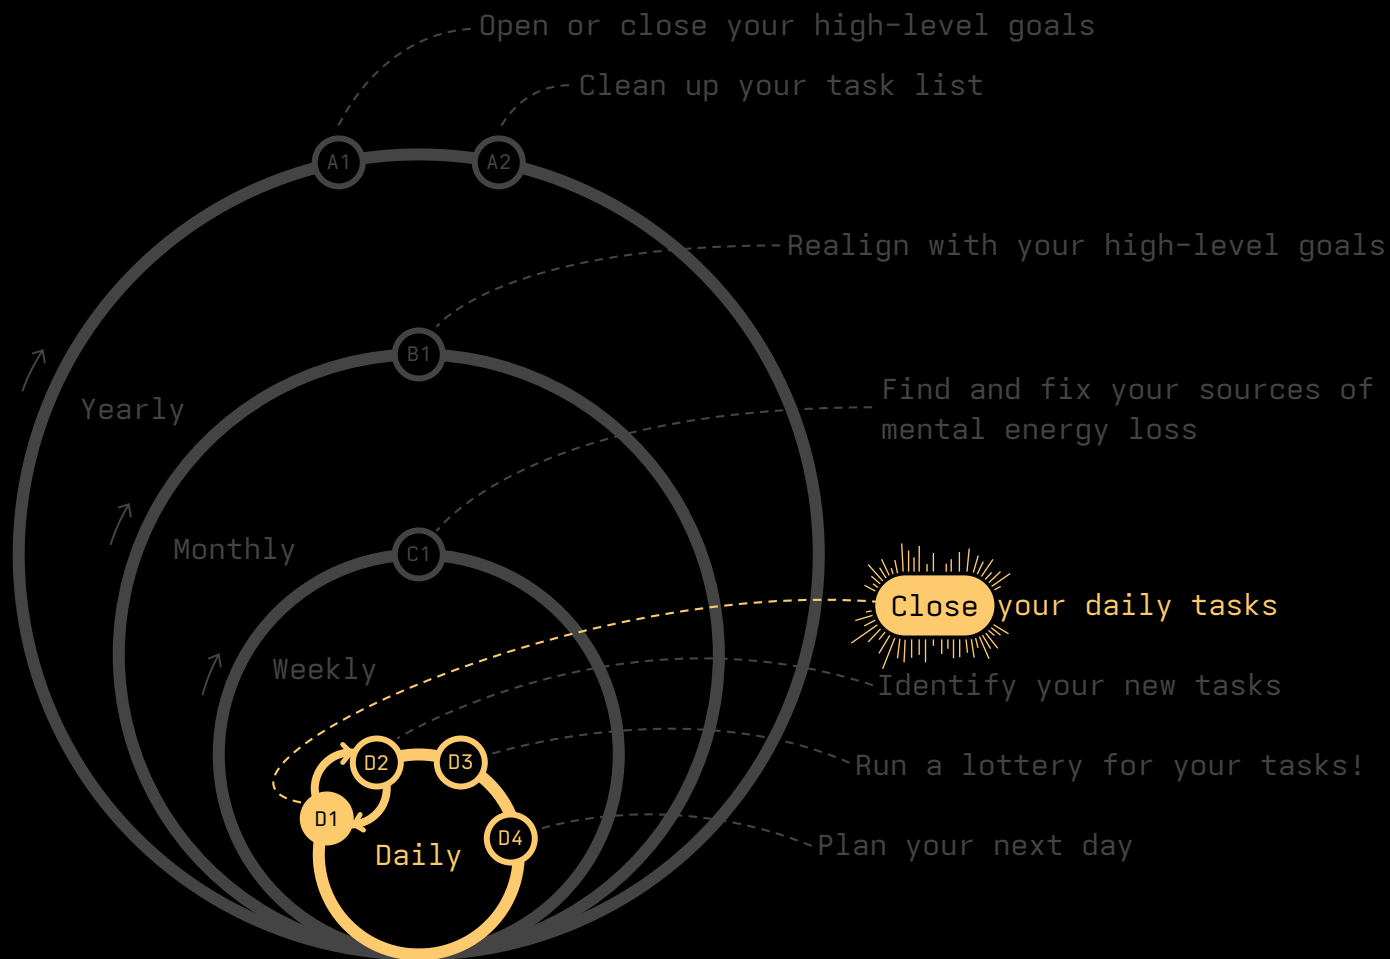

BREAKING NEWS WORLD IN CRISIS

17,635

TO DO:

- ☒ WORK
- ☒ EMAILS
- ☒ CALLS
- ☒ MEETING
- ☒ REPORT
- ☒ DEADLINE

MESSAGES
You have 99+ new messages

Everyone is doing more than you.

SYSTEM UPDATE
Restart Required

"THE ATTENTION ECONOMY
IS STEALING YOUR LIFE."

DISCONNECT
TO RECONNECT?

URGENT
Action Required

CALENDAR
Meeting
10:00 - 11:00 AM

CRYPTO ALERT
Bitcoin is up 15%!
Buy now?

YES

NO

TIME
IS RUNNING OUT.

3:47 AM

VERLOAD: INFORMATION OVERLOAD - WARNING: INFORMATION

Low Battery
10% battery remaining.
Low Power Mode
Close




REMINDER
Take a break?
Snooze Ignore

Screen Time
Daily Average
9h 17m



Most Used



Trending Now

- #1 World War 3
2.3M posts
 - #2 Economic Collapse
1.1M posts
 - #3 AI Takeover
900K posts
- Show more

LIKE
SHARE
SUBSCRIBE
COMMENT
REPEAT

be
productive!

YOU HAVE BEEN
SELECTED!
CLAIM YOUR REWARD



CLICK HERE

ERROR 404
ATTENTION
NOT FOUND

New Video!
You won't believe this!

NEWS
New headlines you need to see.
Slide to view

INBOX (23,167)
You have 23,167 unread emails.

IMPORTANT!
CALL BACK
EMAIL FOLLOW UP
SEND REPORT
CHECK FILES

LIMITED TIME!
50% OFF
SHOP NOW!

Storage Almost Full
You can manage your storage in Settings.

Not Now

Settings

DON'T
MISS OUT!

TOO
MUCH
NOISE

1,293


Doing

Record a video about pro...
Review Dilshod's screenp...
Add a plain text sitemap...
🔄 Do laundry - every Su...

Postponed

Finished

Canceled

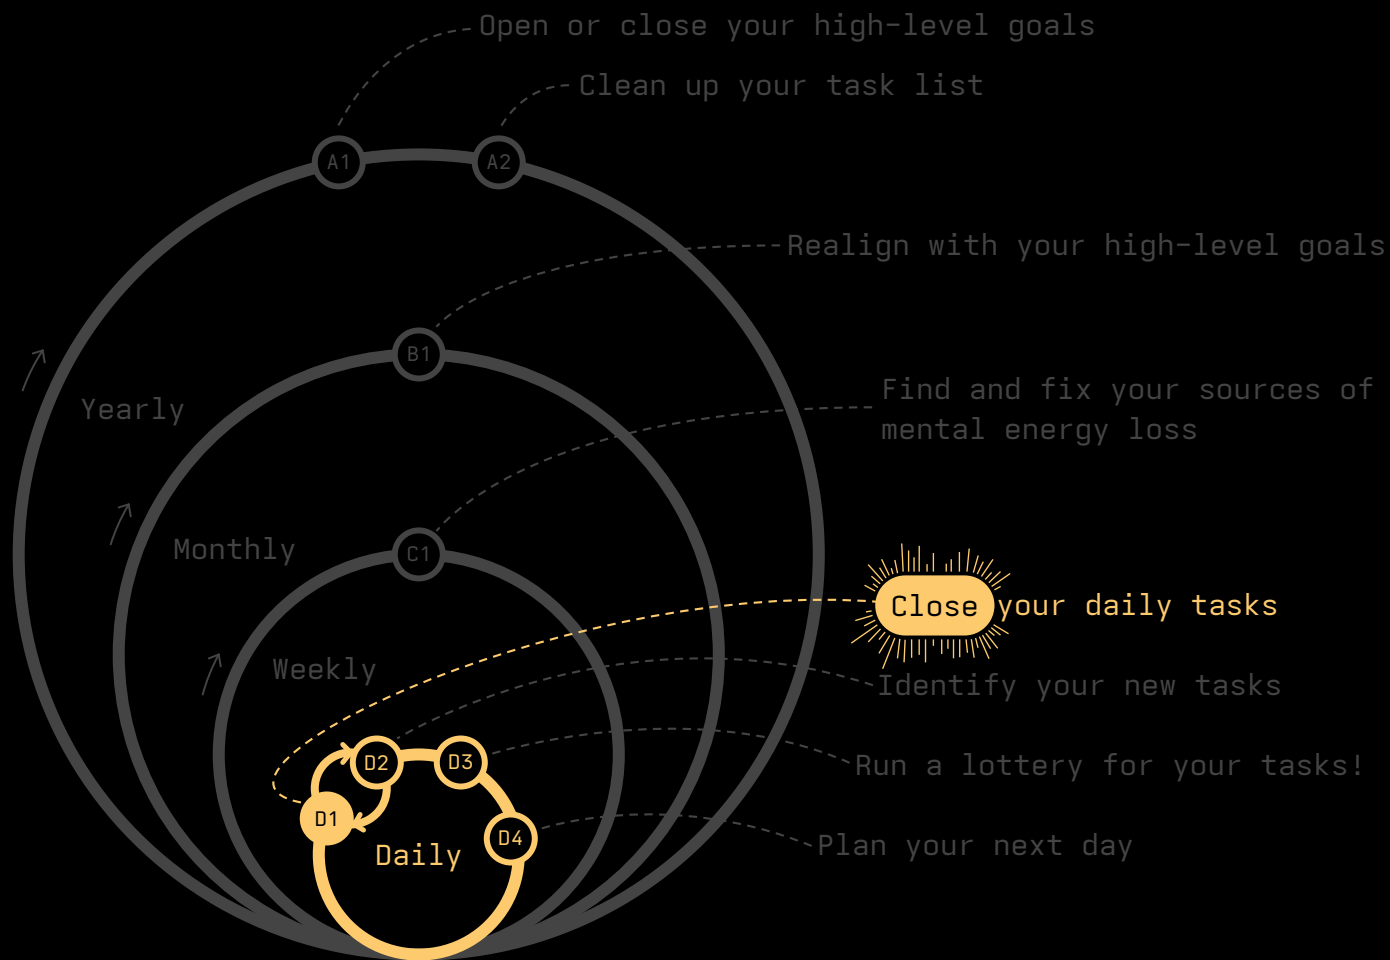

Doing

Record a video about pro...
Review Dilshod's screenp...
Add a plain text sitemap...
🔄 Do laundry - every Su...


Hardest
first?

Simplest
first?

Postponed

Finished

Canceled

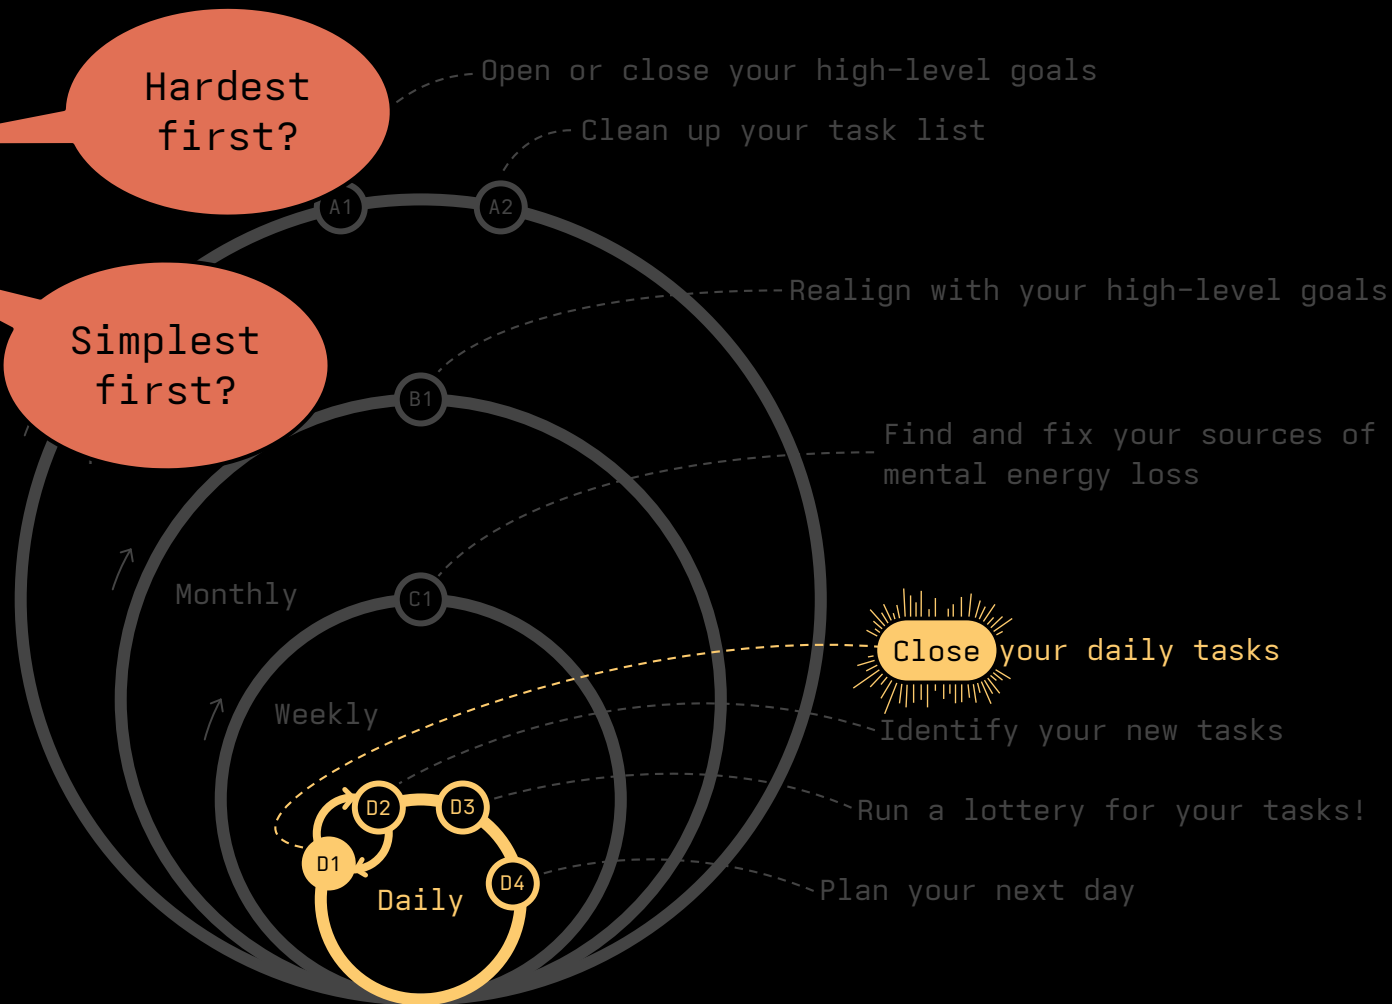

Doing

Record a video about pro...
Review Dilshod's screenp...
Add a plain text sitemap...
🔄 Do laundry - every Su...

Postponed

Finished

Canceled



Doing

Record a video about pro...
Review Dilshod's screenp...
Add a plain text sitemap...
🔄 Do laundry - every Su...

Postponed

Finished

Canceled




Doing

Record a video about pro...
Review Dilshod's screenp...
Add a plain text sitemap...
🔄 Do laundry - every Su...

Postponed

Finished

Canceled

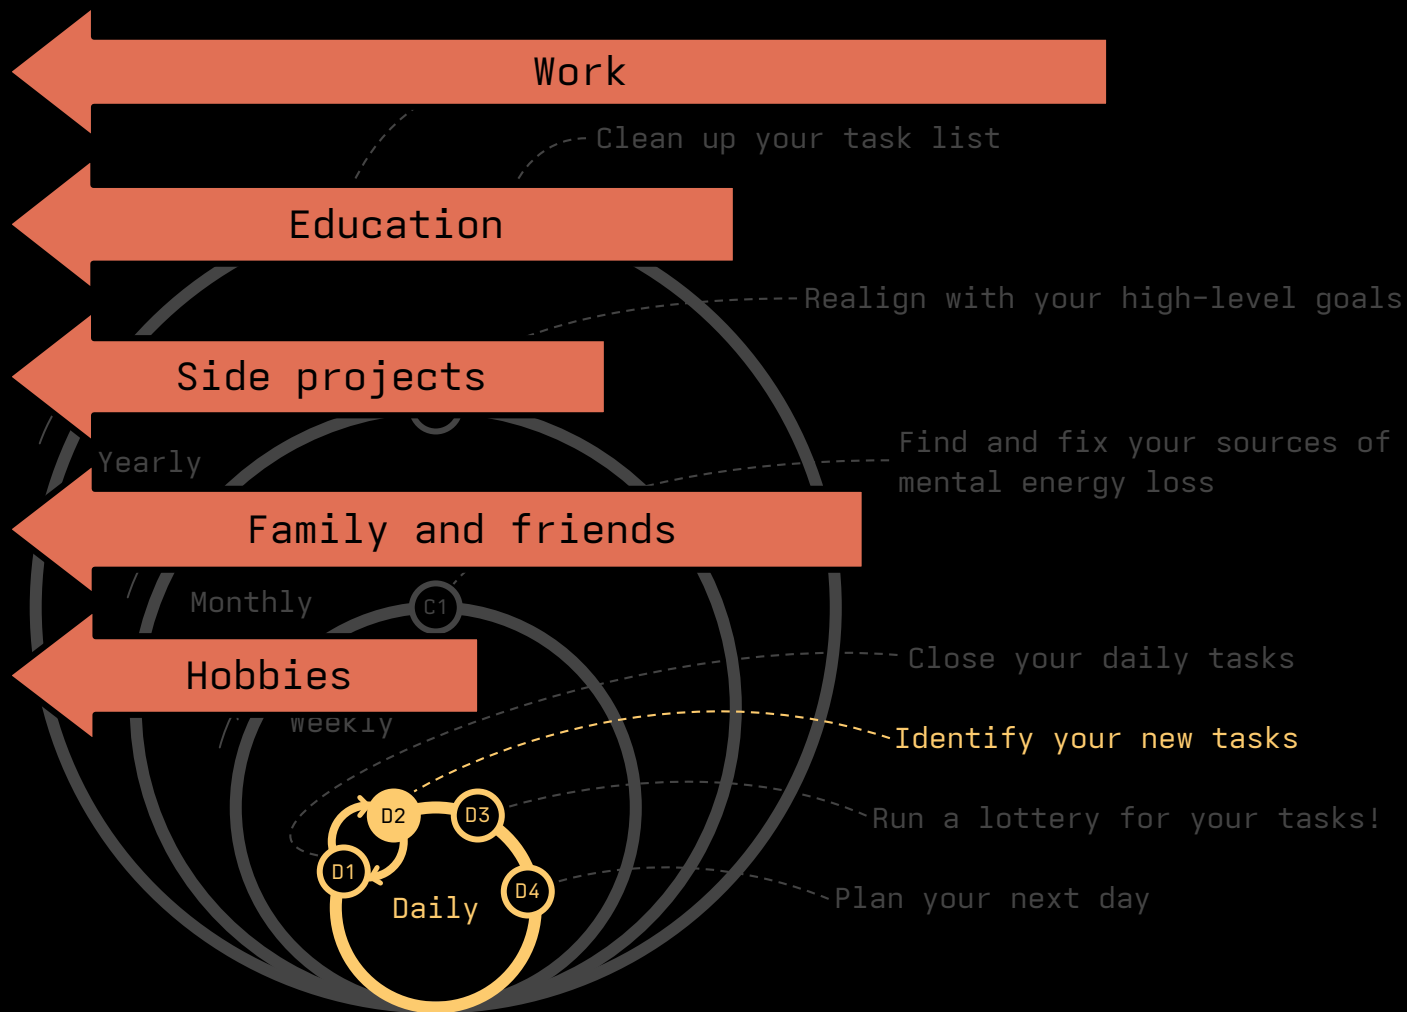

Doing

Record a video about pro...
Review Dilshod's screenp...
Add a plain text sitemap...
🔄 Do laundry - every Su...

Postponed

Finished

Canceled



Doing


Record a video about pro...
Review Dilshod's screenp...
Add a plain text sitemap...
🔄 Do laundry - every Su...

Postponed

Finished

Canceled

Clean the CPU fan

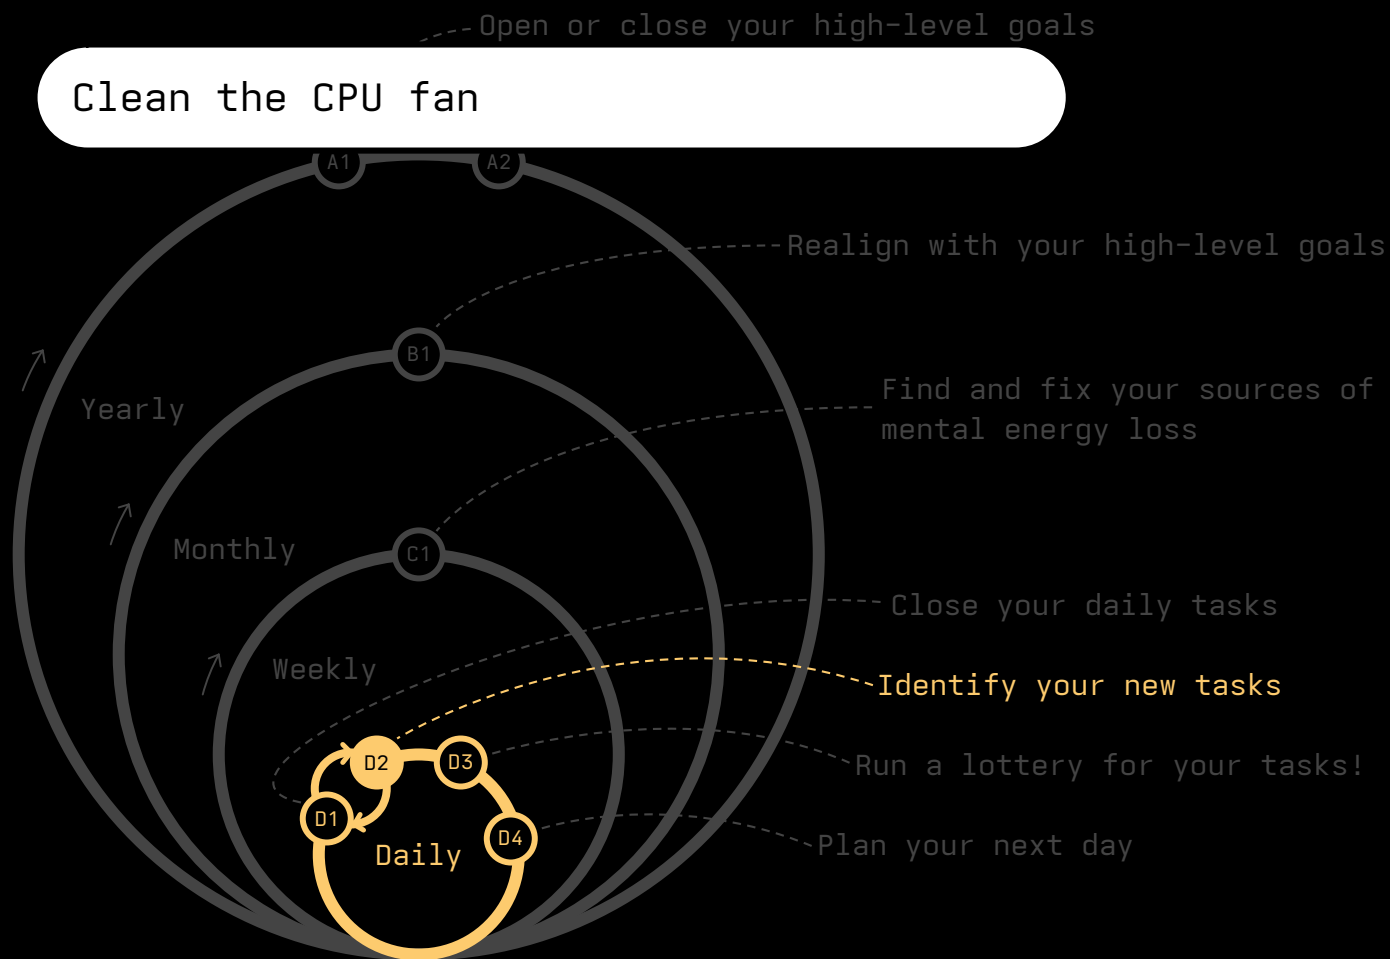

Doing

Record a video about pro...
Review Dilshod's screenp...
Add a plain text sitemap...
🔄 Do laundry - every Su...


Postponed

Finished

Canceled

Clean the CPU fan

🔄 Clean the CPU fan — every 6 months

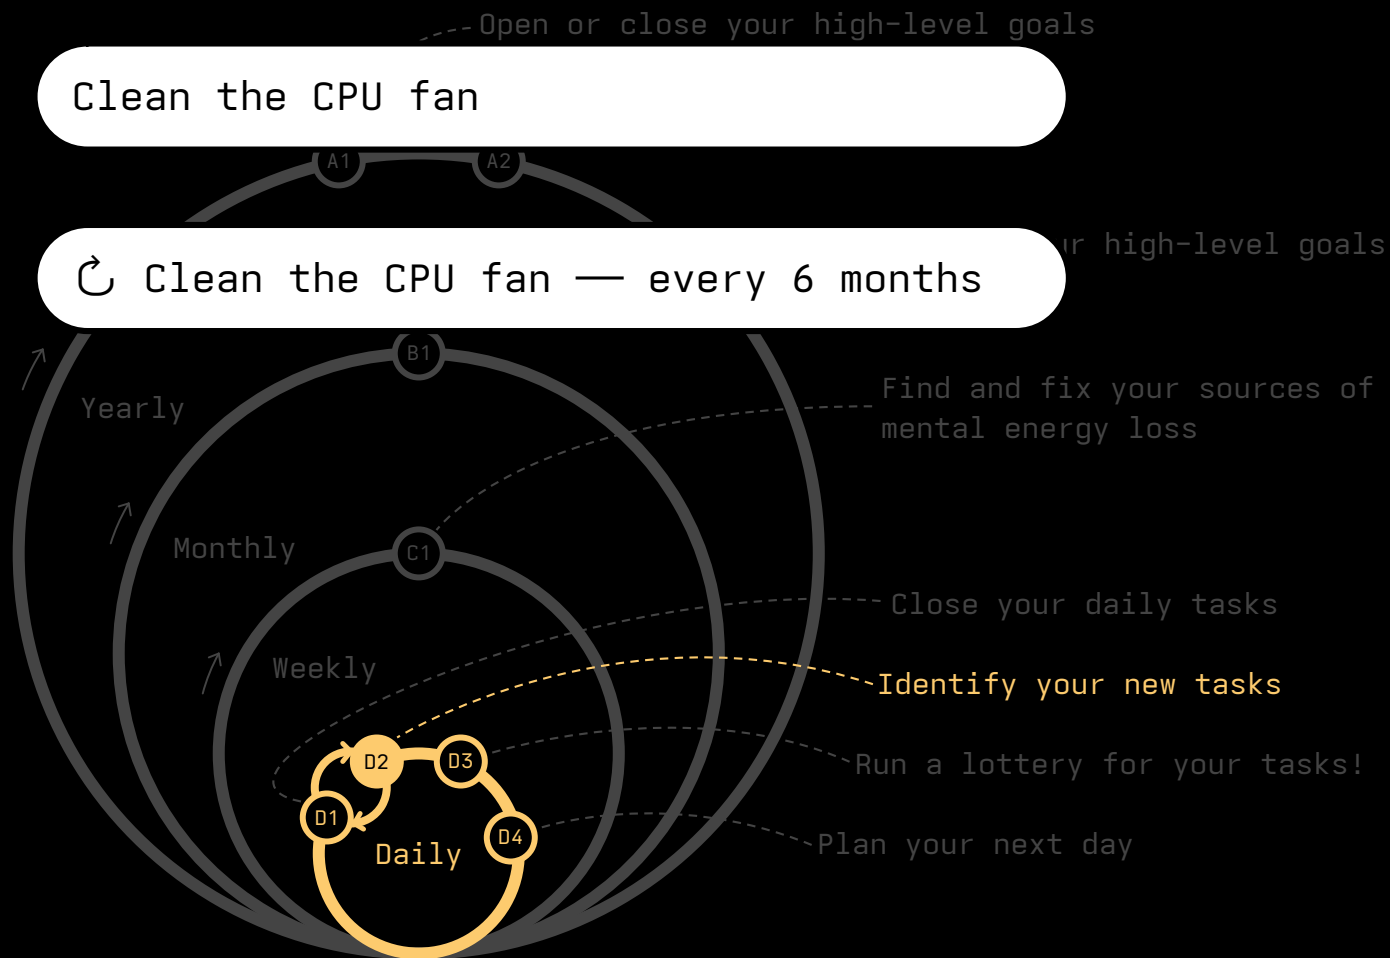

Doing

Record a video about pro...
Review Dilshod's screenp...
Add a plain text sitemap...
↻ Do laundry - every Su...


Postponed

Finished

Canceled

Clean the CPU fan

↻ Clean the CPU fan — every 6 months

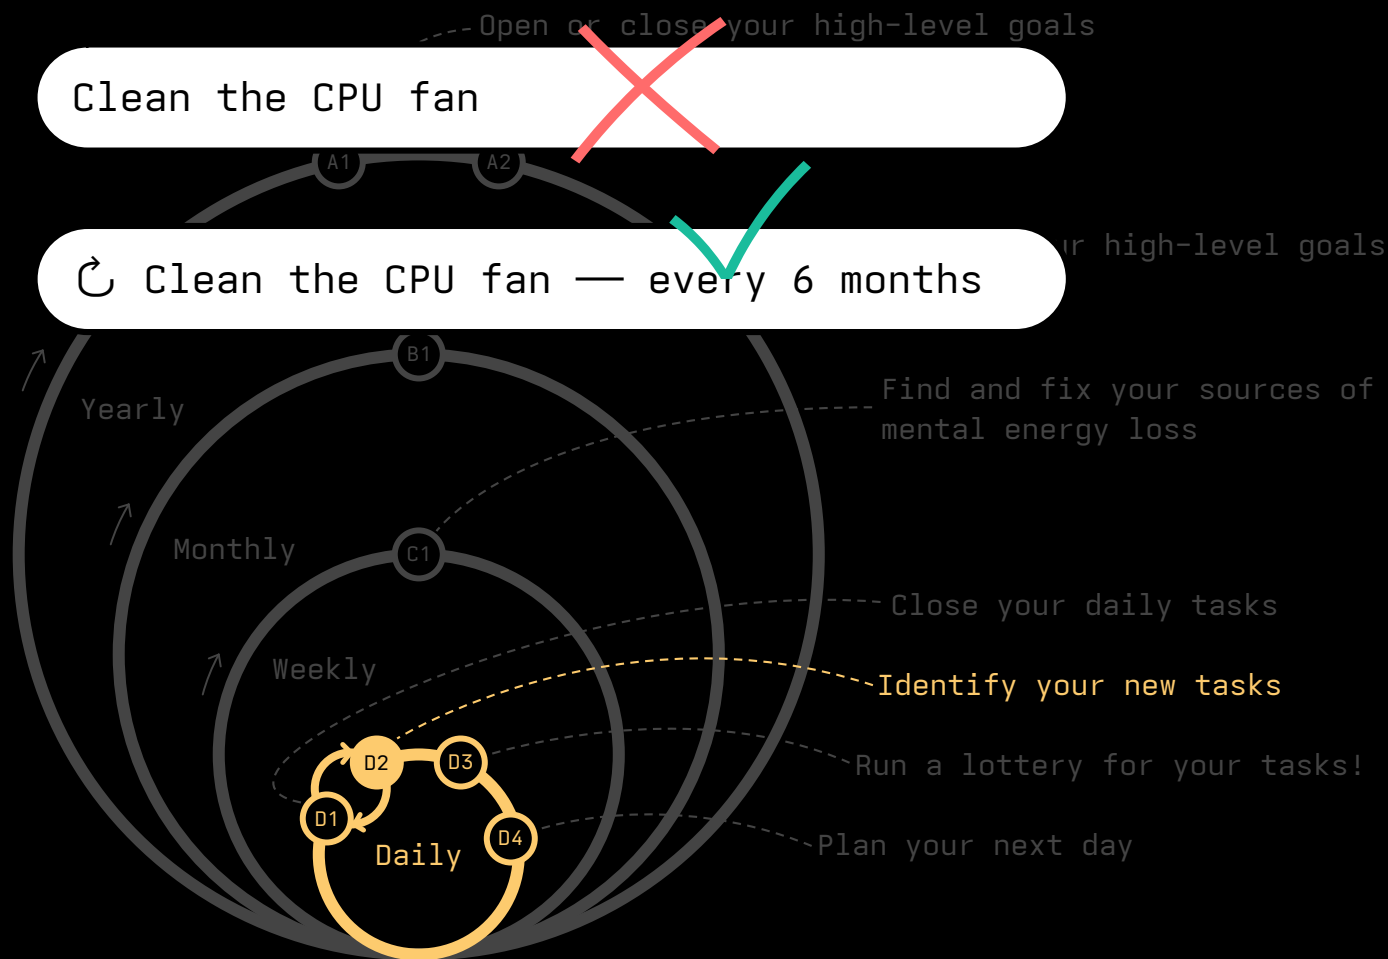


Doing

Record a video about pro...
Review Dilshod's screenp...
Add a plain text sitemap...
🔄 Do laundry - every Su...

Postponed

Finished

Canceled

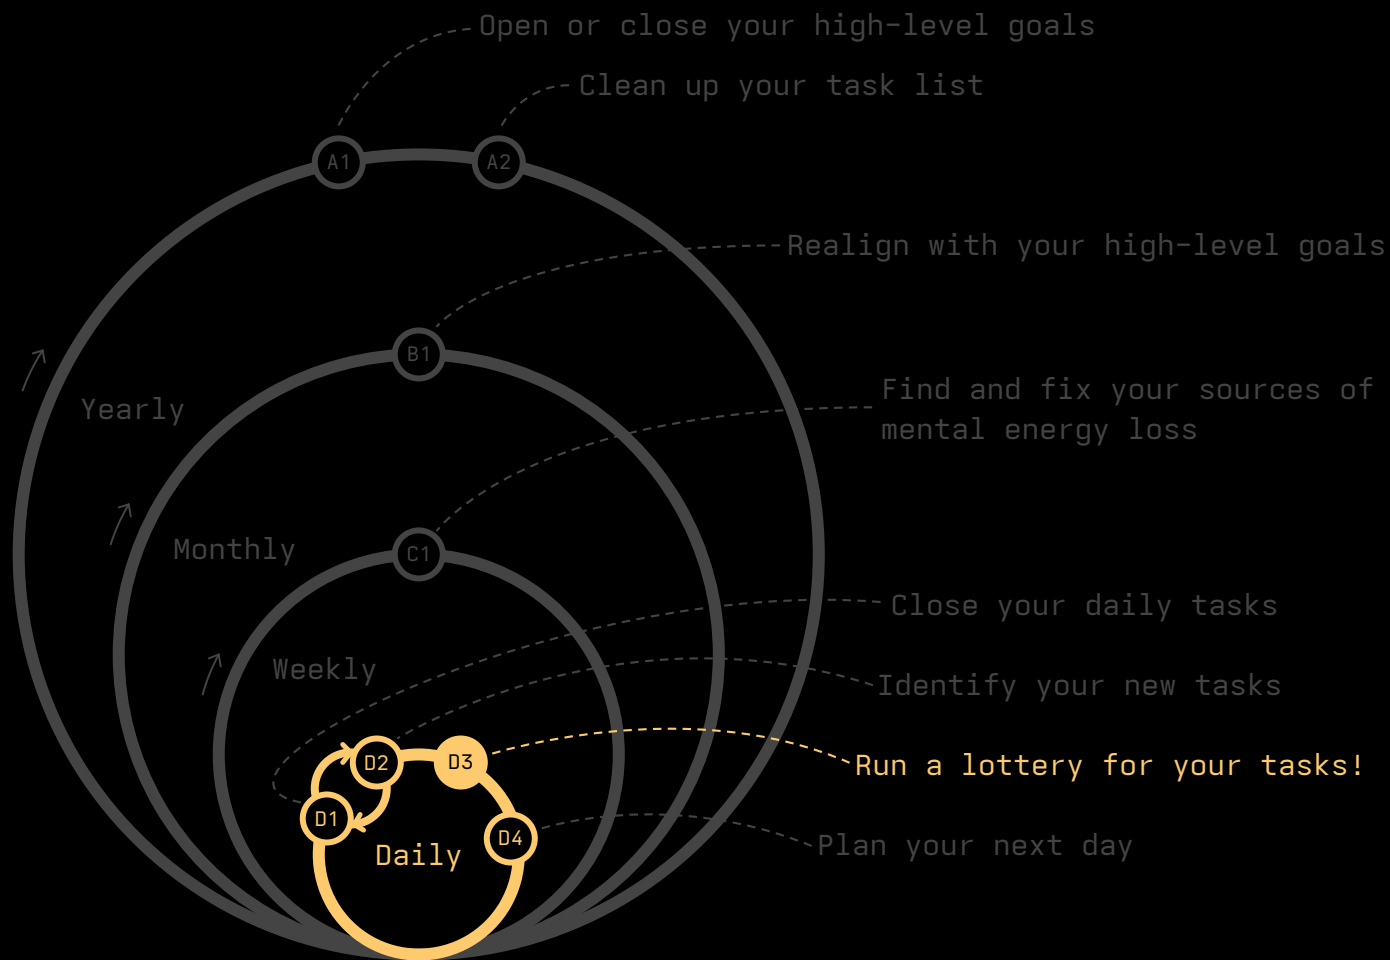

Doing

Postponed

2026-05-14 -- Prepare an...
2026-05-14 -- ↻ Water t...
2026-05-15 -- Match max ...
2026-05-16 -- Find all t...
2026-05-16 -- ↻ Check i...
2026-05-17 -- Buy a port...
2026-05-18 -- Install la...
2026-05-18 -- Write a re...
2026-05-18 -- Review Kam...
2026-05-19 -- Consider a...
2026-05-20 -- Fix the ra...
2026-05-20 -- Write an a...
2026-05-21 -- ↻ Wash th...
⋮

Finished

Canceled




Doing

Postponed

2026-05-14 -- Prepare an...
2026-05-14 -- ↻ Water t...
2026-05-15 -- Match max ...
2026-05-16 -- Find all t...
2026-05-16 -- ↻ Check i...
2026-05-17 -- Buy a port...
2026-05-18 -- Install la...
2026-05-18 -- Write a re...
2026-05-18 -- Review Kam...
2026-05-19 -- Consider a...
2026-05-20 -- Fix the ra...
2026-05-20 -- Write an a...
2026-05-21 -- ↻ Wash th...
⋮

Finished

Canceled

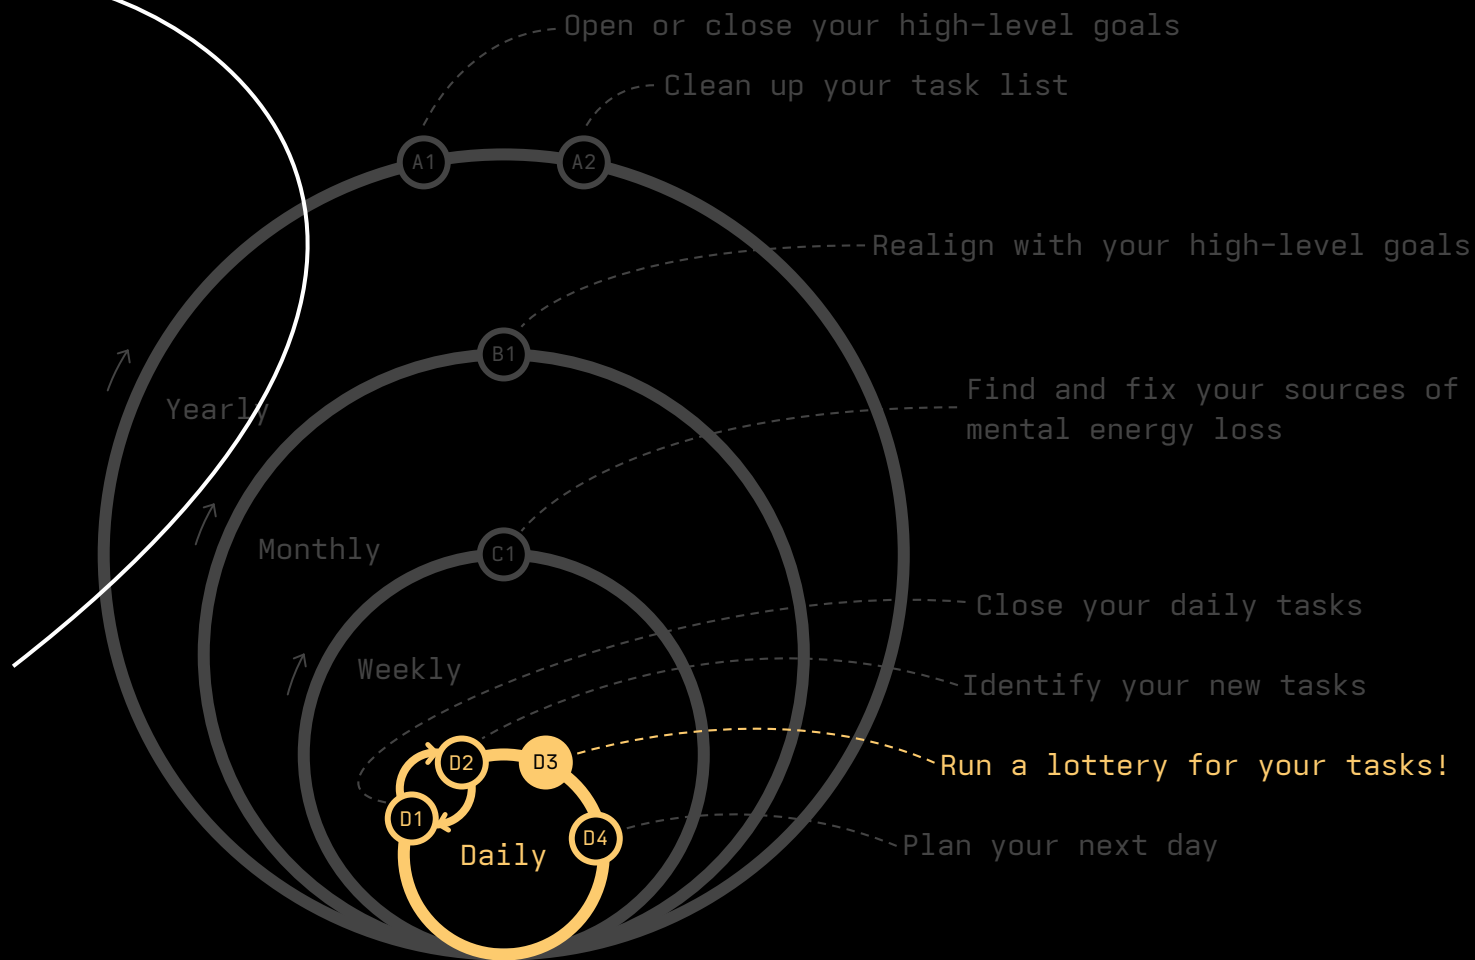

Doing

Postponed

2026-05-14 -- Prepare an...
2026-05-14 -- 🔄 Water t...
2026-05-15 -- Match max ...
2026-05-16 -- Find all t...
2026-05-16 -- 🔄 Check i...
2026-05-17 -- Buy a port...
2026-05-18 -- Install la...
2026-05-18 -- Write a re...
2026-05-18 -- Review Kam...
2026-05-19 -- Consider a...
2026-05-20 -- Fix the ra...
2026-05-20 -- Write an a...
2026-05-21 -- 🔄 Wash th...
⋮

Finished

Canceled



Doing

Postponed

2026-05-14 -- Prepare an...
2026-05-14 -- ↻ Water t...
2026-05-15 -- Match max ...
2026-05-16 -- Find all t...
2026-05-16 -- ↻ Check i...
2026-05-17 -- Buy a port...
2026-05-18 -- Install la...
2026-05-18 -- Write a re...
2026-05-18 -- Review Kam...
2026-05-19 -- Consider a...
2026-05-20 -- Fix the ra...
2026-05-20 -- Write an a...
2026-05-21 -- ↻ Wash th...
⋮

Finished

Canceled



Doing

Postponed

2026-05-14 -- Prepare an...
2026-05-14 -- ↻ Water t...
2026-05-15 -- Match max ...
2026-05-16 -- Find all t...
2026-05-16 -- ↻ Check i...
2026-05-17 -- Buy a port...
2026-05-18 -- Install la...
2026-05-18 -- Write a re...
2026-05-18 -- Review Kam...
2026-05-19 -- Consider a...
2026-05-20 -- Fix the ra...
2026-05-20 -- Write an a...
2026-05-21 -- ↻ Wash th...
⋮

Finished

Canceled



Doing


Record a video about pro...
Review Dilshod's screenp...
Add a plain text sitemap...
🔄 Do laundry - every Su...

Postponed

2026-05-14 -- Prepare an...
2026-05-14 -- 🔄 Water t...
2026-05-15 -- Match max ...
2026-05-16 -- Find all t...
2026-05-16 -- 🔄 Check i...
2026-05-17 -- Buy a port...
⋮

Finished

Canceled

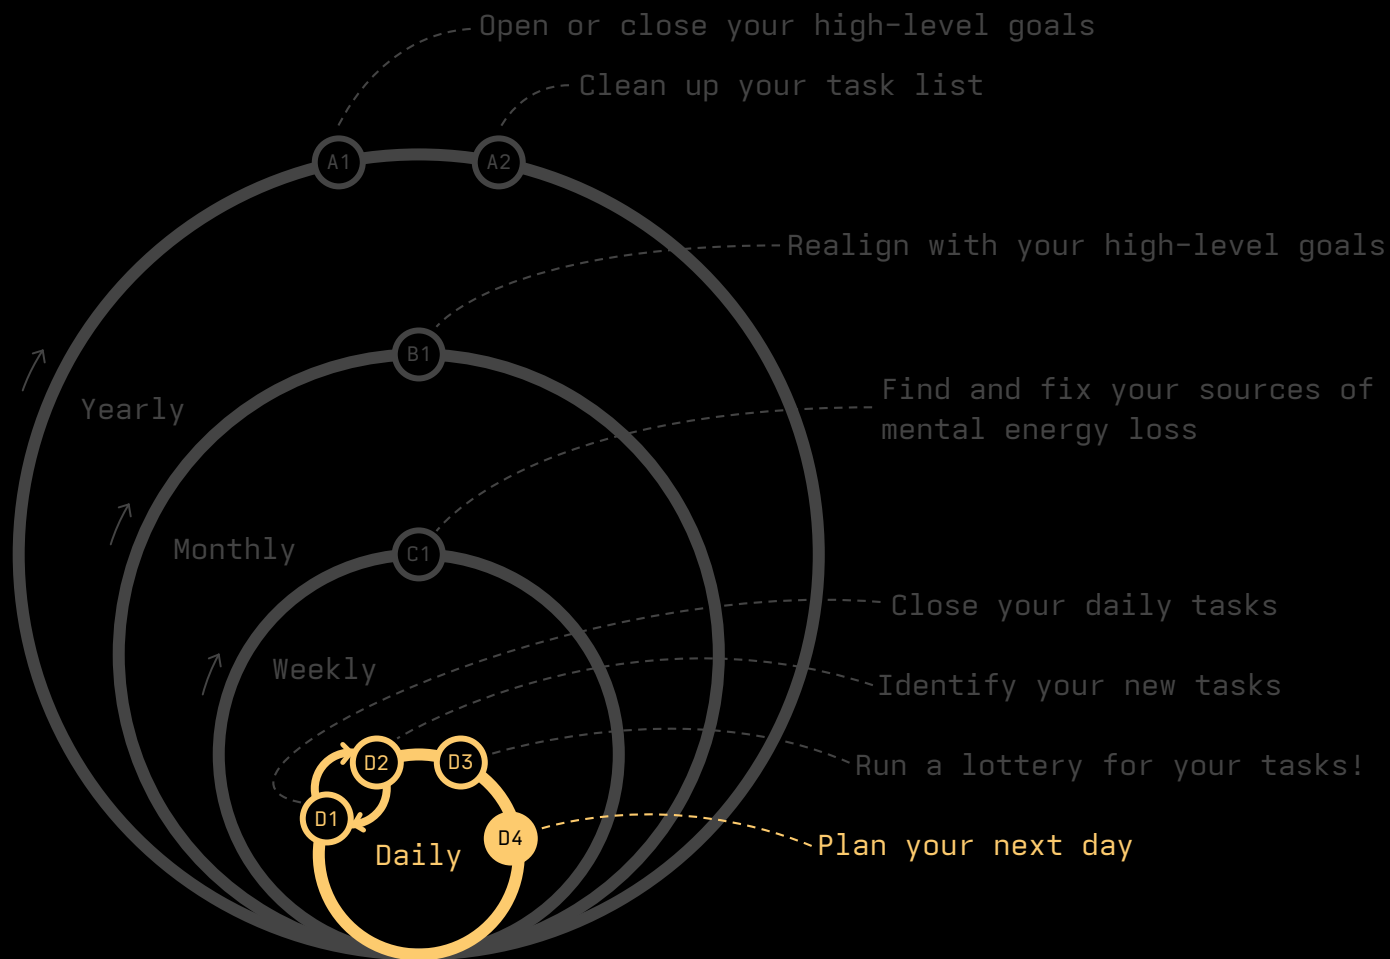

Doing

- Record a video about pro...
- Review Dilshod's screenp...
- Add a plain text sitemap...
- ☞ Do laundry – every Su...

Doing

- Record a video about pro...
- Review Dilshod's screenp...
- Add a plain text sitemap...
- ☞ Do laundry – every Su...

Postponed


```
2026-05-14 -- Prepare an...
2026-05-14 -- ↻ Water t...
2026-05-15 -- Match max ...
2026-05-16 -- Find all t...
2026-05-16 -- ↻ Check i...
2026-05-17 -- Buy a port...
⋮
```

Postponed

```
2026-05-14 -- Prepare an...
2026-05-14 -- ↻ Water t...
2026-05-15 -- Match max ...
2026-05-16 -- Find all t...
2026-05-16 -- ↻ Check i...
2026-05-17 -- Buy a port...
⋮
```

Finished

Canceled

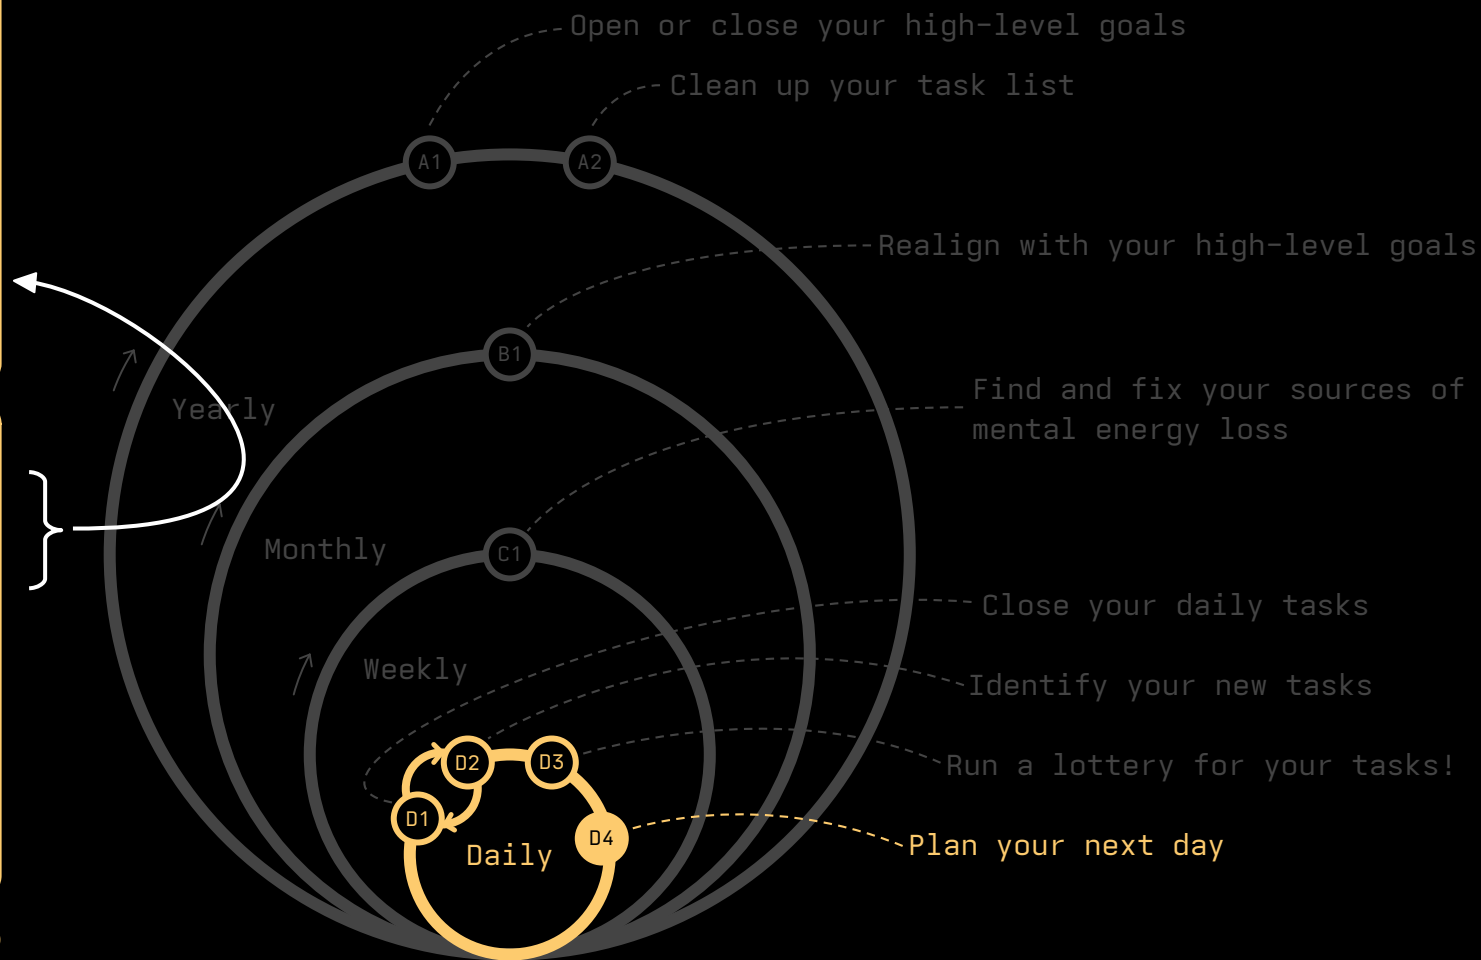

Doing


Record a video about pro...
Review Dilshod's screenp...
Add a plain text sitemap...
🔄 Do laundry – every Su...
Prepare an emergency eva...
🔄 Water the plants

Postponed

2026-05-15 -- Match max ...
2026-05-16 -- Find all t...
2026-05-16 -- 🔄 Check i...
2026-05-17 -- Buy a port...
⋮

Finished

Canceled

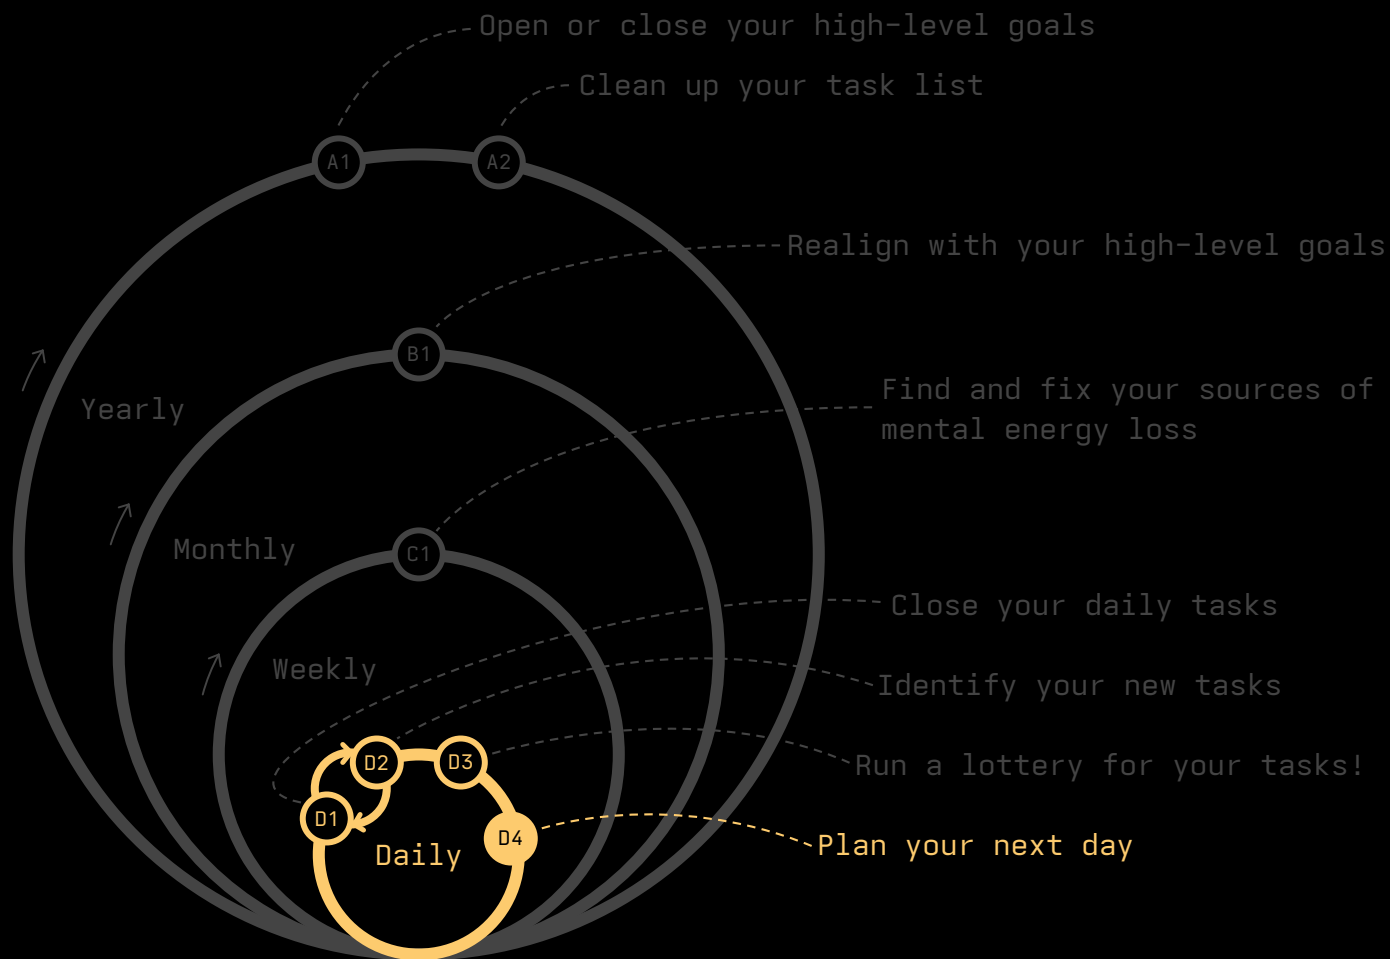

Doing


Record a video about pro...
Review Dilshod's screenp...
Add a plain text sitemap...
🔄 Do laundry – every Su...
Prepare an emergency eva...
🔄 Water the plants

Postponed

2026-05-15 -- Match max ...
2026-05-16 -- Find all t...
2026-05-16 -- 🔄 Check i...
2026-05-17 -- Buy a port...
⋮

Finished

Canceled

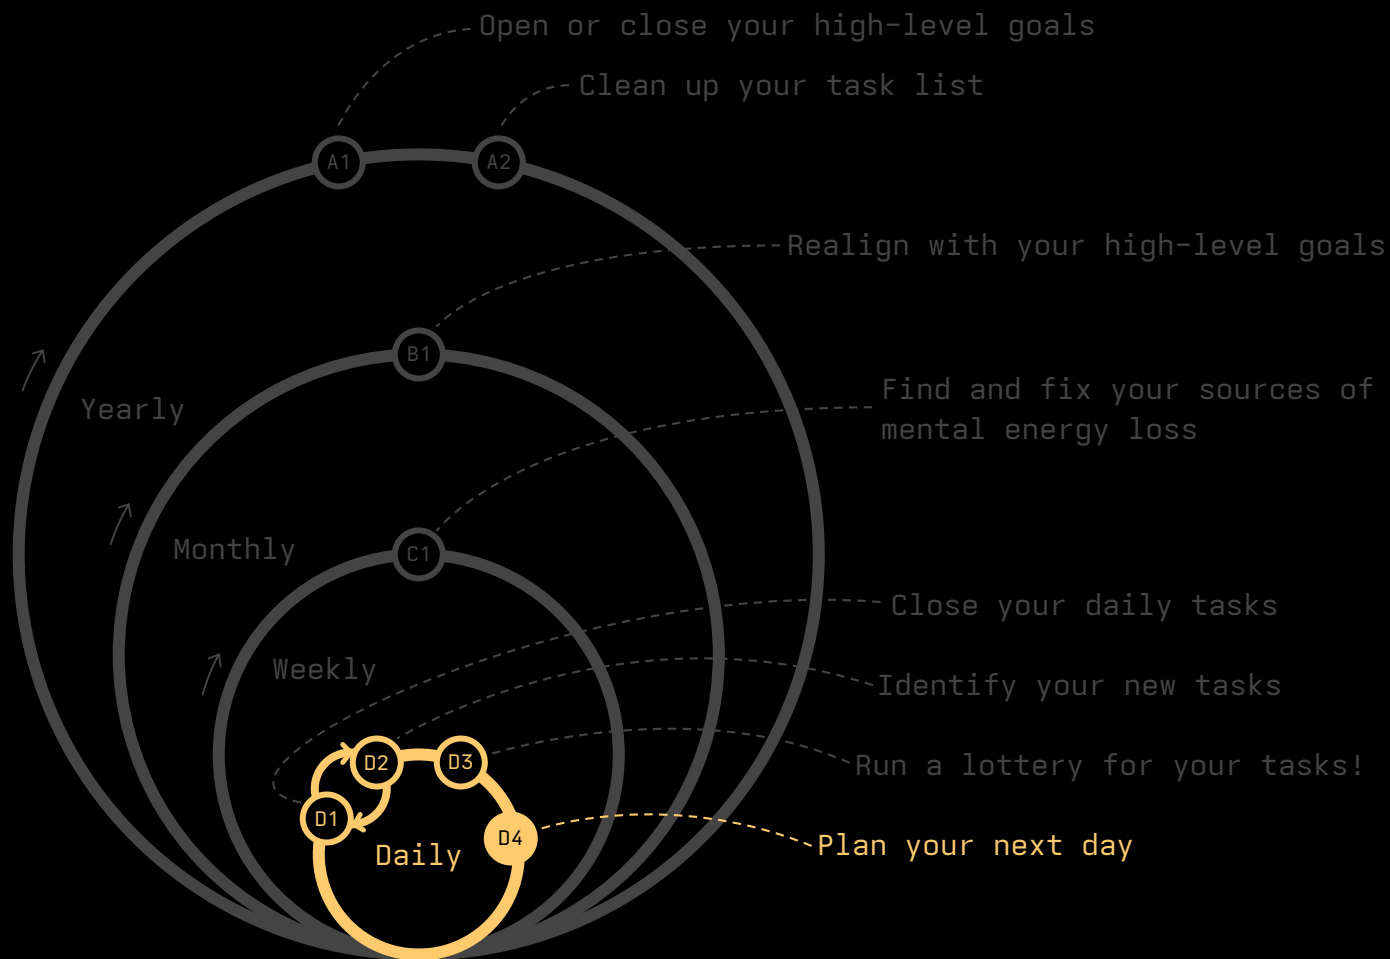

Doing


Record a video about pro...
Review Dilshod's screenp...
Add a plain text sitemap...
🔄 Do laundry – every Su...
Prepare an emergency eva...
🔄 Water the plants

Postponed

2026-05-15 -- Match max ...
2026-05-16 -- Find all t...
2026-05-16 -- 🔄 Check i...
2026-05-17 -- Buy a port...
⋮

Finished

Canceled

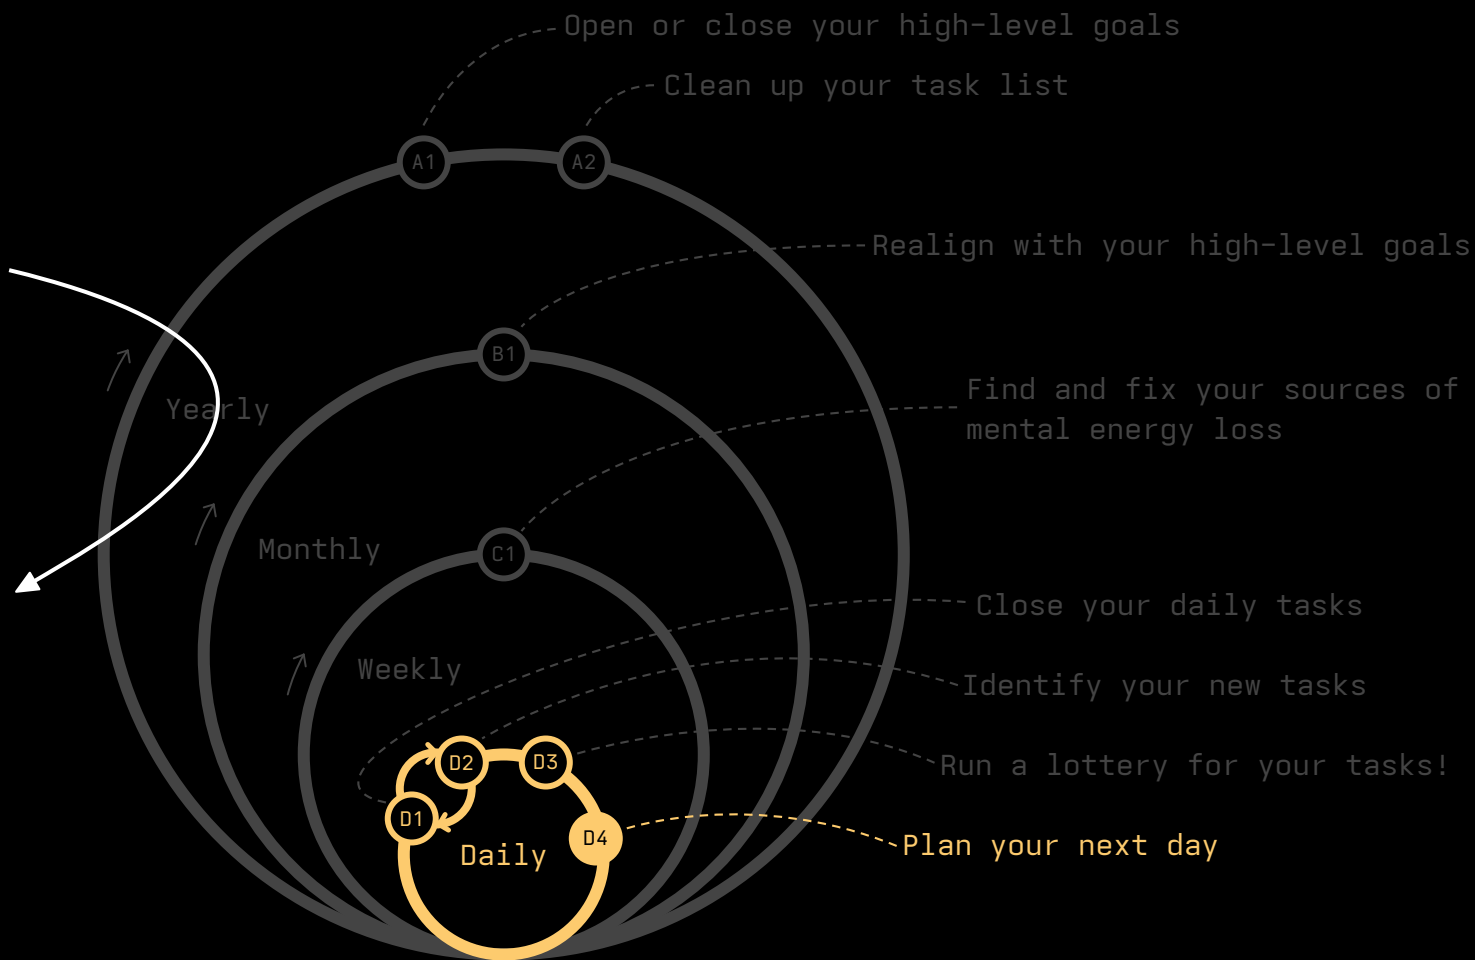

Doing


Record a video about pro...
Review Dilshod's screenp...
Add a plain text sitemap...
🔄 Do laundry – every Su...
🔄 Water the plants

Postponed

2026-05-15 -- Match max ...
2026-05-16 -- Find all t...
2026-05-16 -- Prepare an...
2026-05-16 -- 🔄 Check i...
2026-05-17 -- Buy a port...
⋮

Finished

Canceled

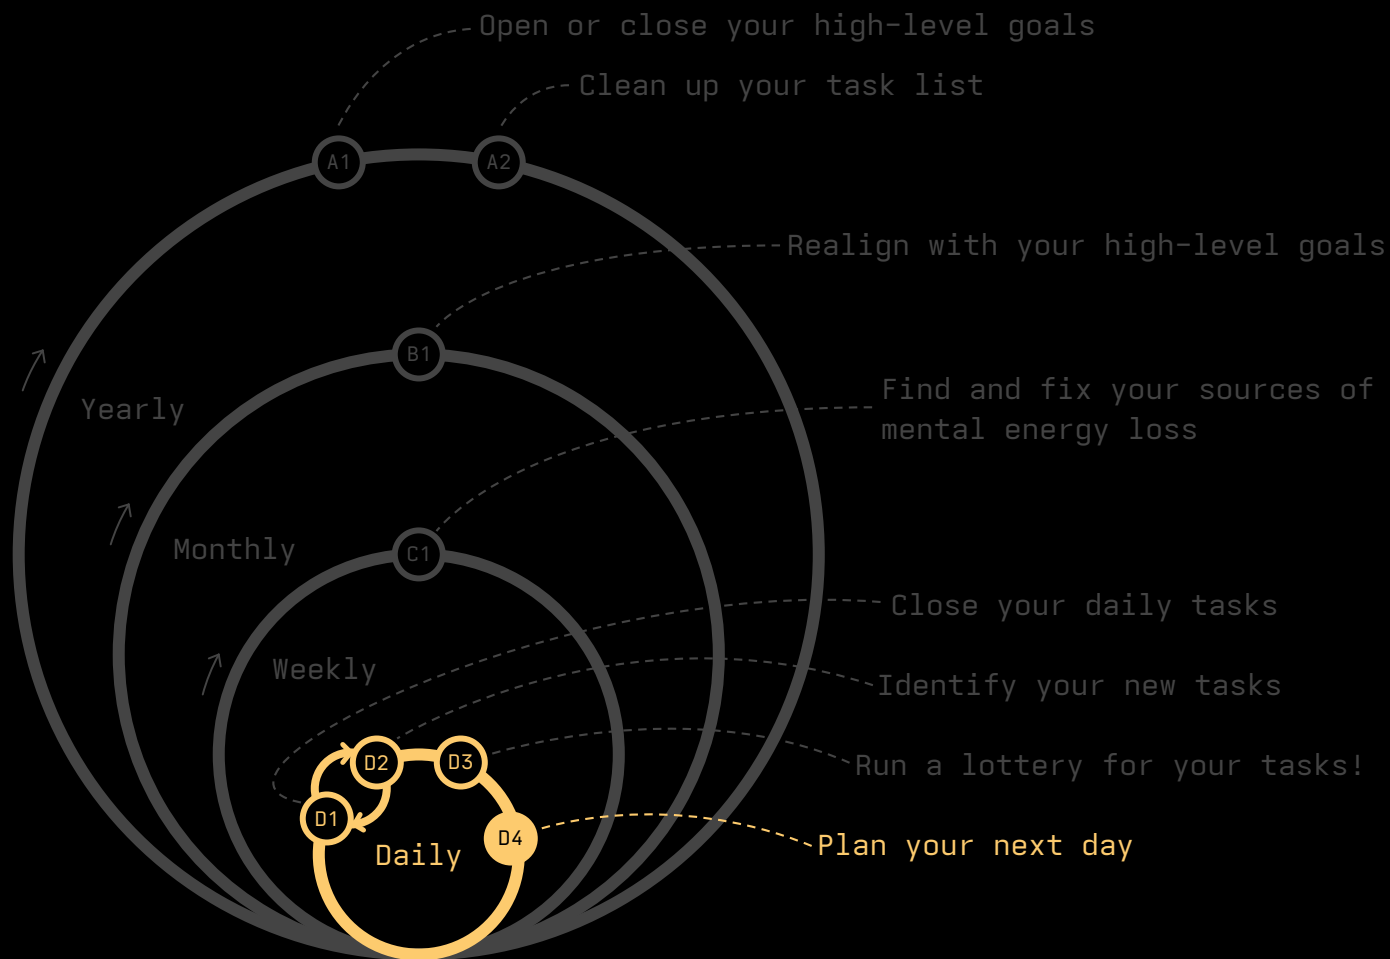

Doing


Record a video about pro...
Review Dilshod's screenp...
Add a plain text sitemap...
🔄 Do laundry – every Su...
🔄 Water the plants

Postponed

2026-05-15 -- Match max ...
2026-05-16 -- Find all t...
2026-05-16 -- Prepare an...
2026-05-16 -- 🔄 Check i...
2026-05-17 -- Buy a port...
⋮

Finished

Canceled

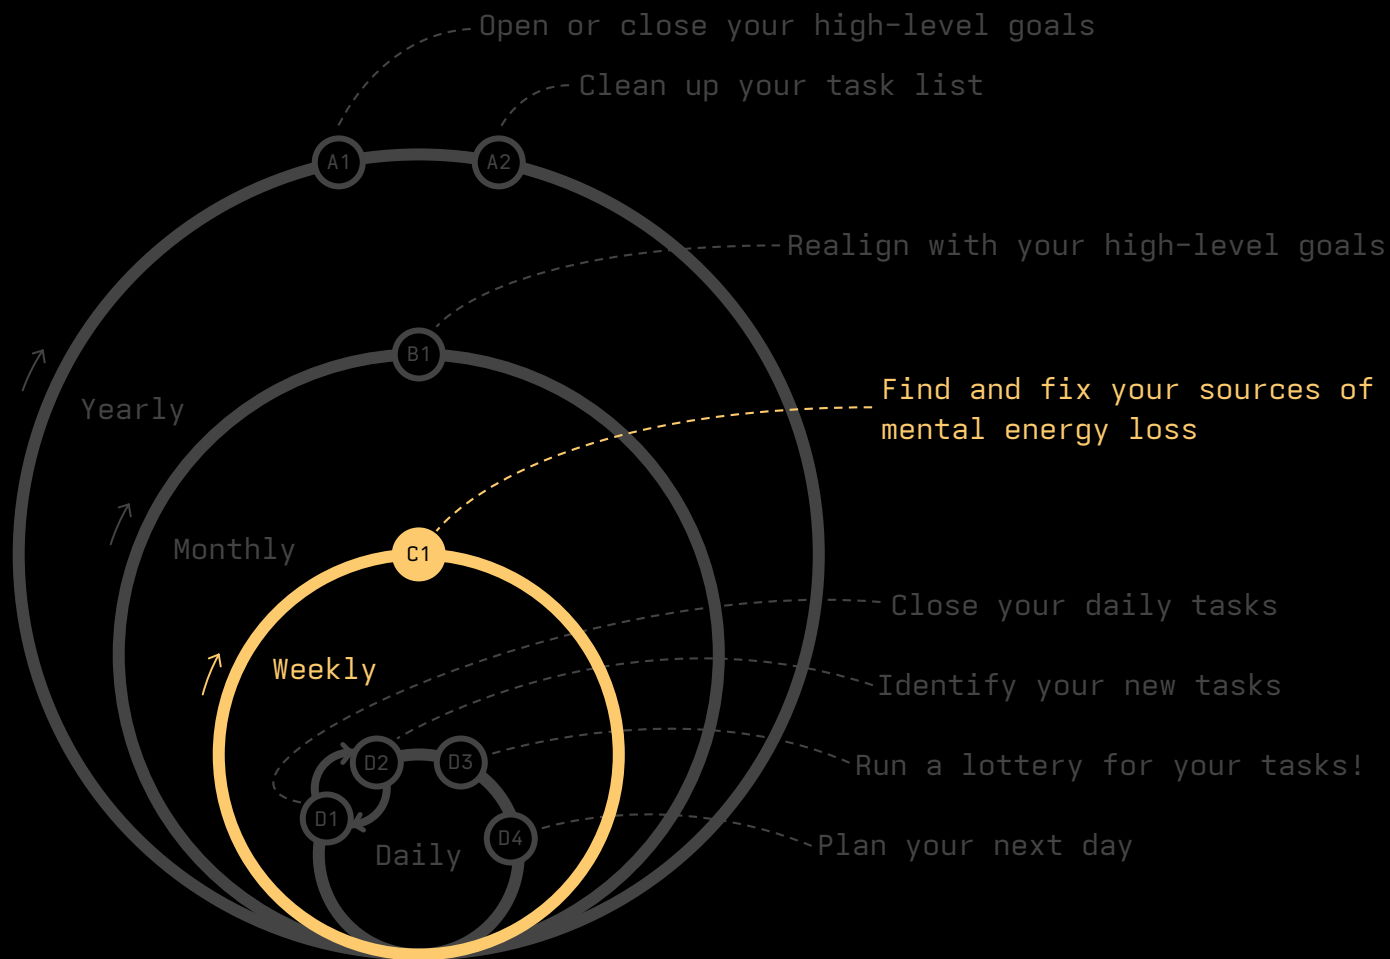

Doing

Postponed

Finished

⋮

2026-05-09 -- Prepare an...

2025-05-10 -- 🔄 Water t...

2026-05-10 -- 🔄 Do laun...

2026-05-11 -- Add a plai...

2026-05-11 -- 🔄 Check t...

2026-05-12 -- Fix the ra...

Canceled

⋮

2026-05-02 -- Convert th...


2025-05-05 -- Wash the c...

2026-05-07 -- Download t...

2026-05-08 -- Add giant ...

2026-05-10 -- Practice a...

2026-05-12 -- Buy a mini...

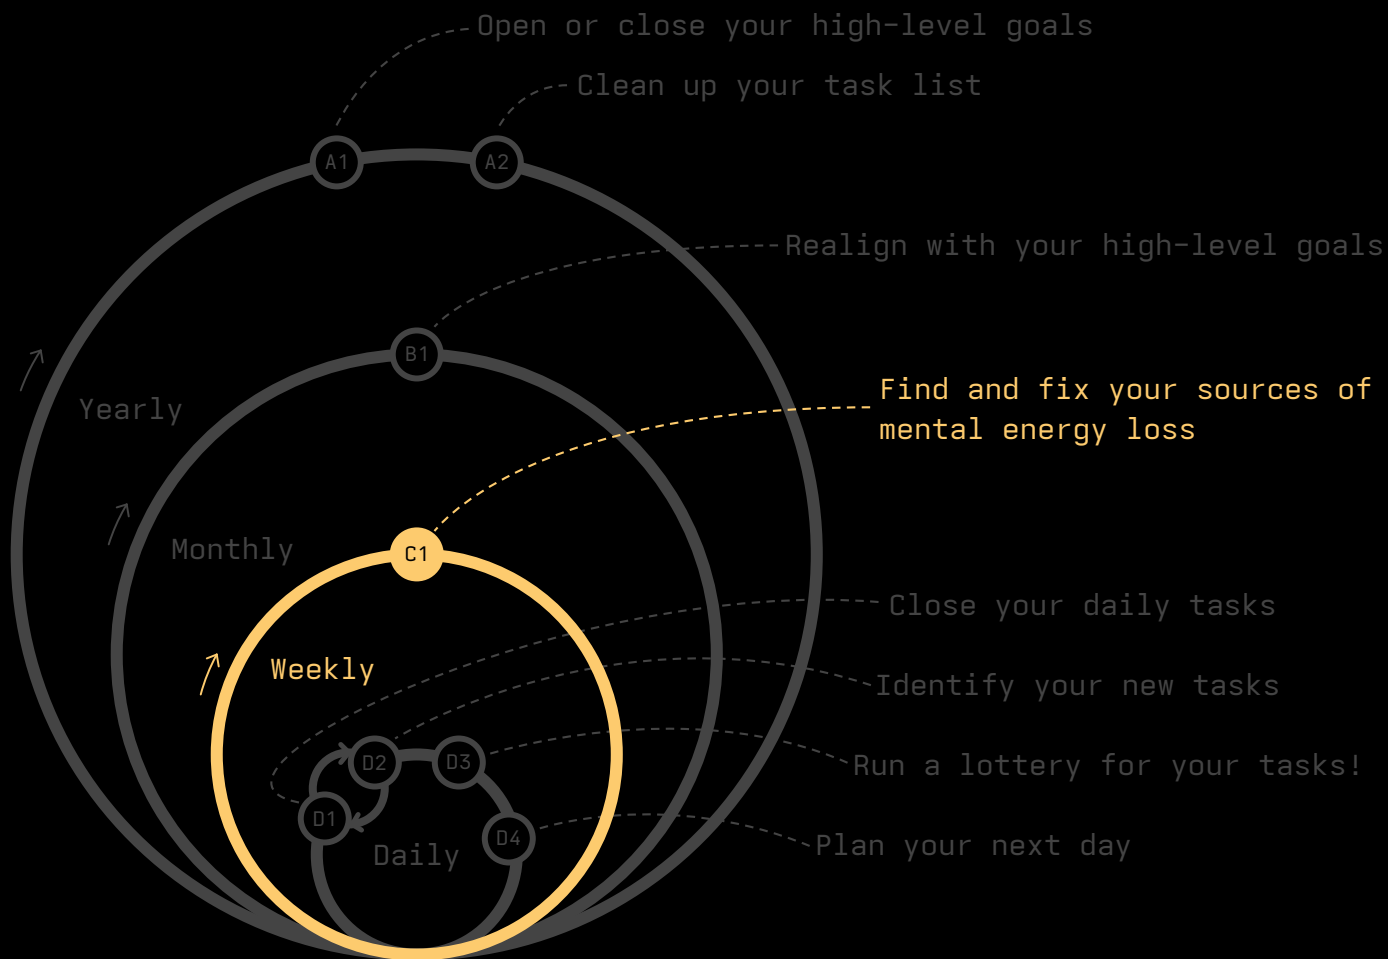

Doing

Postponed

Finished

⋮

2026-05-09 -- Prepare an...

2025-05-10 -- ☞ Water t...

2026-05-10 -- ☞ Do laun...

2026-05-11 -- Add a plai...

2026-05-11 -- ☞ Check t...

2026-05-12 -- Fix the ra...

Canceled

⋮

2026-05-02 -- Convert th...


2025-05-05 -- Wash the c...

2026-05-07 -- Download t...

2026-05-08 -- Add giant ...

2026-05-10 -- Practice a...

2026-05-12 -- Buy a mini...

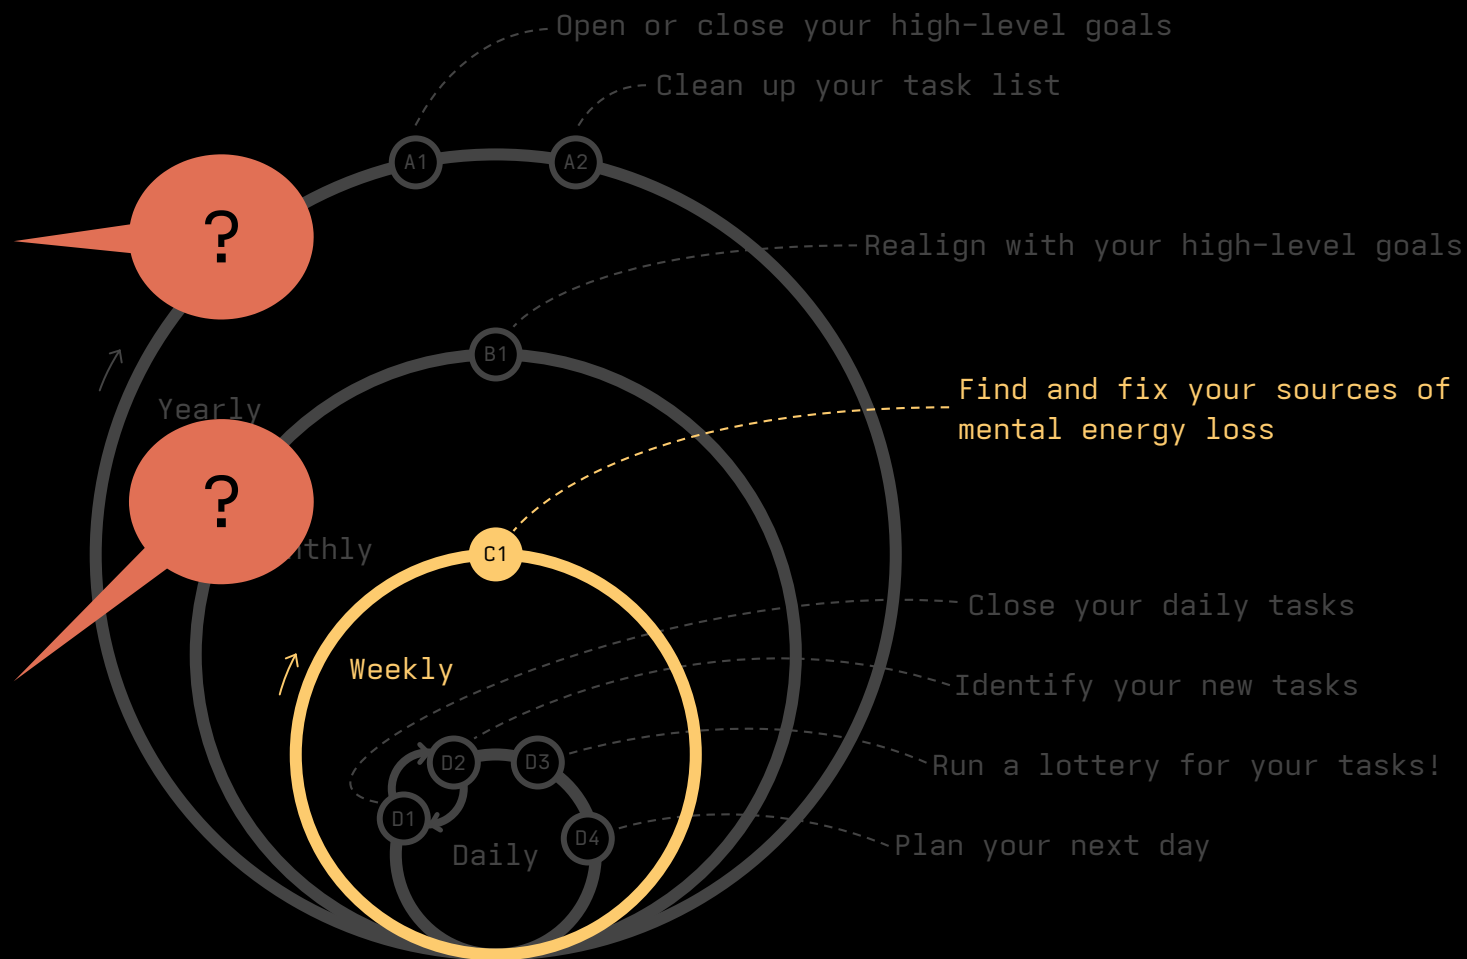

Doing

Postponed

Finished

⋮

2026-05-09 -- Prepare an...

2025-05-10 -- ↻ Water t...

2026-05-10 -- ↻ Do laun...

2026-05-11 -- Add a plai...

2026-05-11 -- ↻ Check t...

2026-05-12 -- Fix the ra...

Canceled

⋮

2026-05-02 -- Convert th...

2025-05-05 -- Wash the c...

2026-05-07 -- Download t...

2026-05-08 -- Add giant ...

2026-05-10 -- Practice a...

2026-05-12 -- Buy a mini...

↻ Find and fix sources of mental energy loss

Doing

Postponed

Finished

⋮

2026-05-09 -- Prepare an...

2025-05-10 -- ↻ Water t...

2026-05-10 -- ↻ Do laun...

2026-05-11 -- Add a plai...

2026-05-11 -- ↻ Check t...

2026-05-12 -- Fix the ra...

Canceled

⋮

2026-05-02 -- Convert th...

2025-05-05 -- Wash the c...

2026-05-07 -- Download t...

2026-05-08 -- Add giant ...

2026-05-10 -- Practice a...

2026-05-12 -- Buy a mini...

↻ Find and fix sources of mental energy loss

- ☐ Procrastination
- ☐ Task switching
- ☐ Toxic people and environments
- ☐ Environment interruptions
- ☐ Social media
- ☐ Perfectionism
- ☐ Sloppiness

Note: don't forget that it's not limited to identifying the losses, but to finding the root cause and and finding a solution.

Doing

Postponed

Finished

⋮

2026-05-09 -- Prepare an...

2025-05-10 -- ↻ Water t...

2026-05-10 -- ↻ Do laun...

2026-05-11 -- Add a plai...

2026-05-11 -- ↻ Check t...

2026-05-12 -- Fix the ra...

Canceled

⋮

2026-05-02 -- Convert th...

2025-05-05 -- Wash the c...

2026-05-07 -- Download t...

2026-05-08 -- Add giant ...

2026-05-10 -- Practice a...

2026-05-12 -- Buy a mini...

↻ Find and fix sources of mental energy loss

- ☐ Procrastination
- ☐ Task switching
- ☐ Toxic people and environments
- ☐ Environment interruptions
- ☐ Social media
- ☐ Perfectionism
- ☐ Sloppiness

Note: don't forget that it's not limited to identifying the losses, but to finding the root cause and and finding a solution.

Gradually
improve it

Doing

Record a video about pro...
Review Dilshod's screenp...
Add a plain text sitemap...
🔄 Do laundry - every Su...

Postponed

Finished

Canceled



Doing

Record a video about pro...
Review Dilshod's screenp...
Add a plain text sitemap...
🔄 Do laundry - every Su...

Postponed

Finished

Canceled



Doing

Record a video about pro...
Review Dilshod's screenp...
Add a plain text sitemap...
🔄 Do laundry - every Su...

Postponed

Finished

Canceled




Doing

Postponed

2026-05-14 -- Prepare an...
2026-05-14 -- ☞ Water t...
2026-05-15 -- Match max ...
2026-05-16 -- Find all t...
2026-05-16 -- ☞ Check i...
2026-05-17 -- Buy a port...
2026-05-18 -- Install la...
2026-05-18 -- Write a re...
2026-05-18 -- Review Kam...
2026-05-19 -- Consider a...
2026-05-20 -- Fix the ra...
2026-05-20 -- Write an a...
2026-05-21 -- ☞ Wash th...
⋮

Finished

Canceled

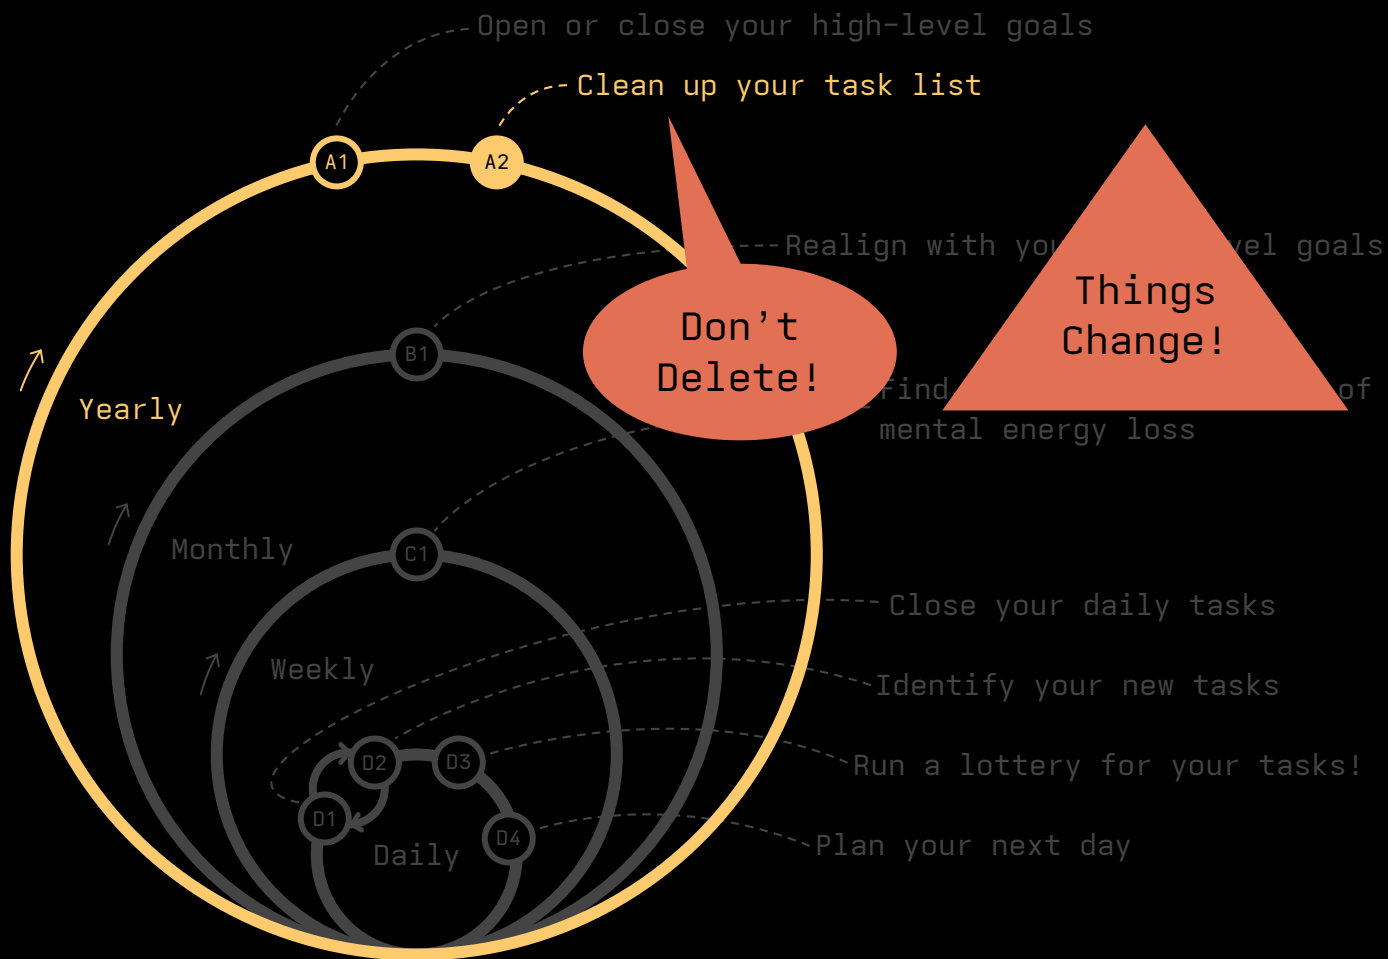

Doing

Postponed

Finished

Canceled

⋮

2026-04-02 -- Configure ...

2026-04-06 -- Move Shuhr...

2026-04-12 -- Design a p...

2026-04-17 -- Call old c...

2026-04-19 -- Polish the...

2026-04-24 -- Discuss al...

2026-04-24 -- Finalize t...

2026-04-27 -- Contact Mi...

2026-05-02 -- Convert th...

2025-05-05 -- Wash the c...

2026-05-07 -- Download t...

2026-05-08 -- Add giant ...

2026-05-10 -- Practice a...

2026-05-12 -- Buy a mini...



Doing

Postponed

Finished

Canceled

⋮

2026-04-02 -- Configure ...

2026-04-06 -- Move Shuhr...

2026-04-12 -- Design a p...

2026-04-17 -- Call old c...

2026-04-19 -- Polish the...

2026-04-24 -- Discuss al...

2026-04-24 -- Finalize t...

2026-04-27 -- Contact Mi...

2026-05-02 -- Convert th...

2025-05-05 -- Wash the c...

2026-05-07 -- Download t...

2026-05-08 -- Add giant ...

2026-05-10 -- Practice a...

2026-05-12 -- Buy a mini...

Finalize the topic of the sustainability report

They've asked Kamol to do it instead of me!

I'm not very happy about it, but there's not much I can do.

Doing

Postponed

Finished

Canceled

⋮

2026-04-02 -- Configure ...

2026-04-06 -- Move Shuhr...

2026-04-12 -- Design a p...

2026-04-17 -- Call old c...

2026-04-19 -- Polish the...

2026-04-24 -- Discuss al...

2026-04-24 -- Finalize t...

2026-04-27 -- Contact Mi...

2026-05-02 -- Convert th...

2025-05-05 -- Wash the c...

2026-05-07 -- Download t...

2026-05-08 -- Add giant ...

2026-05-10 -- Practice a...

2026-05-12 -- Buy a mini...




Doing

Record a video about pro...
Review Dilshod's screenp...
Add a plain text sitemap...
🔄 Do laundry - every Su...

Postponed

Finished

Canceled

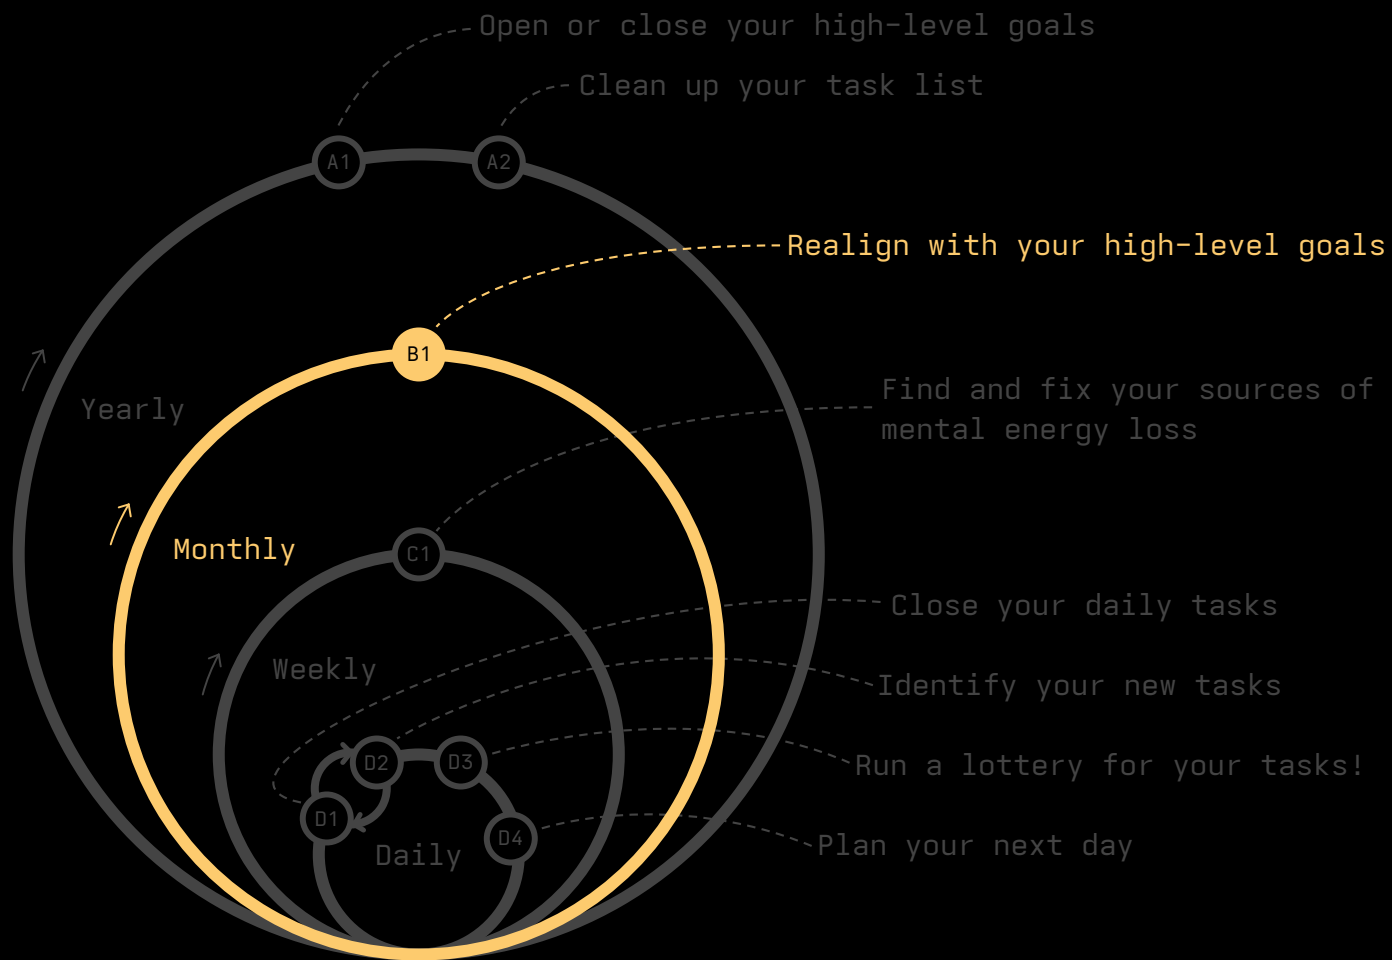


Doing

Record a video about pro...
Review Dilshod's screenp...
Add a plain text sitemap...
🔄 Do laundry - every Su...

Postponed

Finished

Canceled

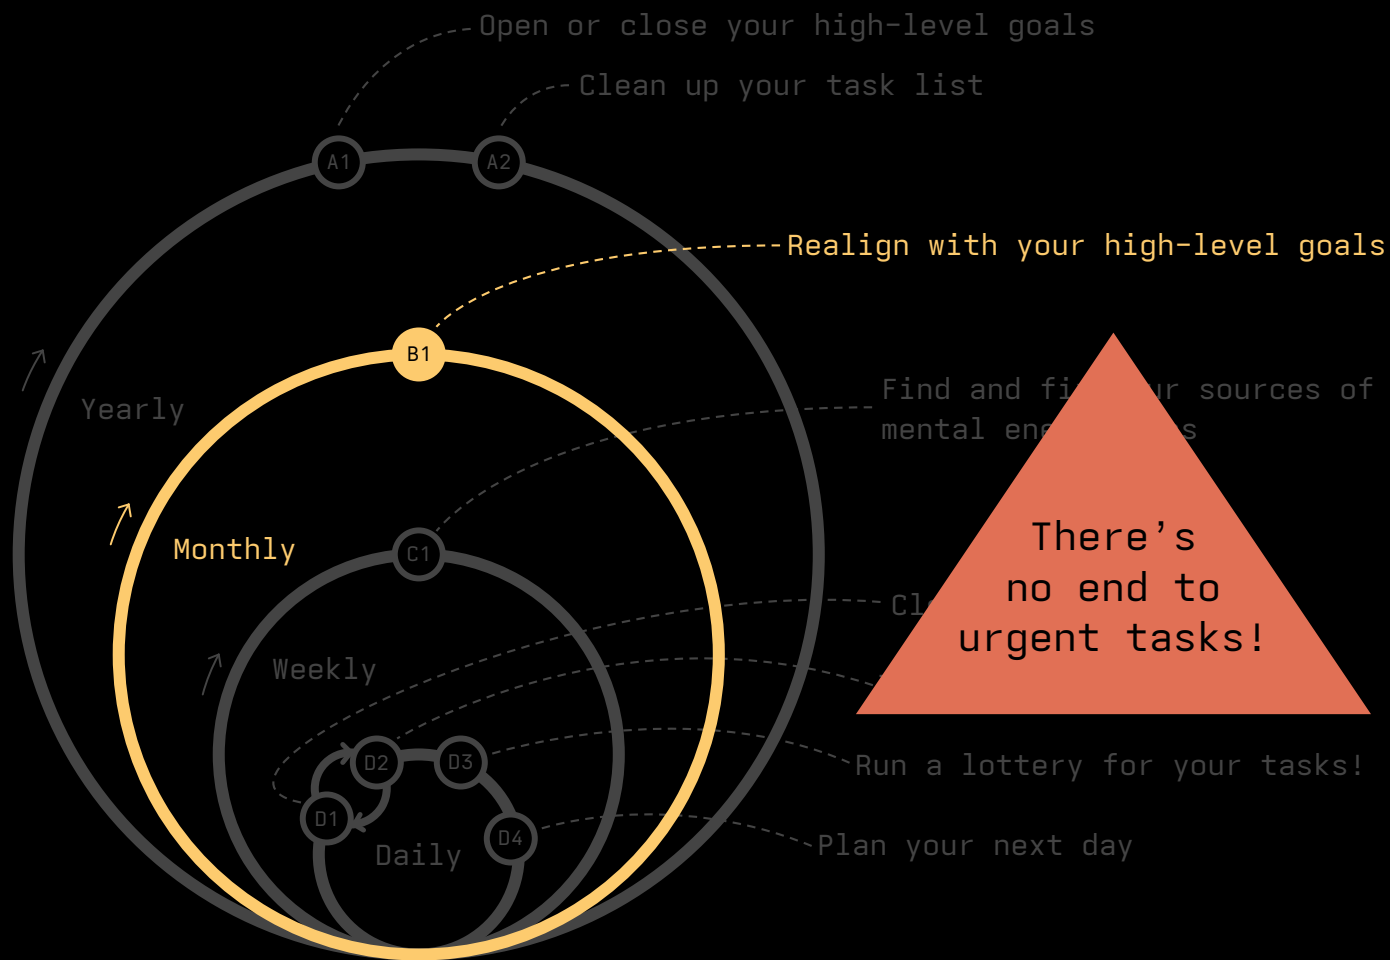


Doing

Record a video about pro...
Review Dilshod's screenp...
Add a plain text sitemap...
🔄 Do laundry - every Su...

Postponed

Finished

Canceled

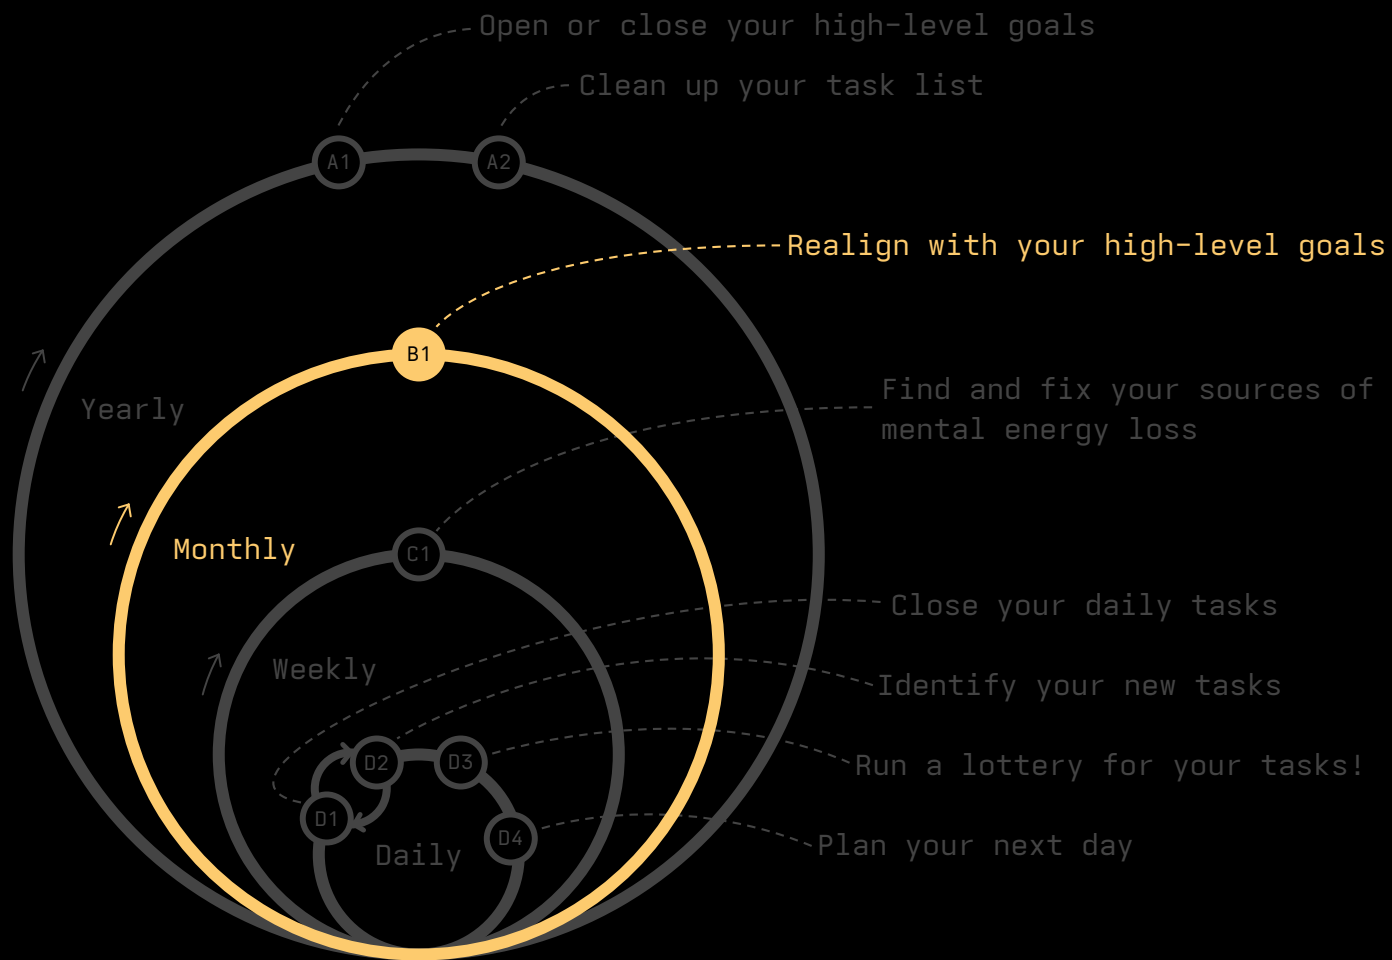

Doing

Record a video about pro...
Review Dilshod's screenp...
Add a plain text sitemap...
🔄 Do laundry - every Su...

Postponed

Finished

Canceled







P1.express



<https://nader.pm/presentations/uz-2026b/>

- Website, email address, LinkedIn profile
- This slide deck
- Related resources
